

June 8, 2021

Summit Homes 120 SE 30<sup>th</sup> St Lee's Summit, MO 64082

# RE: Subgrade Inspection for Lot # 104 Manor at Stoney Creek – 4416 SW Tanzanite Cir Lee's Summit, MO 64082 – Permit # PRRES20212066

On June 7, 2021, a special inspection was performed by Everstead at the above referenced property. The purpose of this inspection was to determine structural adequacy of the existing soil for construction of concrete foundation.

Findings:

- The soils observed at footing elevation were silty clay; medium-dark brown; medium plasticity and dry.
- Probes and penetrometer readings indicated that the soils do not have sufficient bearing capacity for the loads applied by foundation per permit plans.

## **Recommendations:**

- Everstead recommends that the footings be enlarged to 24"X8" with three (3) #4 rebar continuous (see attached specifications)
- Basement and garage pier pads shall be enlarged a minimum of 6" each way (i.e existing 30"x30" shall be enlarged to 36"x36", etc.) (see attached specifications)

We would like to thank you for the opportunity to consult you on your project. Please feel free to contact us if you have any questions regarding this report or need any further consultation.

Sincerely,

Bradley Huxol, PE




#### NOTE:

- MAXIMUM 9'-0" WALL HEIGHT
- USE REBAR AS SHOWN ON DRAWING OR XX LB/YD<sup>3</sup> HELIX 5-25 DESIGNED IN ACCORDANCE WITH UNIFORM-ES ER-0279

## ALTERNATIVE PIER PAD SCHEDULE

ALTERNATIVE PIER PAD SCHEDULE							
PAD SIZE	ADJUSTED PAD SIZE	REINFORCEMENT	SLAB TOP STEEL	HELIX DOSAGE			
30"x30"x12"	36"x36"x12"	(6) #4 BAR E.W.	(4) #4 BAR E.W.	9 LB/CUBIC YARD			
36"x36"x12"	42"x42"x14"	(7) #4 BAR E.W.	(5) #4 BAR E.W.	9 LB/CUBIC YARD			
42"x42"x14"	48"x48"x16"	(8) #4 BAR E.W.	(6) #4 BAR E.W.	9 LB/CUBIC YARD			
48"x48"x16"	54"x54"x16"	(9) #4 BAR E.W.	(6) #4 BAR E.W.	9 LB/CUBIC YARD			
54"x54"x16"	60"x60"x16"	(10) #4 BAR E.W.	(7) #4 BAR E.W.	9 LB/CUBIC YARD			

NOTE: PIER PAD SCHEDULE HAS BEEN INCREASED WITH THE USE OF THIS SPREAD FOOTING DETAIL. TABLE IS BASED ON RES SPECIFICATION REFERENCES AND MAY NOT DIRECTLY TRANSLATE TO PLANS ENGINEERED BY OTHER FIRMS. REFER TO SITE SPECIFIC DESIGN FOR PIER PAD SIZES.

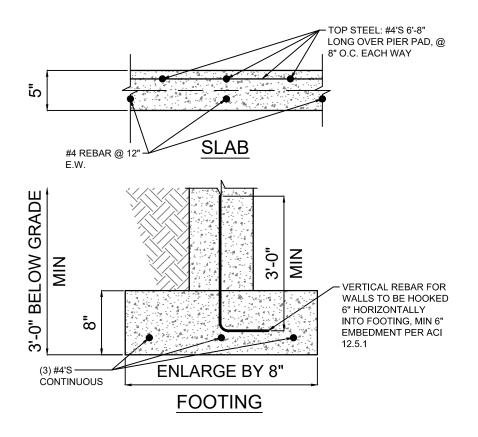

### ALTERNATIVE HELIX OPTION:

- SLAB HELIX DOSAGE = 9 LB/YD<sup>3</sup>
- FOOTING HELIX DOSAGE = 9 LB/YD<sup>3</sup>
- PIER PAD HELIX DOSAGE = 9 LB/YD<sup>3</sup>
- HORIZONTAL REBAR IS NOT REQUIRED IN FOOTINGS FOR HELIX
- SLAB ONLY REQUIRES TOP STEEL REBAR OVER PIER PADS FOR HELIX
- VERTICAL REBAR IN WALL IS STILL REQUIRED. HOOK REBAR 6" HORIZONTALLY INTO FOOTING @ 24" O.C.

SH 1	REVISION					
	0	TYPE	JT	SPREAD FOOTING DETAIL N.T.S.		EVERSTEAD ENGINEERING & DESIGN
	-	-	-			
	-	-	-			
	-	-	-			
	-	-	-			
	-	-	-			
	-	-	-			
