

PROSSER | WILBERT
CONSTRUCTION, INC.

GENERAL CONTRACTORS • CONSTRUCTION MANAGERS

13730 W. 108th St
Lenexa, KS 66215
Ph : 913-906-0104

RFI

To: Jeff Windmeyer
The Hollis & Miller Group, Inc
1828 Walnut Street Suite 922
Kansas City, MO 64108

RFI #: 2

Date: 7/19/2017

3201 SW Fascination Dr

Job: 17-011 17-011 B&B Theaters NLV7

Phone:

CC: Russ Pearson (NAI Heartland), Harold Cooper (Prosser Wilbert Construction)

Subject: Auditorium 1 Footing & Slab - Means & Method

Drawing: S101 & S337

Spec Section:

Cost Impact: Unchanged

Schedule Impact: Unchanged

Request:

Date Required: 7/21/2017

Summit concrete would like to continue the spread footing around the west and south sides of the lower auditorium 1 bowl, similar to the north and east sides per detail A1/S337. This would allow the CIP walls to be poured first on top of the footing. Then the lower 93'-0" slab poured last. See details.

This additional footing would be completed at no additional cost.

Requested by: Travis Townsley
PWCI Field Office

Response:

Approved to proceed so long as no additional costs.


Answered by

Hollis-Miller Architects

Company

07.19.2017


Date

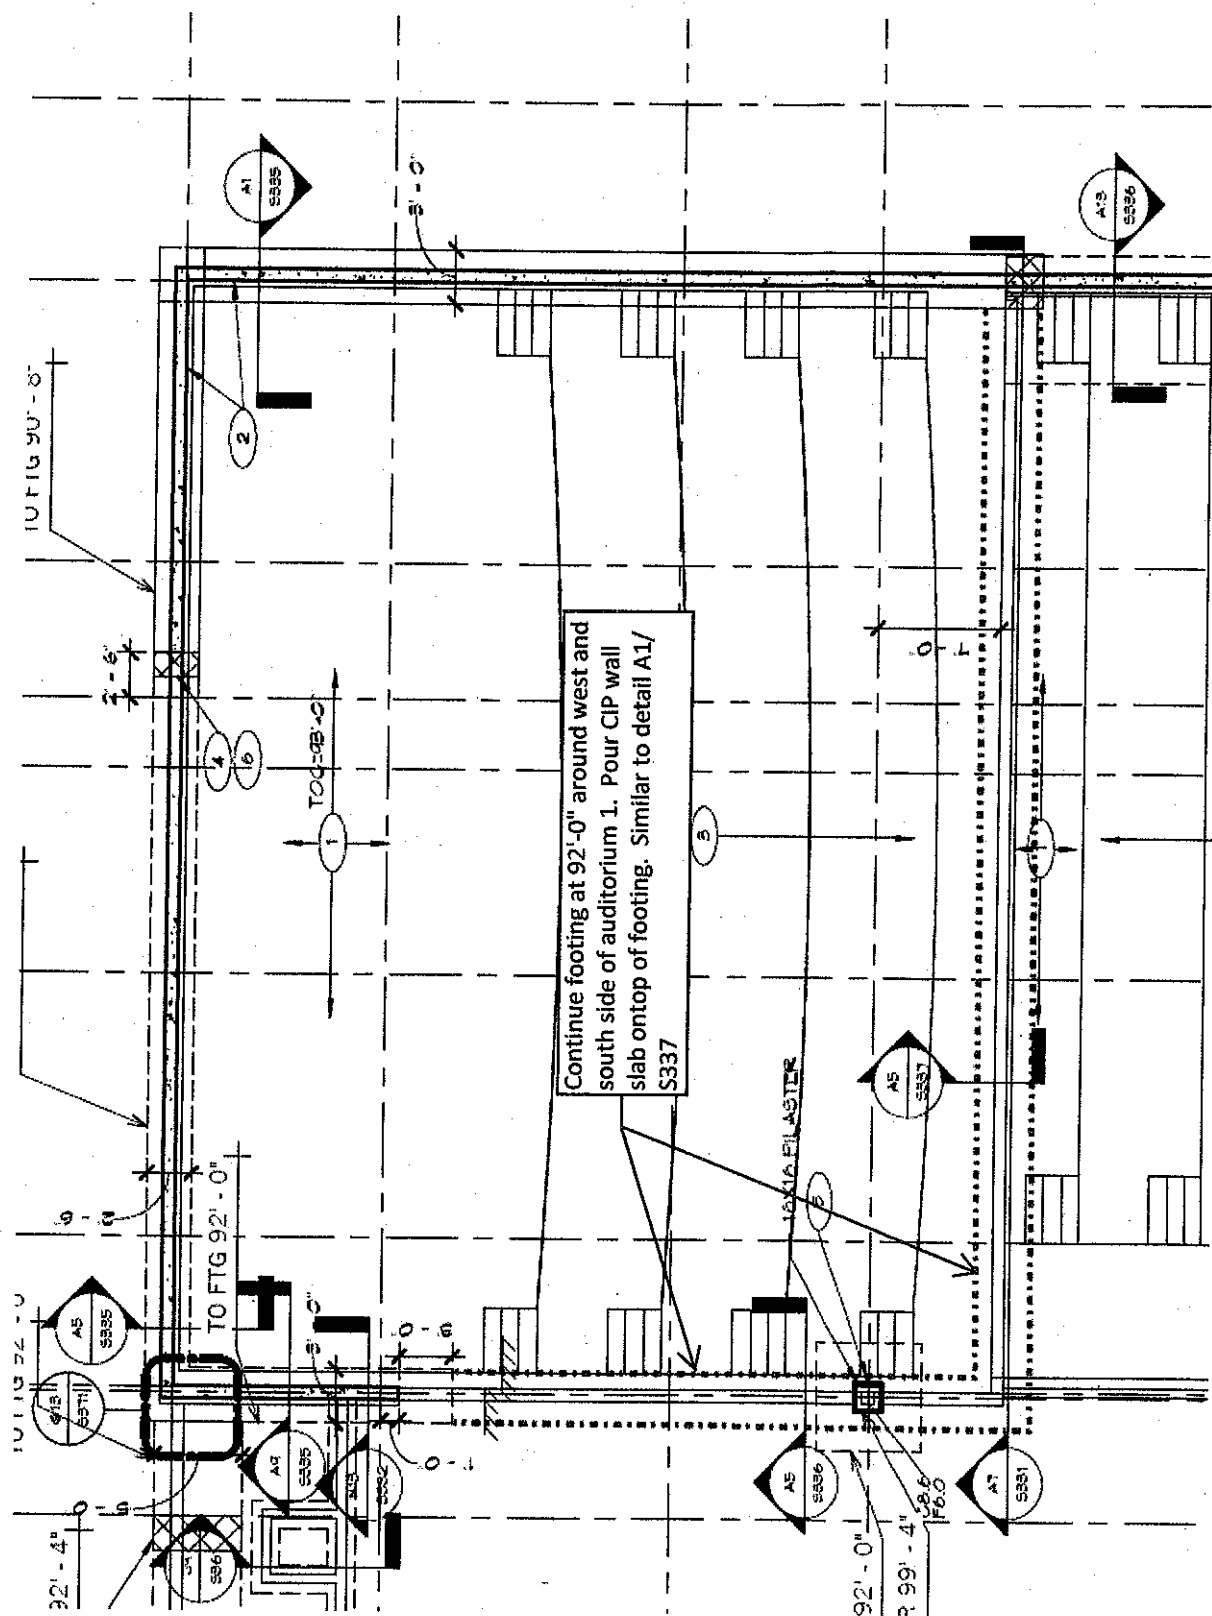


6/22/17

B+B LONGVIEW

FOOTING SKETCH



T.O.F. = 92'-0"

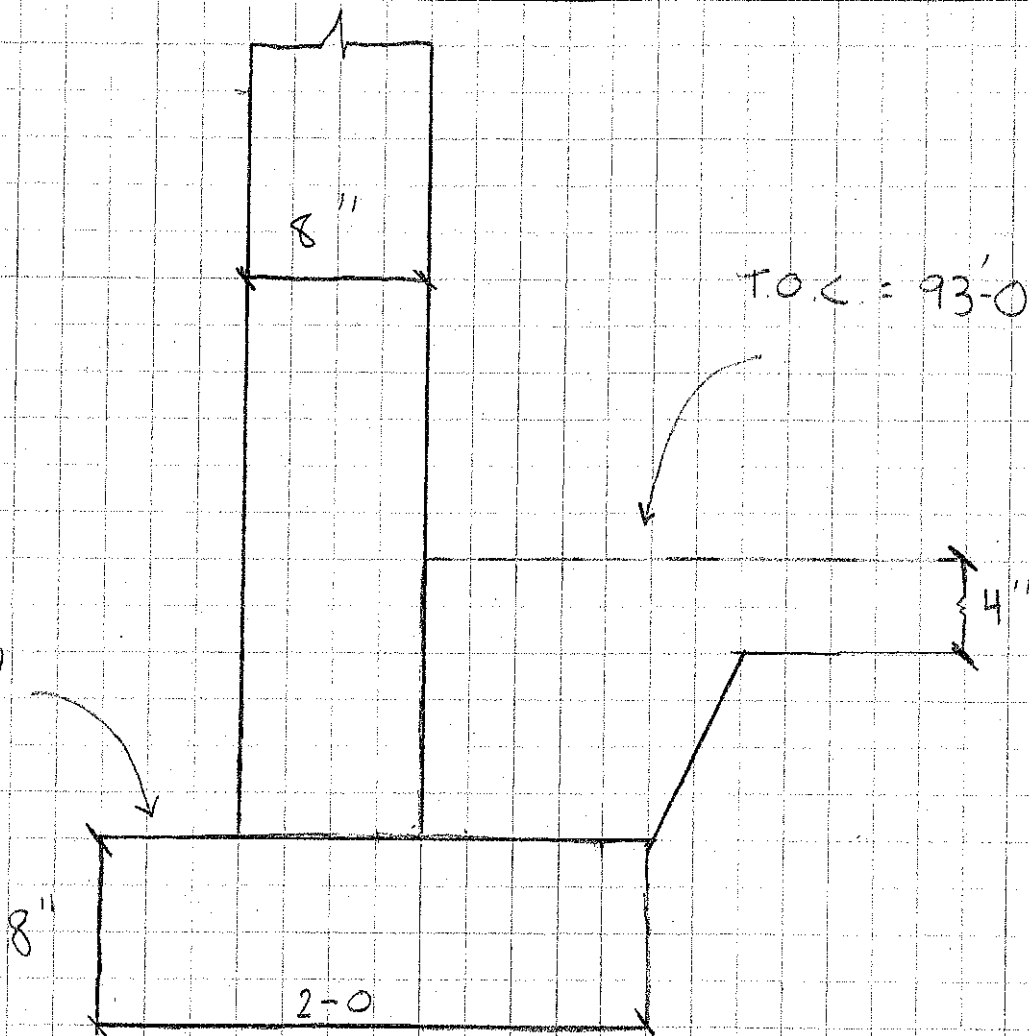

T.O.C. = 93'-0"

Detail between GRID 7-10 + GRID J-M
