


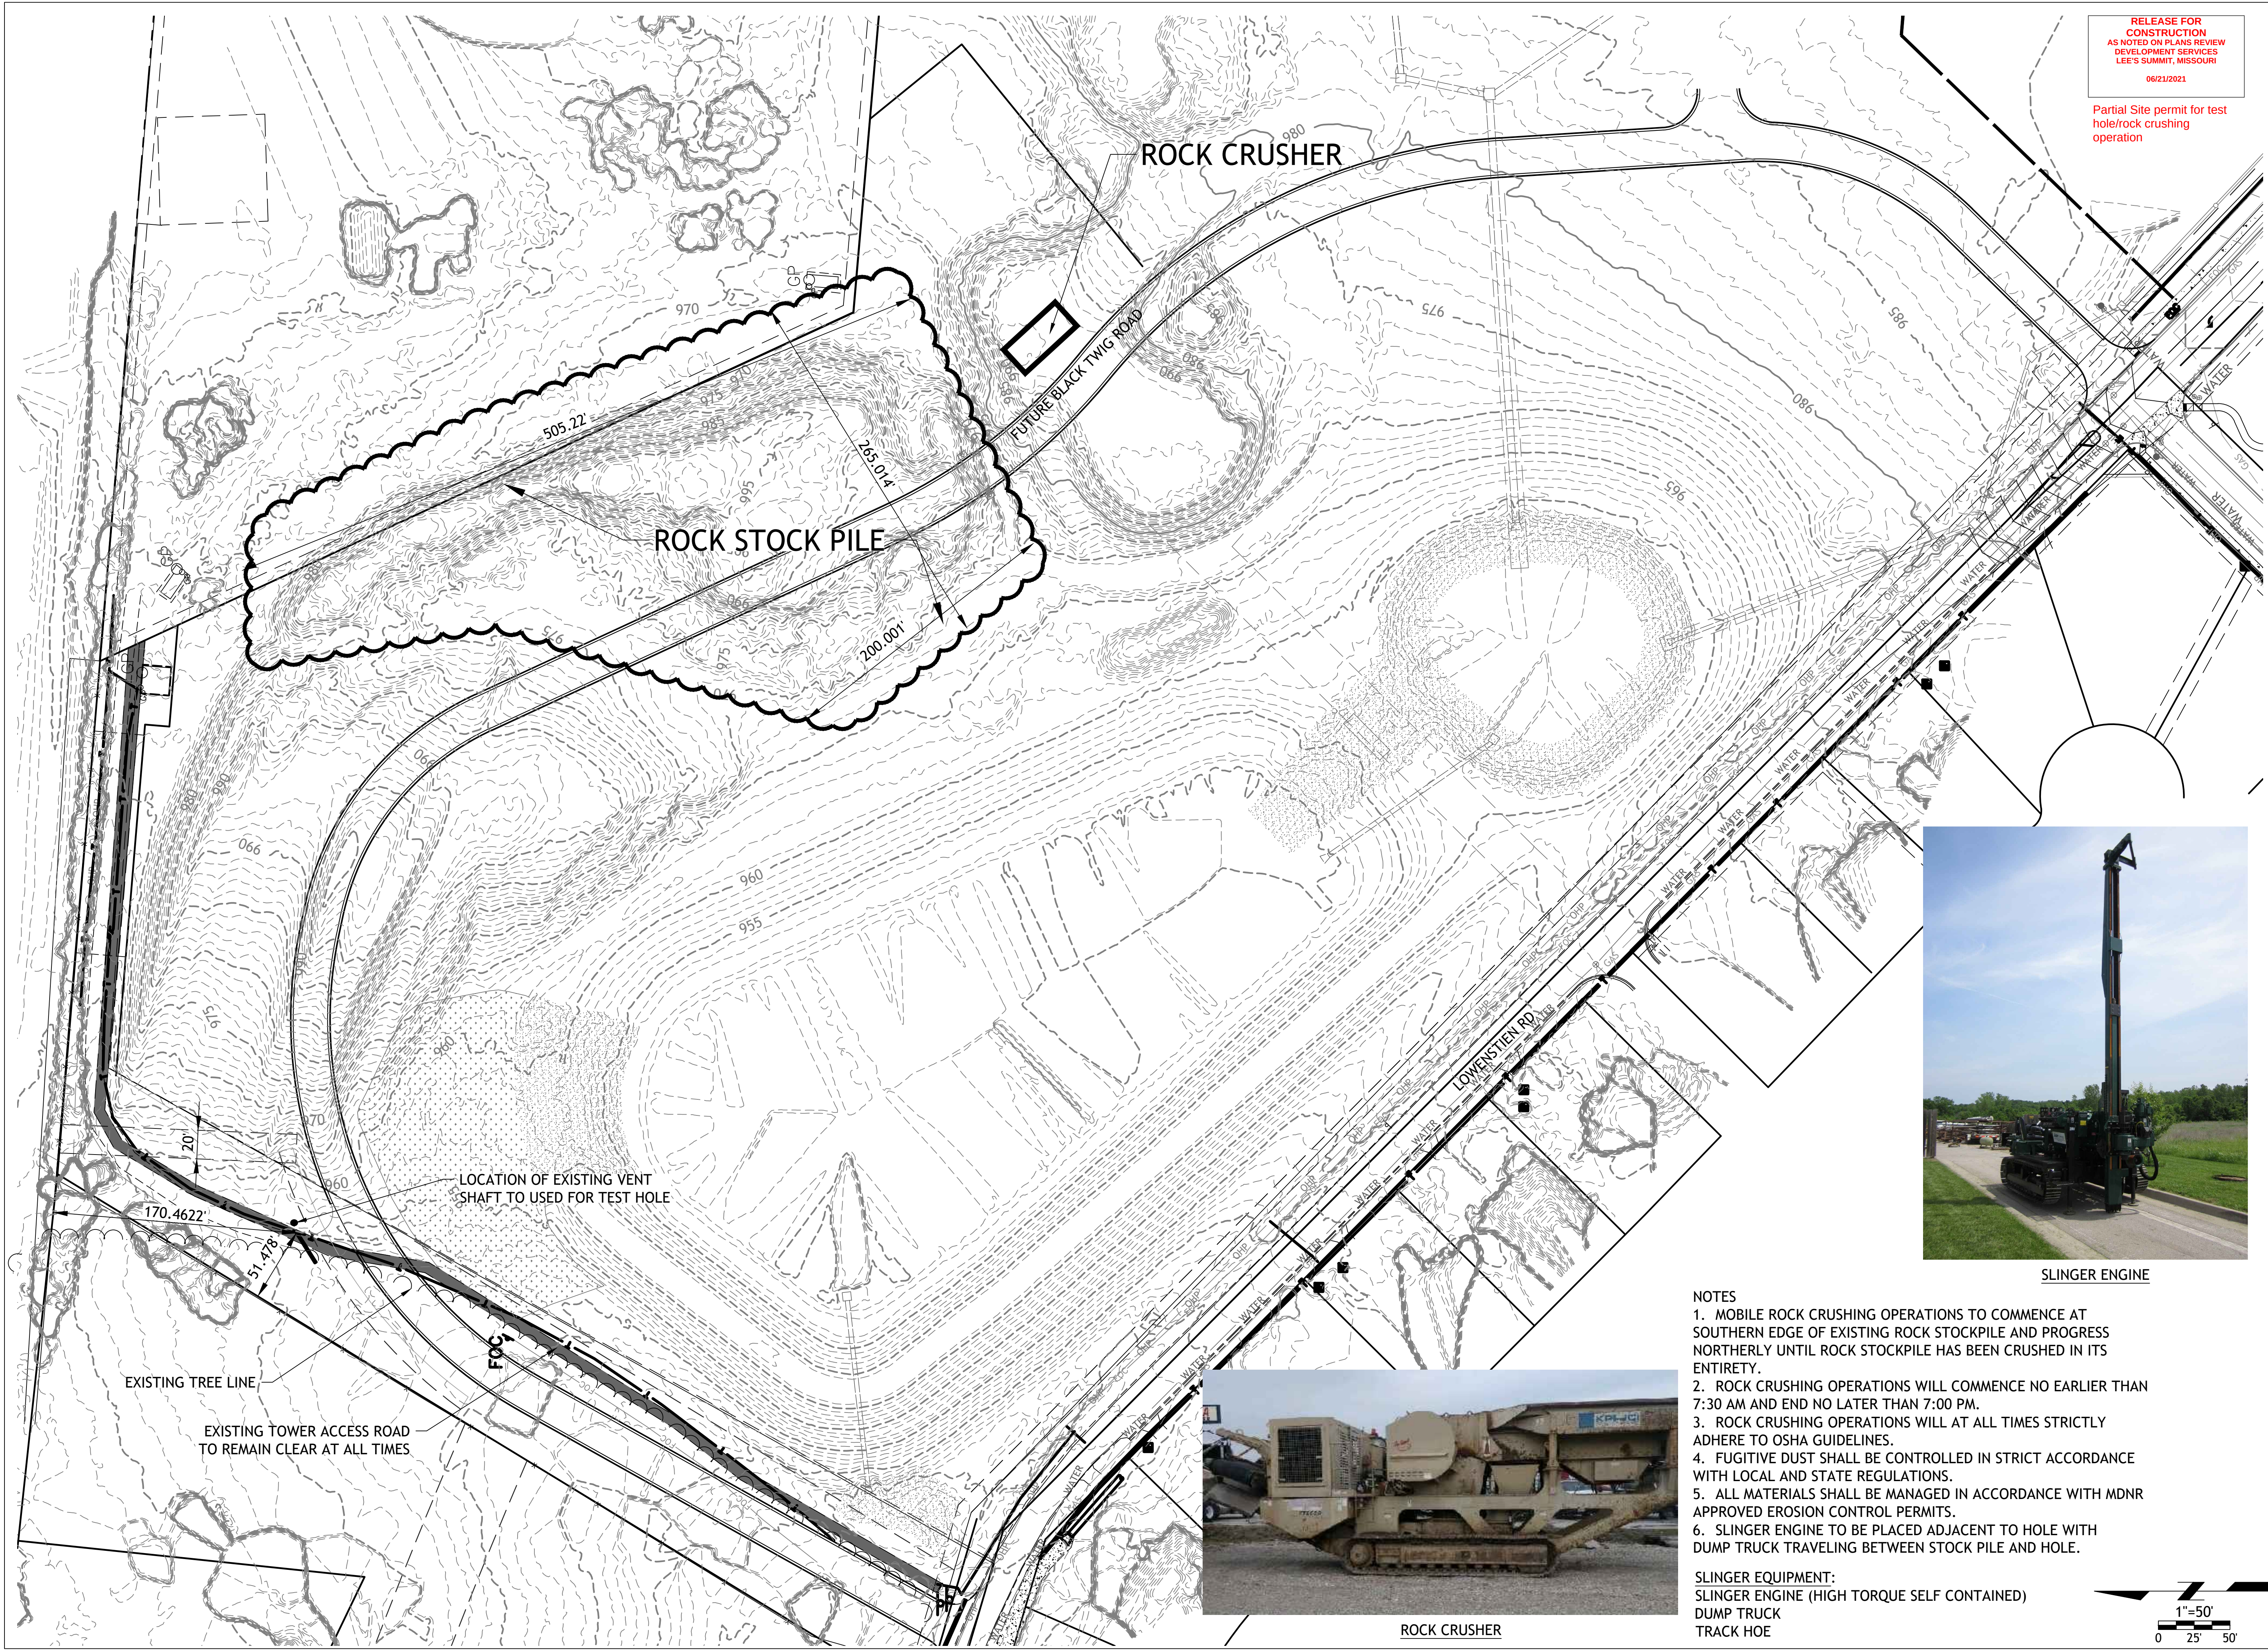

RELEASE FOR
CONSTRUCTION
AS NOTED ON PLANS REVIEW
LEE'S SUMMIT, MISSOURI
06/21/2021

Partial Site permit for test
hole/rock crushing
operation

SM Engineering
SM E
5507 High Meadow Circle
Manhattan Kansas, 66503
smcivilengr@gmail.com
785.341.9747

Drawings and/or Specifications are original
proprietary work and property of the
Engineer and intended specifically for this
project. Use of items contained herein
without consent of the Engineer is
prohibited. Drawings illustrate best
information available to the Engineer. Field
verification of actual elements, conditions,
and dimensions is required.

Revisions
5-6-21 PICS OF THE ROCK
CRUSHER
5-7-21 CITY COMMENTS



Slinger Engine



Rock Crusher

- NOTES
1. MOBILE ROCK CRUSHING OPERATIONS TO COMMENCE AT SOUTHERN EDGE OF EXISTING ROCK STOCKPILE AND PROGRESS NORTHERLY UNTIL ROCK STOCKPILE HAS BEEN CRUSHED IN ITS ENTIRETY.
 2. ROCK CRUSHING OPERATIONS WILL COMMENCE NO EARLIER THAN 7:30 AM AND END NO LATER THAN 7:00 PM.
 3. ROCK CRUSHING OPERATIONS WILL AT ALL TIMES STRICTLY ADHERE TO OSHA GUIDELINES.
 4. FUGITIVE DUST SHALL BE CONTROLLED IN STRICT ACCORDANCE WITH LOCAL AND STATE REGULATIONS.
 5. ALL MATERIALS SHALL BE MANAGED IN ACCORDANCE WITH MDNR APPROVED EROSION CONTROL PERMITS.
 6. SLINGER ENGINE TO BE PLACED ADJACENT TO HOLE WITH DUMP TRUCK TRAVELING BETWEEN STOCK PILE AND HOLE.
- SLINGER EQUIPMENT:
SLINGER ENGINE (HIGH TORQUE SELF CONTAINED)
DUMP TRUCK
TRACK HOE

