

SAB Homes


HF02 Redbud 2034 SW Farmfield Ln. Lee's Summit, MO

Our firm has been asked to make alternate structural recommendations for the house being built at the address listed above. During the rough in inspection the AHJ has questioned items. Below is a list of our recommendations along with the corresponding city item.

The framer has installed a (2) 1 3/4"X9 1/2" LVL between the Entry and Breakfast room instead of the planned W8X13 steel beam. After reviewing the code loading and spans our firm recommends approval of this alternate framing item as shown below.

This report has been prepared for the exclusive use of our client for specific application to the project discussed and has been prepared in accordance with generally accepted engineering practices. No warranties, either express or implied, are intended or made.

We appreciate the opportunity to be of service to you on this project. If you have any questions regarding this report, please contact us.

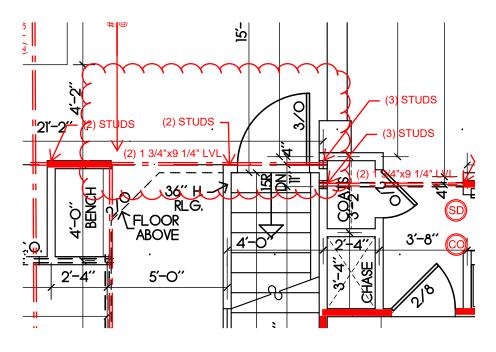



STRUCTURAL REVIEW HD ENGINEERING & DESIGN HD: 42618 DATE: 5/16/2022

11656 W. 75th Street Shawnee, KS 66214
