



PPF Location: 201 NW Chipman Rd
HH FID: 15640427
Distance to PFP: ~10 ft

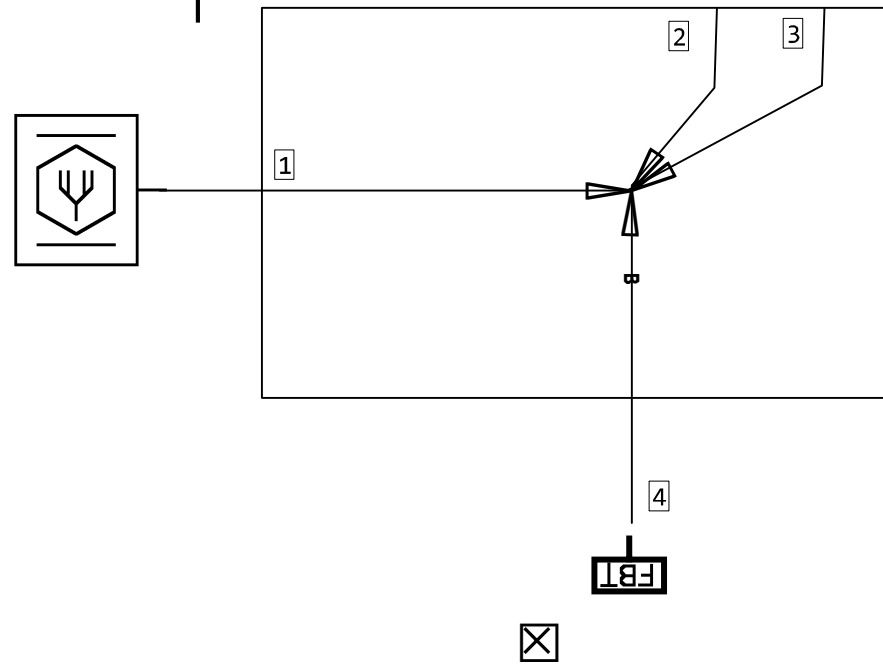

- 1 (2018) 845C 100' 5BQ2MR-288 PON201NWC,1-288
- 2 (2018) 845C 715' FNAP-CBL-024EUC PON201NWC,181-204
- 3 (2018) 845C 2532' 5BQ2MT-216 PON201NWC,1-180 A,181-216
- 4 **kscymo41**
R 201-2 NW Chipman RD
EVOLV6/100RAW (PPA) 845C
PON201NWC,205-210

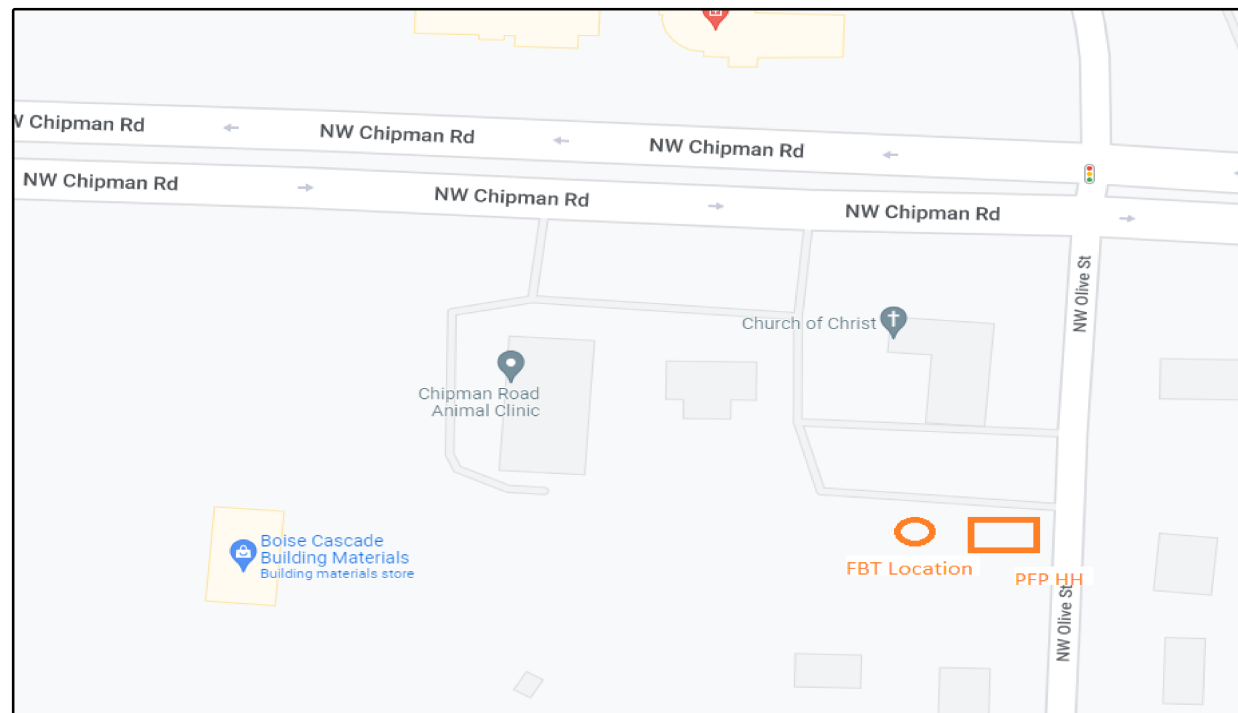

- 1 845C
1 READY FOR SERVICE TRIGGER
- 2 845C
12 SPLICE FIBER NEW RIBBON Z
- 3 845C
6 TESTING FIBER FACILITIES
- 4 845C
6 TESTING FIBER FACILITIES
- 5 845C
EVOLV6/100RAW
1 PLACE FLEXNAP TERMINAL, I
1 EXEMPT MATERIAL ONLY
- 6 845C
PEDESTAL
1 SVA ONLY - PLACE PEDESTAL
1 EXEMPT MATERIAL ONLY
- 7 845C
CONT-PL-CABLE
10 SVA ONLY - HAND DIG AND P
10 EXEMPT MATERIAL ONLY

PROJECT # A02HTJ8		DATE SVC REQ'D 02/08/2023
NPANNX 816524	GEO LOC EE4160	CLLI KSCYMO41
PRIMARY ENGR.: PEDERSEN, CHARLES M		
ENGR. ID: CP861N	PERMIT REQ'D.	N
PHONE #: 8168133667	PRINT	1 OF 1

Project will place new FBT and PEDESTAL by existing HH at PFP location.
 Place 6 port FBT EVOLV with 100 ft Raw tether to Splice in HH.
 Place Pedestal to the west of the of HH
