

TRANSMITTAL No. 003

To: Battalion Chief Jim Eden
207 S.E. Douglas
Lee's Summit, MO 64063

Date: 3/4/24

Contract No: 20543M

Attn: Jim Eden

Job Name: SLE ASC Expansion

The following listed items are enclosed:

☒ Drawings ☐ Submittal Data ☒ Hydraulics ☐ Other

Copies	Dated	Drawing No.	Description
1	2/28/24	1-6 of 6	FP Drawings for Approval (PDF COPY)
1	2/28/24	Area	Hydraulic Calculations for Approval (PDF COPY)


These are transmitted to you for:


☒ Approval ☐ Your use ☐ Coordination ☐ Construction

Please return 2 copy(s) bearing your approval.

REMARKS: Please find attached the above referenced item(s).
Please return (2) copy(s) bearing your approval. If you have any
questions, please contact Tucker S. at (913) 422-3770. Thank you.

Shelly Meyers
Administrative Assistant



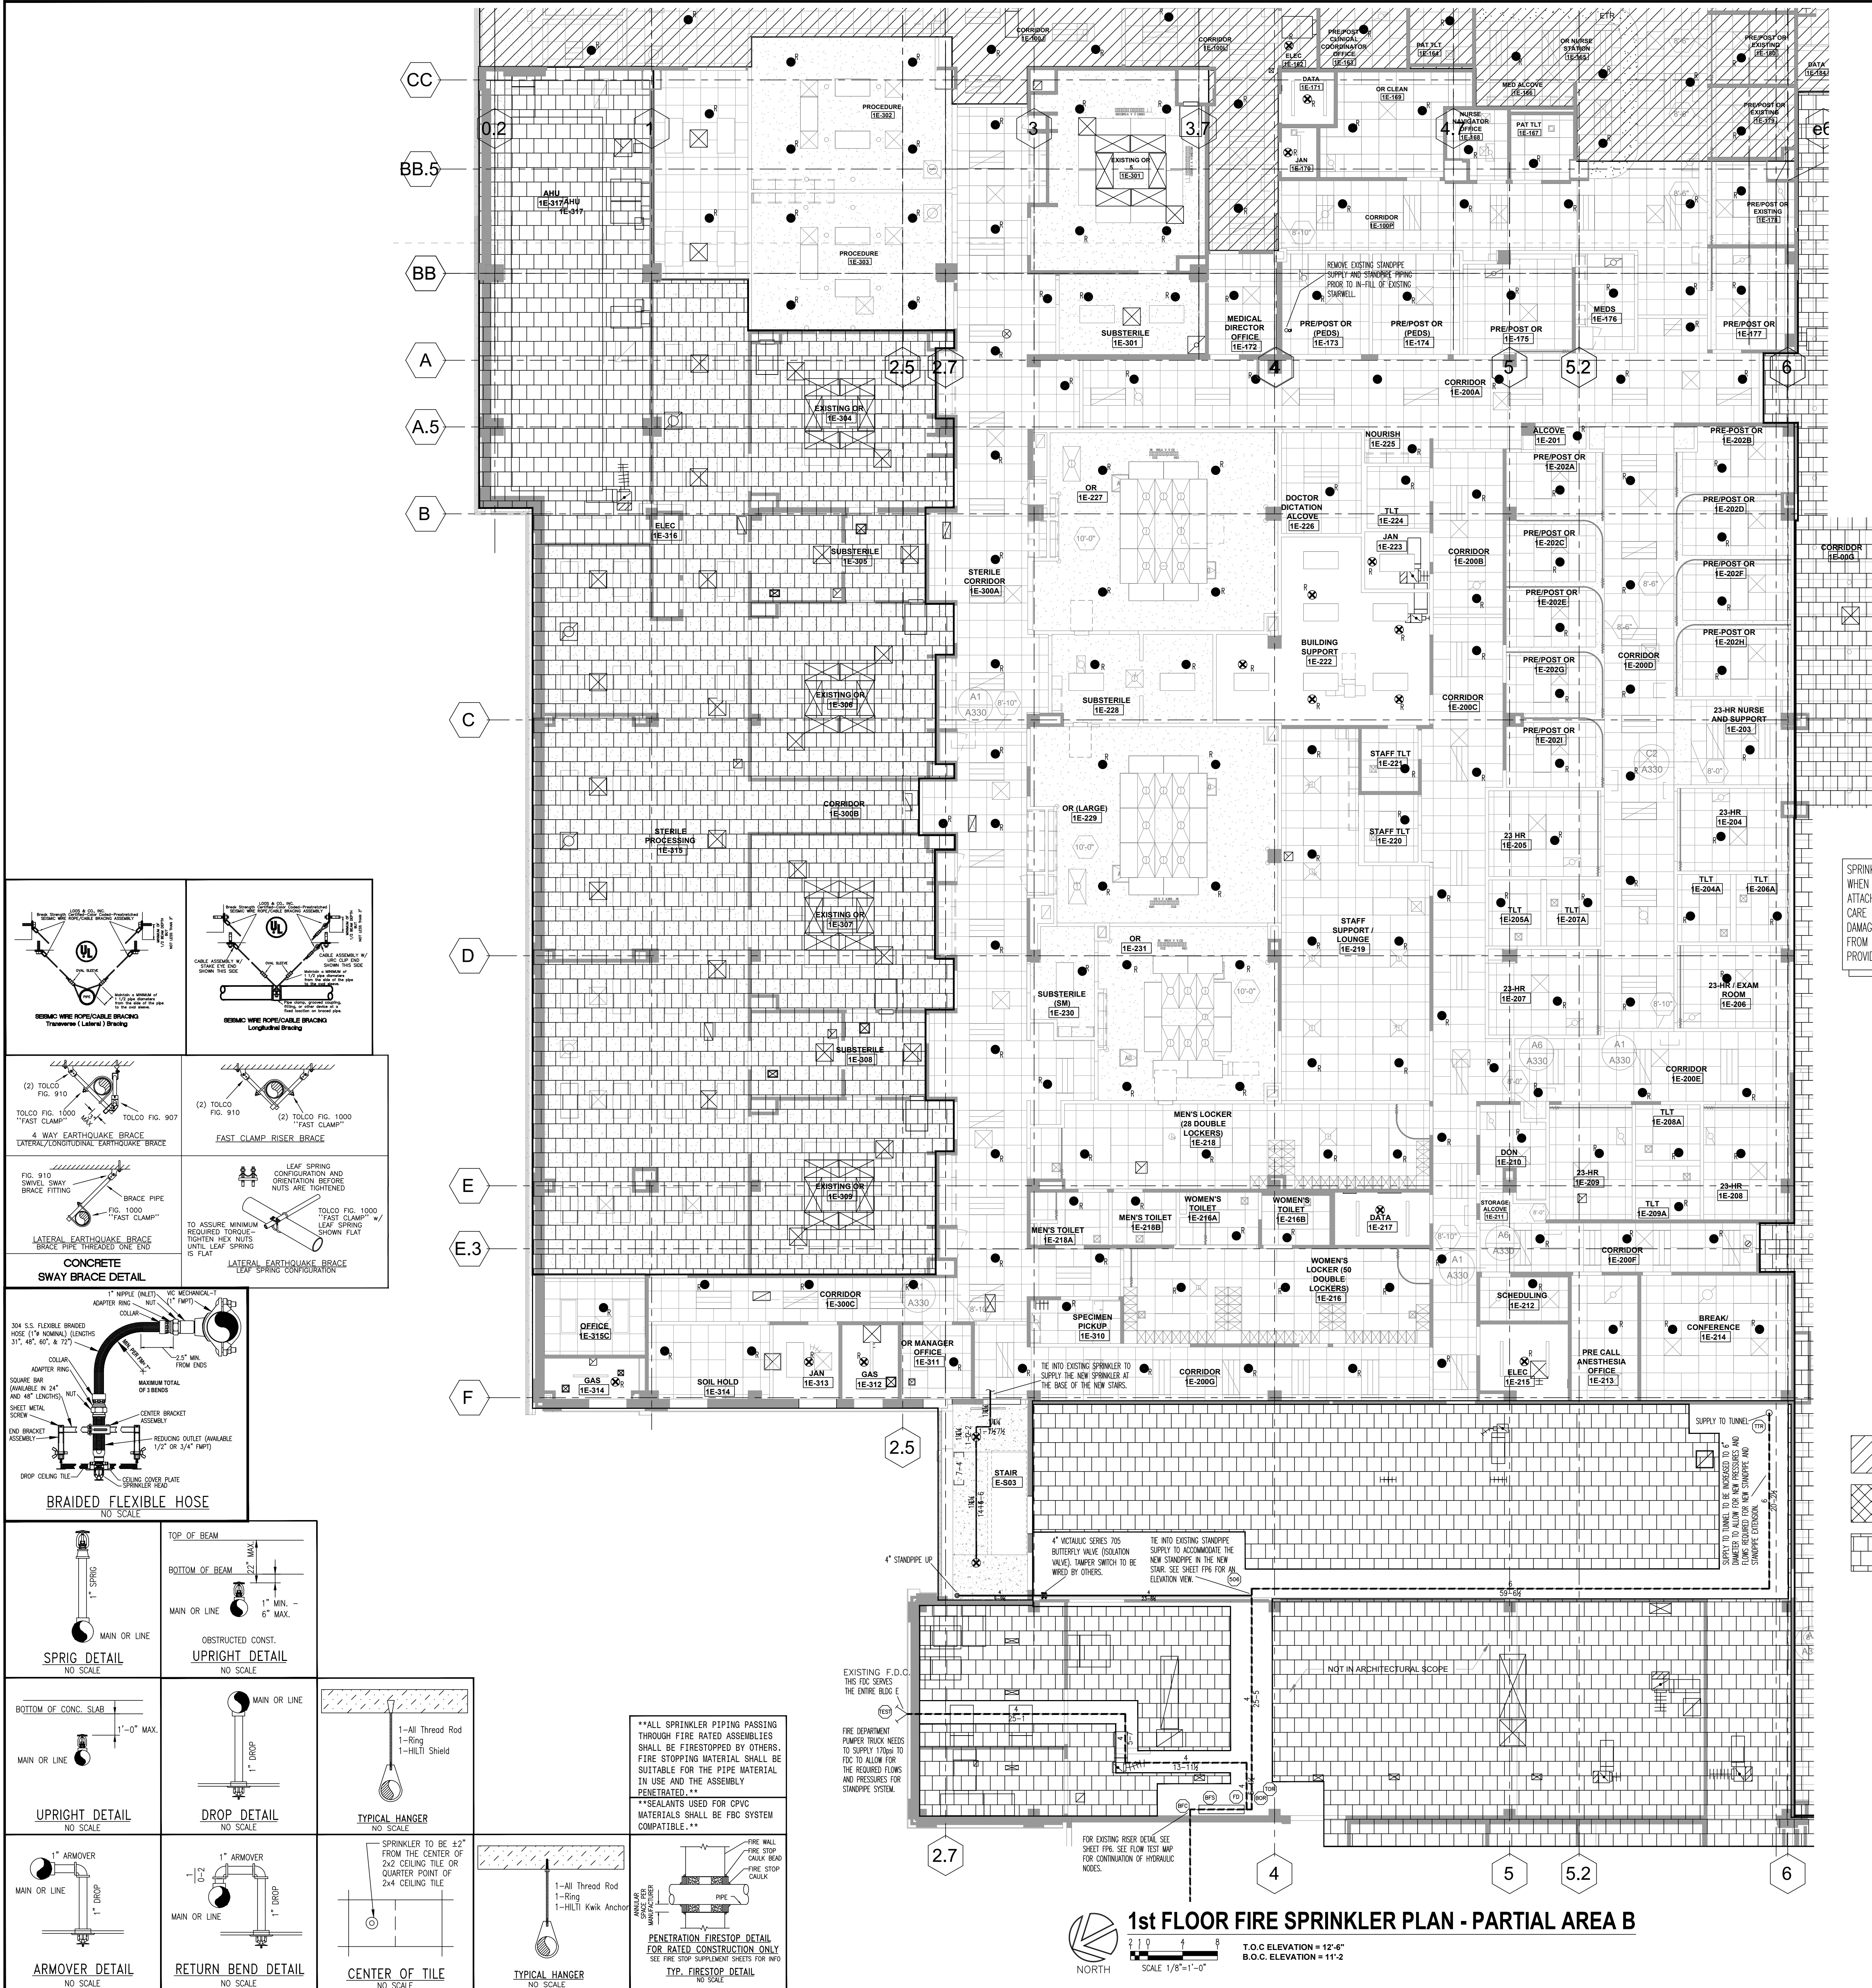


SPRINKLERS ARE PERMITTED TO BE RELOCATED AND RE-INSTALLED WHEN THE SPRINKLER BEING REMOVED FROM THE SYSTEM REMAINS ATTACHED TO THE ORIGINAL FITTING OR WELDED OUTLET, PROVIDED CARE HAS BEEN TAKEN TO ENSURE THE SPRINKLER HAS NOT BEEN DAMAGED. PER NFPA 13, WHEN A SPRINKLER HAS BEEN REMOVED FROM A FITTING OR WELDED OUTLET, IT SHALL NOT BE RE-INSTALLED. PROVIDE NEW SPRINKLERS AS REQUIRED.

AREA A & PARTIAL AREA B - SHEET FP1

AREA B - PARTIAL VIEW - SHEET FP2

NO WORK - NOT IN CONTRACT

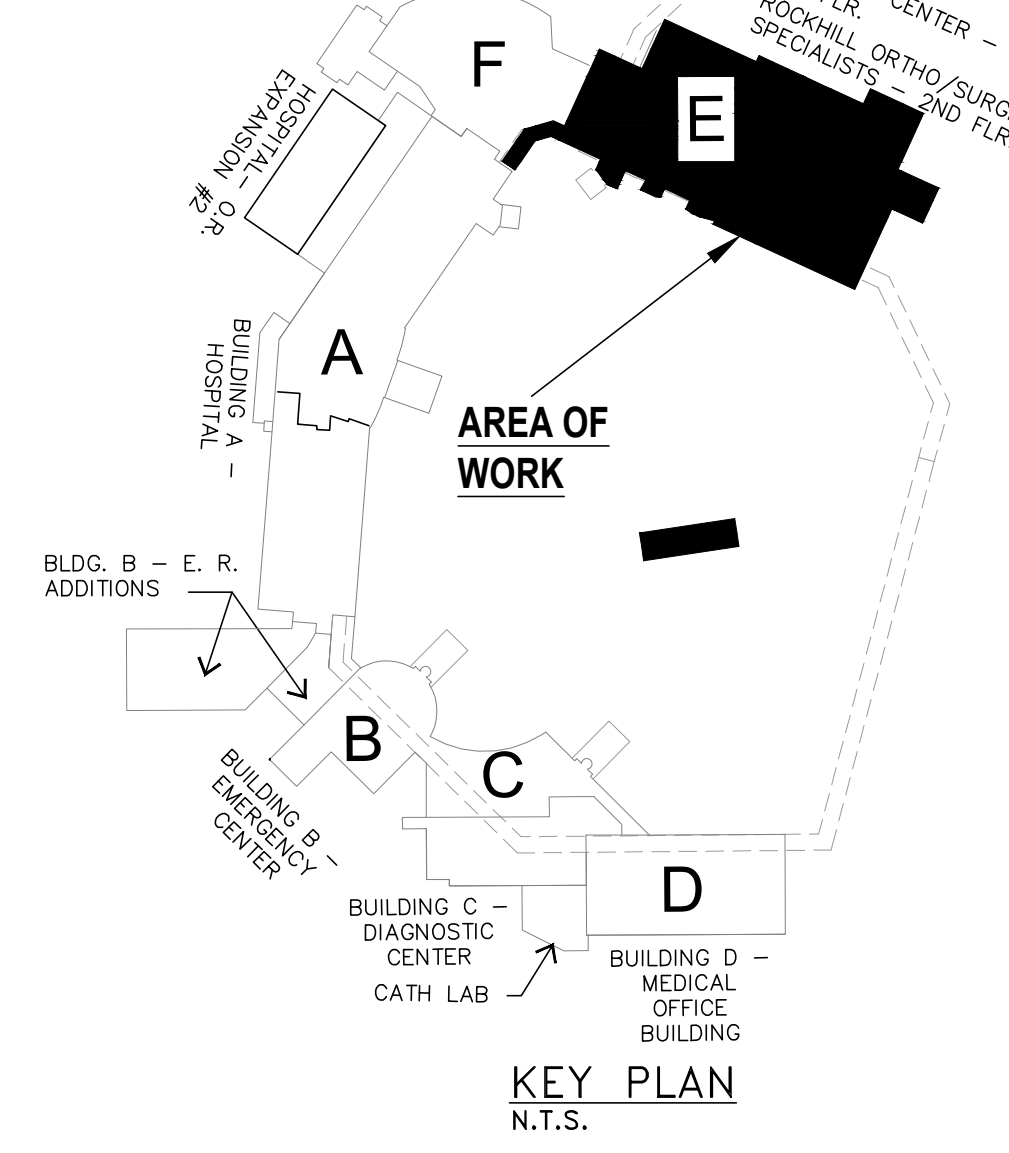

REVISIONS:

NO.	DATE	DESCRIPTION
1	10/27/24	ALL DRAWINGS ARE CURRENT THROUGH ALL 18 CHANGES

JAYHAWK FIRE SPRINKLER CO., INC.

12010 E. 120th St., Suite 100, Overland Park, KS 66204

PHONE: (913) 777-7777

FAX: (913) 777-7777

MOBILE: (913) 777-7777

MASSBY CONSTRUCTION

7850 SAINT LUKE DRIVE

OVERLAND PARK, KANSAS 66204

100 NE Saint Luke's Blvd.

Lee's Summit, MO 64066

SAINT LUKE'S HEALTH SYSTEM

ASC EXPANSION

WALTER A. WARREN

REGISTERED PROFESSIONAL ENGINEER

NUMBER E-24557

03/09/2024

Warren KTD, LLC

20543M

PROJECT NUMBER: TJA

CHECKED BY: DO

PROJECT MANAGER: TS

APPROVAL

DATE: 01/15/2024

ISSUE DATE: 02/28/2024

FP-2

FIRE PROTECTION

REMODEL 1ST FLOOR

AREA B

2 OF 6

2ND FLOOR SPRINKLER SYSTEM PIPING HAS BEEN CALCULATED USING THE EXISTING 4" SUPPLY IN THE TUNNEL. IF JFS IS TO INCREASE THIS PIPING TO 6" TO ACCOMMODATE THE NEW PRESSURE AND FLOW REQUIREMENTS FOR THE EXTENSION OF THE STANDPIPE SYSTEM, IT WILL ONLY INCREASE THE AMOUNT OF SAFETY ON THE SYSTEM PIPING.

AREA OF REDUCTION TAKEN FOR QUICK RESPONSE SPRINKLERS

CEILING HEIGHT, FT.

SCALE: NONE

AREA #2

HYDRAULIC SYSTEM

THIS BUILDING IS PROTECTED BY A HYDRAULICALLY DESIGNED AUTOMATIC SPRINKLER SYSTEM

DESIGN AREA: AREA 2

LOCATION: EXAM ROOMS AND CORRIDOR

NO. OF SPRINKLERS: 10

SPRINKLER TYPE: VICTALUC Q.R. PENDENT

ORIFICE: 1/2" K-FACTOR: 5.6

BASIS FOR DESIGN:

1. DENSITY: .10

2. REQUIRED AREA OF DISCHARGE: 900 SQ.FT.

SYSTEM DEMAND:

1. Q.M. DISCHARGE: 324.098 GPM

2. RESIDUAL PRESSURE AT THE MOUTH OF THE RISER: 65.218 PSI

3. HOSE SYSTEM: 100 GPM

4. RESIDUAL PRESSURE AT POINT CONNECTION: 73.560 PSI

PLAN NOTES:

1. ALL CEILING HEIGHTS TO BE 9'-0" ABOVE FINISHED FLOOR UNLESS NOTED OTHERWISE.

2. SPRINKLERS SHALL BE CENTERED IN THE NARROW DIMENSION OF CEILING TILES, AS SPECIFIED (211313-3.6.A).

3. ALL THREADED PIPING IS TO BE ALLIED "SCHEDULE 40" WITH THREADED CAST IRON FITTINGS.

4. ALL GROOVED PIPING IS TO BE SCH. 40 PIPE, ASTM A-795 WITH ROLLED GROOVED ENDS. ALL FITTINGS TO BE IRON GROOVED OR WELDED STEEL OUTLETS.

DESIGN CRITERIA:

BUILDING CODE: SEE CODE SUMMARY

OCCUPANCY: SEE CODE SUMMARY

TYPE OF CONSTRUCTION: SEE CODE SUMMARY

AREA OF CONSTRUCTION: SEE CODE SUMMARY

PER NFPA 13, 2016 EDITION:

SYSTEM TYPE: WET (EXISTING)

CORRIDOR, PATIENT ROOMS, OFFICES, ETC., LIGHT HAZARD

0.10 GPM/S.F. FOR 1500 S.F.

MAXIMUM 225 S.F. SPRINKLER SPACING

100 GPM HOSE ALLOWANCE

MECHANICAL ROOMS, STORAGE ROOMS, ETC., LIGHT HAZARD

0.10 GPM/S.F. FOR 1500 S.F.

MAXIMUM 225 S.F. SPRINKLER SPACING

300 GPM HOSE ALLOWANCE

FLOW TEST DATA:

DATE: 12-18-2023 / 11:15AM

INFO FROM: CITY OF LEE'S SUMMIT

STATID: 104 PSI

RESIDUAL: 92 PSI

FLOW: 2300 GPM

LOCATION: 100 NE ST. LUKE'S BLVD.

GENERAL NOTES:

ALL FITTINGS CONFORM TO SECTION 2-4 OF NFPA PAMPHLET 13.

VALVES ON CONNECTIONS TO WATER SUPPLIES, SECTIONAL CONTROL VALVES AND OTHER VALVES IN SUPPLY LINES TO SPRINKLERS SHALL BE SUPERVISED OPEN BY AN APPROVED METHOD.

IT IS THE OWNERS RESPONSIBILITY TO PROVIDE ADEQUATE HEAT TO KEEP THE SPRINKLER SYSTEM FROM FREEZING.

ALL ELECTRICAL WIRING OF ALARM BELLS, FLOW SWITCHES AND TAMPERS SWITCHES (IF REQUIRED) TO BE DONE BY OTHERS.

THE SPRINKLER SYSTEM TO BE INSTALLED IN ACCORDANCE WITH NFPA 13.

HANGERS TO BE SPACED TO MEET NFPA REQUIREMENTS

PER NFPA 13, SECTION 8.6.3.2.4, WITHIN SMALL ROOMS AS DEFINED IN SECTION 3.3.2.0, SPRINKLERS SHALL BE PERMITTED TO BE LOCATED NOT MORE THAN 9 FT. FROM ANY SINGLE WALL, AND SPRINKLER SPACING LIMITATIONS OF SECTION 8.6.3 AND AREA LIMITATIONS OF TABLE 8.6.2.2.1(a) SHALL NOT BE EXCEEDED. JFS MAY MODIFY HEADS SHOWN ON THIS DRAWING TO COMPLY WITH THIS RULE.

CL = CENTER LINE OF PIPE BELOW TOP OF STEEL

EL = CENTER LINE OF PIPE ABOVE FINISHED FLOOR

CONSTRUCTION:

CONCRETE SLABS, CONCRETE BEAMS AND TEES

CODE NOTE:

8.6.5.2.2.1

IN LIGHT HAZARD OCCUPANCIES, PRIVACY CURTAINS SHALL NOT BE CONSIDERED OBSTRUCTIONS WHERE ALL OF THE FOLLOWING AREA MET:

(1) THE CURTAINS ARE SUPPORTED BY FABRIC MESH OR CEILING TRACK.

(2) OPENINGS IN THE MESH ARE EQUAL TO 70 PERCENT OR GREATER.

(3) THE MESH EXTENDS A MINIMUM OF 22 INCHES DOWN FROM CEILING.

CODE SUMMARY:

Project Construction Purpose: New 3 story addition and partial renovation of existing ASC building.

Project Address: Saint Luke's East Hospital 120 NE Saint Luke's Blvd Lee's Summit, MO 64063

Code Information

2018 International Building Code

2018 International Plumbing Code

2018 International Mechanical Code

2017 National Electrical Code (NFPA 70)

2018 International Fire Code

2012 Life Safety Code (NFPA 101 Chapter 20)

2009 ICC/ANSI A117.1 as amended and adopted by the City of Lee's Summit

2010 ADA Standards for Accessible Design / Americans with Disabilities Act of 1990

State of Missouri Dept. of Health & Environment references the following codes:

2012 NFPA 101 Life Safety Code (LSC)

2018 FGI Guidelines for Design & Construction of Hospitals & Outpatient Facilities

1979 19-CSR-30

Note: If code requirements overlap, the most stringent shall apply.

Owner Information

Saint Luke's East Hospital 120 NE Saint Luke's Blvd Lee's Summit, MO 64063

Designer Information

ACI Boland Architects 1710 Wyandotte St. Kansas City, MO 64108 Phone: (816) 763-3600

Local Authority

Responding Fire Service: Lee's Summit Fire Department

Local Building Inspection: Lee's Summit, MO - Codes Administration Department

Type of Construction: I-A

Area of Renovation and Addition

1st floor addition 18,000+/- SF

2nd floor renovation 23,000+/- SF

2nd floor addition 16,700+/- SF

2nd floor renovation 28,988+/- SF

3rd floor addition 27,514+/- SF

Total addition: 62,214+/- SF

Total renovation: 51,889+/- SF

Total of new construction: 115,913+/- SF

Occupancy Group: B - Ambulatory Healthcare

Max Travel Distance: 200' (NFPA 101 20.2.6.2.1)

Occupant Load: 1505SF/OCC (table 1004.5)

1st floor: 41,601/150 = 278

2nd floor: 44,798/150 = 299

3rd floor: 27,514/150 = 184

Total Number of Occupants = 761

Required Fire Resistance Ratings (in hours)

Per NFPA 101 A.8.2.1.2:

Exterior Bearing Walls 3 HR

Interior Bearing Walls 3 HR

Primary Structural Frame 3 HR

Floor Construction 1 1/2 HR

Roof Construction 1 1/2 HR

Interior Non-bearing Walls 0 HR

Shaft Enclosure 2 HR

Stair Enclosure 2 HR

Fire Separation: (table 508.4)

2 HR separation between tenants I-B

1 HR separation between tenants B-B

SPRINKLERS ARE PERMITTED TO BE RELOCATED AND RE-INSTALLED WHEN THE SPRINKLER BEING REMOVED FROM THE SYSTEM REMAINS ATTACHED TO THE ORIGINAL FITTING OR WELDED OUTLET. PROVIDED CARE HAS BEEN TAKEN TO ENSURE THE SPRINKLER HAS NOT BEEN DAMAGED. PER NFPA 13, WHEN A SPRINKLER HAS BEEN REMOVED FROM A FITTING OR WELDED OUTLET, IT SHALL NOT BE RE-INSTALLED. PROVIDE NEW SPRINKLERS AS REQUIRED.

2nd FLOOR FIRE SPRINKLER PLAN - AREA A

SCALE: 1/8"=1'-0"

T.O.C. ELEVATION = 12'-6"

B.O.C. ELEVATION = 11'-2"

AREA A - SHEET FP3

AREA B - SHEET FP4

-NO WORK - NOT IN CONTRACT

SPRINKLER RELOCATION LEGEND

SYMBOL	DESCRIPTION
SYMBOL A	RELOCATED SPRINKLER FROM EXISTING OUTLET
SYMBOL B	CHANGED EXISTING SPRINKLER FROM S.R. TO Q.R.
SYMBOL C	ADDED SPRINKLER FROM EXISTING SPRINKLER SYSTEM
SYMBOL D	NEW SPRINKLER BEING INSTALLED FROM NEW SYSTEM

LEGEND

SYMBOL	DESCRIPTION
SYMBOL E	EXISTING SPRINKLER TO REMAIN
SYMBOL F	EXISTING SPRINKLER TO BE RELOCATED/REPLACED
SYMBOL G	EXISTING RISER NIPPLE TO REMAIN
SYMBOL H	NEW SPRINKLER LINE
SYMBOL I	EXISTING SPRINKLER LINE
SYMBOL J	POINT OF CONNECTION
SYMBOL K	HANGER LOCATION
SYMBOL L	PIPE END CAP

SPRINKLER LEGEND

SYMBOL	SPRINKLER TYPE	SIN #	FINISH	TEMP.	ORIFICE	K-FACTOR	COUNT
SYMBOL M	VICTALUC Q.R. CONCEALED PENDENT	V5606	WHITE	155°	1/2"	5.6 K	242
SYMBOL N	VICTALUC Q.R. UPRIGHT	V3402	BRASS	155°	3/4"	8.0 K	03

KEY PLAN

AREA A

AREA B

AREA C

AREA D

AREA E

AREA F

AREA G

AREA H

AREA I

AREA J

AREA K

AREA L

AREA M

AREA N

AREA O

AREA P

AREA Q

AREA R

AREA S

AREA T

AREA U

AREA V

AREA W

AREA X

AREA Y

AREA Z

AREA AA

AREA AB

AREA AC

AREA AD

AREA AE

AREA AF

AREA AG

AREA AH

AREA AI

AREA AJ

AREA AK

AREA AL

AREA AM

AREA AN

AREA AO

AREA AP

AREA AQ

AREA AR

AREA AS

AREA AT

AREA AU

AREA AV

AREA AW

AREA AX

AREA AY

AREA AZ

AREA BA

AREA BB

AREA BC

AREA BD

AREA BE

AREA BF

AREA BG

AREA BH

AREA BI

AREA BJ

AREA BK

AREA BL

AREA BM

AREA BN

AREA BO

AREA BP

AREA BQ

AREA BR

AREA BS

AREA BT

AREA BU

AREA BV

AREA BW

AREA BX

AREA BY

AREA BZ

AREA CA

AREA CB

AREA CC

AREA CD

AREA CE

AREA CF

AREA CG

AREA CH

AREA CI

AREA CJ

AREA CK

AREA CL

AREA CM

AREA CN

AREA CO

AREA CP

AREA CQ

AREA CR

AREA CS

AREA CT

AREA CU

AREA CV

AREA CW

AREA CX

AREA CY

AREA CZ

AREA DA

AREA DB

AREA DC

AREA DD

AREA DE

AREA DF

AREA DG

AREA DH

AREA DI

AREA DJ

AREA DK

AREA DL

AREA DM

AREA DN

AREA DO

AREA DP

AREA DQ

AREA DR

AREA DS

AREA DT

AREA DU

AREA DV

AREA DW

AREA DX

AREA DY

AREA DZ

AREA EA

AREA EB

AREA EC

AREA ED

AREA EE

AREA EF

AREA EG

AREA EH

AREA EI

AREA EJ

AREA EK

AREA EL

AREA EM

AREA EN

AREA EO

AREA EP

AREA EQ

AREA ER

AREA ES

AREA ET

AREA EU

AREA EV

AREA EW

AREA EX

AREA EY

AREA EZ

AREA FA

AREA FB

AREA FC

AREA FD

AREA FE

AREA FF

AREA FG

AREA FH

AREA FI

AREA FJ

AREA FK

AREA FL

AREA FM

AREA FN

AREA FO

AREA FP

AREA FQ

AREA FR

AREA FS

AREA FT

AREA FU

AREA FV

AREA FW

AREA FX

AREA FY

AREA FZ

AREA GA

AREA GB

AREA GC

AREA GD

AREA GE

AREA GF

AREA GH

AREA GI

AREA GJ

AREA GK

AREA GL

AREA GM

AREA GN

AREA GO

AREA GP

AREA GQ

AREA GR

AREA GS

AREA GT

AREA GU

AREA GV

AREA GW

AREA GX

AREA GY

AREA GZ

AREA HA

AREA HB

AREA HC

AREA HD

AREA HE

AREA HF

AREA HG

AREA HH

AREA HI

AREA HJ

AREA HK

AREA HL

AREA HM

AREA HN

AREA HO

AREA HP

AREA HQ

AREA HR

AREA HS

AREA HT

AREA HU

AREA HV

AREA HW

AREA HX

AREA HY

AREA HZ

AREA IA

AREA IB

AREA IC

AREA ID

AREA IE

AREA IF

AREA IG

AREA IH

AREA II

AREA IJ

AREA IK

AREA IL

AREA IM

AREA IN

AREA IO

AREA IP

AREA IQ

AREA IR

AREA IS

AREA IT

AREA IU

AREA IV

AREA IW

AREA IX

AREA IY

AREA IZ

AREA JA

AREA JB

AREA JC

AREA JD

AREA JE

AREA JF

AREA JG

AREA JH

AREA JI

AREA JJ

AREA JK

AREA JL

AREA JM

AREA JN

AREA JO

AREA JP

AREA JQ

AREA JR

AREA JS

AREA JT

AREA JU

AREA JV

AREA JW

AREA JX

AREA JY

AREA JZ

AREA KA

AREA KB

AREA KC

AREA KD

AREA KE

AREA KF

AREA KG

AREA KH

AREA KI

AREA KJ

AREA KK

AREA KL

AREA KM

AREA KN

AREA KO

AREA KP

AREA KQ

AREA KR

AREA KS

AREA KT

AREA KU

AREA KV

AREA KW

AREA KX

AREA KY

AREA KZ

AREA LA

AREA LB

AREA LC

AREA LD

AREA LE

AREA LF

AREA LG

AREA LH

AREA LI

AREA LJ

AREA LK

AREA LL

AREA LM

AREA LN

AREA LO

AREA LP

AREA LQ

AREA LR

AREA LS

AREA LT

AREA LU

AREA LV

AREA LW

AREA LX

AREA LY

AREA LZ

AREA MA

AREA MB

AREA MC

AREA MD

AREA ME

AREA MF

AREA MG

AREA MH

AREA MI

AREA MJ

AREA MK

AREA ML

AREA MN

AREA MO

AREA MP

AREA MQ

AREA MR

AREA MS

AREA MT

AREA MU

AREA MV

AREA MW

AREA MX

AREA MY

AREA MZ

AREA NA

AREA NB

AREA NC

AREA ND

AREA NE

AREA NF

AREA NG

AREA NH

AREA NI

AREA NJ

AREA NK

AREA NL

AREA NM

AREA NN

AREA NO

AREA NP

AREA NQ

AREA NR

AREA NS

AREA NT

AREA NU

AREA NV

AREA NW

AREA NX

AREA NY

AREA NZ

AREA OA

AREA OB

AREA OC

AREA OD

AREA OE

AREA OF

AREA OG

AREA OH

AREA OI

AREA OJ

AREA OK

AREA OL

AREA OM

AREA ON

AREA OO

AREA OP

AREA OQ

AREA OR

AREA OS

AREA OT

AREA OU

AREA OV

AREA OW

AREA OX

AREA OY

AREA OZ

AREA PA

AREA PB

AREA PC

AREA PD

AREA PE

AREA PF

AREA PG

AREA PH

AREA PI

AREA PJ

AREA PK

AREA PL

AREA PM

AREA PN

AREA PO

AREA PP

AREA PQ

AREA PR

AREA PS

AREA PT

AREA PU

AREA PV

AREA PW

AREA PX

AREA PY

AREA PZ

AREA QA

AREA QB

AREA QC

AREA QD

AREA QE

AREA QF

AREA QG

AREA QH

AREA QI

AREA QJ

AREA QK

AREA QL

AREA QM

AREA QN

AREA QO

AREA QP

AREA QQ

AREA QR

AREA QS

AREA QT

AREA QU

AREA QV

AREA QW

AREA QX

AREA QY

AREA QZ

AREA RA

AREA RB

AREA RC

AREA RD

AREA RE

AREA RF

AREA RG

AREA RH

AREA RI

AREA RJ

AREA RK

AREA RL

AREA RM

AREA RN

AREA RO

AREA RP

AREA RQ

AREA RR

AREA RS

AREA RT

AREA RU

AREA RV

AREA RW

AREA RX

AREA RY

AREA RZ

AREA SA

AREA SB

AREA SC

AREA SD

AREA SE

AREA SF

AREA SG

AREA SH

AREA SI

AREA SJ

AREA SK

AREA SL

AREA SM

AREA SN

AREA SO

AREA SP

AREA SQ

AREA SR

AREA SS

AREA ST

AREA SU

AREA SV

AREA SW

AREA SX

AREA SY

AREA SZ

AREA TA

AREA TB

AREA TC

AREA TD

AREA TE

AREA TF

AREA TG

AREA TH

AREA TI

AREA TJ

AREA TK

AREA TL

AREA TM

AREA TN

AREA TO

AREA TP

AREA TQ

AREA TR

AREA TS

AREA TT

AREA TU

AREA TV

AREA TW

AREA TX

AREA TY

AREA TZ

AREA UA

AREA UB

AREA UC

AREA UD

AREA UE

AREA UF

AREA UG

AREA UH

AREA UI

AREA UJ

AREA UK

AREA UL

AREA UM

AREA UN

AREA UO

AREA UP

AREA UQ

AREA UR

AREA US

AREA UT

AREA UY

AREA UZ

AREA VA

AREA VB

AREA VC

AREA VD

AREA VE

AREA VF

AREA VG

AREA VH

AREA VI

AREA VJ

AREA VK

AREA VL

AREA VM

AREA VN

AREA VO

AREA VP

AREA VQ

AREA VR

AREA VS

AREA VT

AREA VY

AREA VZ

AREA WA

AREA WB

AREA WC

AREA WD

AREA WE

AREA WF

AREA WG

AREA WH

AREA WI

AREA WJ

AREA WK

AREA WL

AREA WM

AREA WN

AREA WO

AREA WP

AREA WQ

AREA WR

AREA WS

AREA WT

AREA WY

AREA WZ

AREA XA

AREA XB

AREA XC

AREA XD

AREA XE

AREA XF

AREA XG

AREA XH

AREA XI

AREA XJ

AREA XK

AREA XL

AREA XM

AREA XN

AREA XO

AREA XP

AREA XQ

AREA XR

AREA XS

AREA XT

AREA XU

AREA XV

AREA XW

AREA XX

AREA XY

AREA XZ

AREA YA

AREA YB

AREA YC

AREA YD

AREA YE

AREA YF

AREA YG

AREA YH

AREA YI

AREA YJ

AREA YK

AREA YL

AREA YM

AREA YN

AREA YO

AREA YP

AREA YQ

AREA YR

AREA YS

AREA YT

AREA YU

AREA YV

AREA YW

AREA YX

AREA YY

AREA YZ

AREA ZA

AREA ZB

AREA ZC

AREA ZD

AREA ZE

AREA ZF

AREA ZG

AREA ZH

AREA ZI

AREA ZJ

AREA ZK

AREA ZL

AREA ZM

AREA ZN

AREA ZO

AREA ZP

AREA ZQ

AREA ZR

AREA ZS

AREA ZT

AREA ZY

AREA ZZ

SPRIG DETAIL

NO SCALE

UPRIGHT DETAIL

NO SCALE

UPRIGHT DETAIL

NO SCALE

DROP DETAIL

NO SCALE

ARMORER DETAIL

NO SCALE

RETURN BEND DETAIL

NO SCALE

CENTER OF TILE

NO SCALE

TYPICAL HANGER

NO SCALE

TYPICAL HANGER

NO SCALE

PENETRATION FIRESTOP DETAIL

FOR RATED CONSTRUCTION ONLY

SEE FIRE STOP SUPPLEMENT SHEETS FOR INFO

TYP. FIRESTOP DETAIL

NO SCALE

SPRINKLER RELOCATION LEGEND

SYMBOL	DESCRIPTION
SYMBOL A	RELOCATED SPRINKLER FROM EXISTING OUTLET
SYMBOL B	CHANGED EXISTING SPRINKLER FROM S.R. TO Q.R.
SYMBOL C	ADDED SPRINKLER FROM EXISTING SPRINKLER SYSTEM
SYMBOL D	NEW SPRINKLER BEING INSTALLED FROM NEW SYSTEM

LEGEND

SYMBOL	DESCRIPTION
SYMBOL E	EXISTING SPRINKLER TO REMAIN
SYMBOL F	EXISTING SPRINKLER TO BE RELOCATED/REPLACED
SYMBOL G	EXISTING RISER NIPPLE TO REMAIN
SYMBOL H	NEW SPRINKLER LINE
SYMBOL I	EXISTING SPRINKLER LINE
SYMBOL J	POINT OF CONNECTION
SYMBOL K	HANGER LOCATION
SYMBOL L	PIPE END CAP

SPRINKLER LEGEND

SYMBOL	SPRINKLER TYPE	SIN #	FINISH	TEMP.	ORIFICE	K-FACTOR	COUNT
SYMBOL M	VICTALUC Q.R. CONCEALED PENDENT	V5606	WHITE	155°	1/2"	5.6 K	242
SYMBOL N	VICTALUC Q.R. UPRIGHT	V3402	BRASS	155°	3/4"	8.0 K	03

KEY PLAN

AREA A

AREA B

AREA C

AREA D

AREA E

AREA F

AREA G

AREA H

AREA I

AREA J

AREA K

AREA L

AREA M

AREA N

AREA O

AREA P

AREA Q

AREA R

AREA S

AREA T

AREA U

AREA V

AREA W

AREA X

AREA Y

AREA Z

AREA AA

AREA AB

AREA AC

AREA AD

AREA AE

AREA AF

AREA AG

AREA AH

AREA AI

AREA AJ

AREA AK

AREA AL

AREA AM

AREA AN

AREA AO

AREA AP

AREA AQ

AREA AR

AREA AS

AREA AT

AREA AU

AREA AV

AREA AW

AREA AX

AREA AY

AREA AZ

AREA BA

AREA BB

AREA BC

AREA BD

AREA BE

AREA BF

AREA BG

AREA BH

AREA BI

AREA BJ

AREA BK

AREA BL

AREA BM

AREA BN

AREA BO

AREA BP

AREA BQ

AREA BR

AREA BS

AREA BT

AREA BU

AREA BV

AREA BW

AREA BX

AREA BY

AREA BZ

AREA CA

AREA CB

AREA CC

AREA CD

AREA CE

AREA CF

AREA CG

AREA CH

AREA CI

AREA CJ

AREA CK

AREA CL

AREA CM

AREA CN

AREA CO

AREA CP

AREA CQ

AREA CR

AREA CS

AREA CT

AREA CU

AREA CV

AREA CW

AREA CX

AREA CY

AREA CZ

AREA DA

AREA DB

AREA DC

AREA DD

AREA DE

AREA DF

AREA DG

AREA DH

AREA DI

AREA DJ

AREA DK

AREA DL

AREA DM

AREA DN

AREA DO

AREA DP

AREA DQ

AREA DR

AREA DS

AREA DT

AREA DU

AREA DV

AREA DW

AREA DX

AREA DY

AREA DZ

AREA EA

AREA EB

AREA EC

AREA ED

AREA EE

AREA EF

AREA EG

AREA EH

AREA EI

AREA EJ

AREA EK

AREA EL

AREA EM

AREA EN

AREA EO

AREA EP

AREA EQ

AREA ER

AREA ES

AREA ET

AREA EU

AREA EV

AREA EW

AREA EX

AREA EY

AREA EZ

AREA FA

AREA FB

AREA FC

AREA FD

AREA FE

AREA FF

AREA FG

AREA FH

AREA FI

AREA FJ

AREA FK

AREA FL

AREA FM

AREA FN

AREA FO

AREA FP

AREA FQ

AREA FR

AREA FS

AREA FT

AREA FU

AREA FV

AREA FW

AREA FX

AREA FY

AREA FZ

AREA GA

AREA GB

AREA GC

AREA GD

AREA GE

AREA GF

AREA GH

AREA GI

AREA GJ

AREA GK

AREA GL

AREA GM

AREA GN

AREA GO

AREA GP

AREA GQ

AREA GR

AREA GS

AREA GT

AREA GU

AREA GV

AREA GW

AREA GX

AREA GY

AREA GZ

AREA HA

AREA HB

AREA HC

AREA HD

AREA HE

AREA HF

AREA HG

AREA HH

AREA HI

AREA HJ

AREA HK

AREA HL

AREA HM

AREA HN

AREA HO

AREA HP

AREA HQ

AREA HR

AREA HS

AREA HT

AREA HU

AREA HV

AREA HW

AREA HX

AREA HY

AREA HZ

AREA IA

AREA IB

AREA IC

AREA ID

AREA IE

AREA IF

AREA IG

AREA IH

AREA II

AREA IJ

AREA IK

AREA IL

AREA IM

AREA IN

AREA IO

AREA IP

AREA IQ

AREA IR

AREA IS

AREA IT

AREA IU

AREA IV

AREA IW

AREA IX

AREA IY

AREA IZ

AREA JA

AREA JB

AREA JC

AREA JD

AREA JE

AREA JF

AREA JG

AREA JH

AREA JI

AREA JJ

AREA JK

AREA JL

AREA JM

AREA JN

AREA JO

AREA JP

AREA JQ

AREA JR

AREA JS

AREA JT

AREA JU

AREA JV

AREA JW

AREA JX

AREA JY

AREA JZ

AREA KA

AREA KB

AREA KC

AREA KD

AREA KE

AREA KF

AREA KG

AREA KH

AREA KI

AREA KJ

AREA KL

AREA KM

AREA KN

AREA KO

AREA KP

AREA KQ

AREA KR

AREA KS

AREA KT

AREA KU

AREA KV

AREA KW

AREA KX

AREA KY

AREA KZ

AREA LA

AREA LB

AREA LC

AREA LD

AREA LE

AREA LF

AREA LG

AREA LH

AREA LI

AREA LJ

AREA LK

AREA LL

AREA LM

AREA LN

AREA LO

AREA LP

AREA LQ

AREA LR

AREA LS

AREA LT

AREA LU

AREA LV

AREA LW

AREA LX

AREA LY

AREA LZ

AREA MA

AREA MB

AREA MC

AREA MD

AREA ME

AREA MF

AREA MG

AREA MH

AREA MI

AREA MJ

AREA MK

AREA ML

AREA MN

AREA MO

AREA MP

AREA MQ

AREA MR

AREA MS

AREA MT

AREA MU

AREA MV

AREA MW

AREA MX

AREA MY

AREA MZ

AREA NA

AREA NB

AREA NC

AREA ND

AREA NE

AREA NF

AREA NG

AREA NH

AREA NI

AREA NJ

AREA NK

AREA NL

AREA NM

AREA NN

AREA NO

AREA NP

AREA NQ

AREA NR

AREA NS

AREA NT

AREA NU

AREA NV

AREA NW

AREA NX

AREA NY

AREA NZ

AREA OA

AREA OB

AREA OC

AREA OD

AREA OE

AREA OF

AREA OG

AREA OH

AREA OI

AREA OJ

AREA OK

AREA OL

AREA OM

AREA ON

AREA OO

AREA OP

AREA OQ

AREA OR

AREA OS

AREA OT

AREA OU

AREA OV

AREA OW

AREA OX

AREA OY

AREA OZ

AREA PA

AREA PB

AREA PC

AREA PD

AREA PE

AREA PF

AREA PG

AREA PH

AREA PI

AREA PJ

AREA PK

AREA PL

AREA PM

AREA PN

AREA PO

AREA PP

AREA PQ

AREA PR

AREA PS

AREA PT

AREA PU

AREA PV

AREA PW

AREA PX

AREA PY

AREA PZ

AREA QA

AREA QB

AREA QC

AREA QD

AREA QE

AREA QF

AREA QG

AREA QH

AREA QI

AREA QJ

AREA QK

AREA QL

AREA QM

AREA QN



AREA QO

AREA QP

AREA QQ

AREA QR

AREA QS

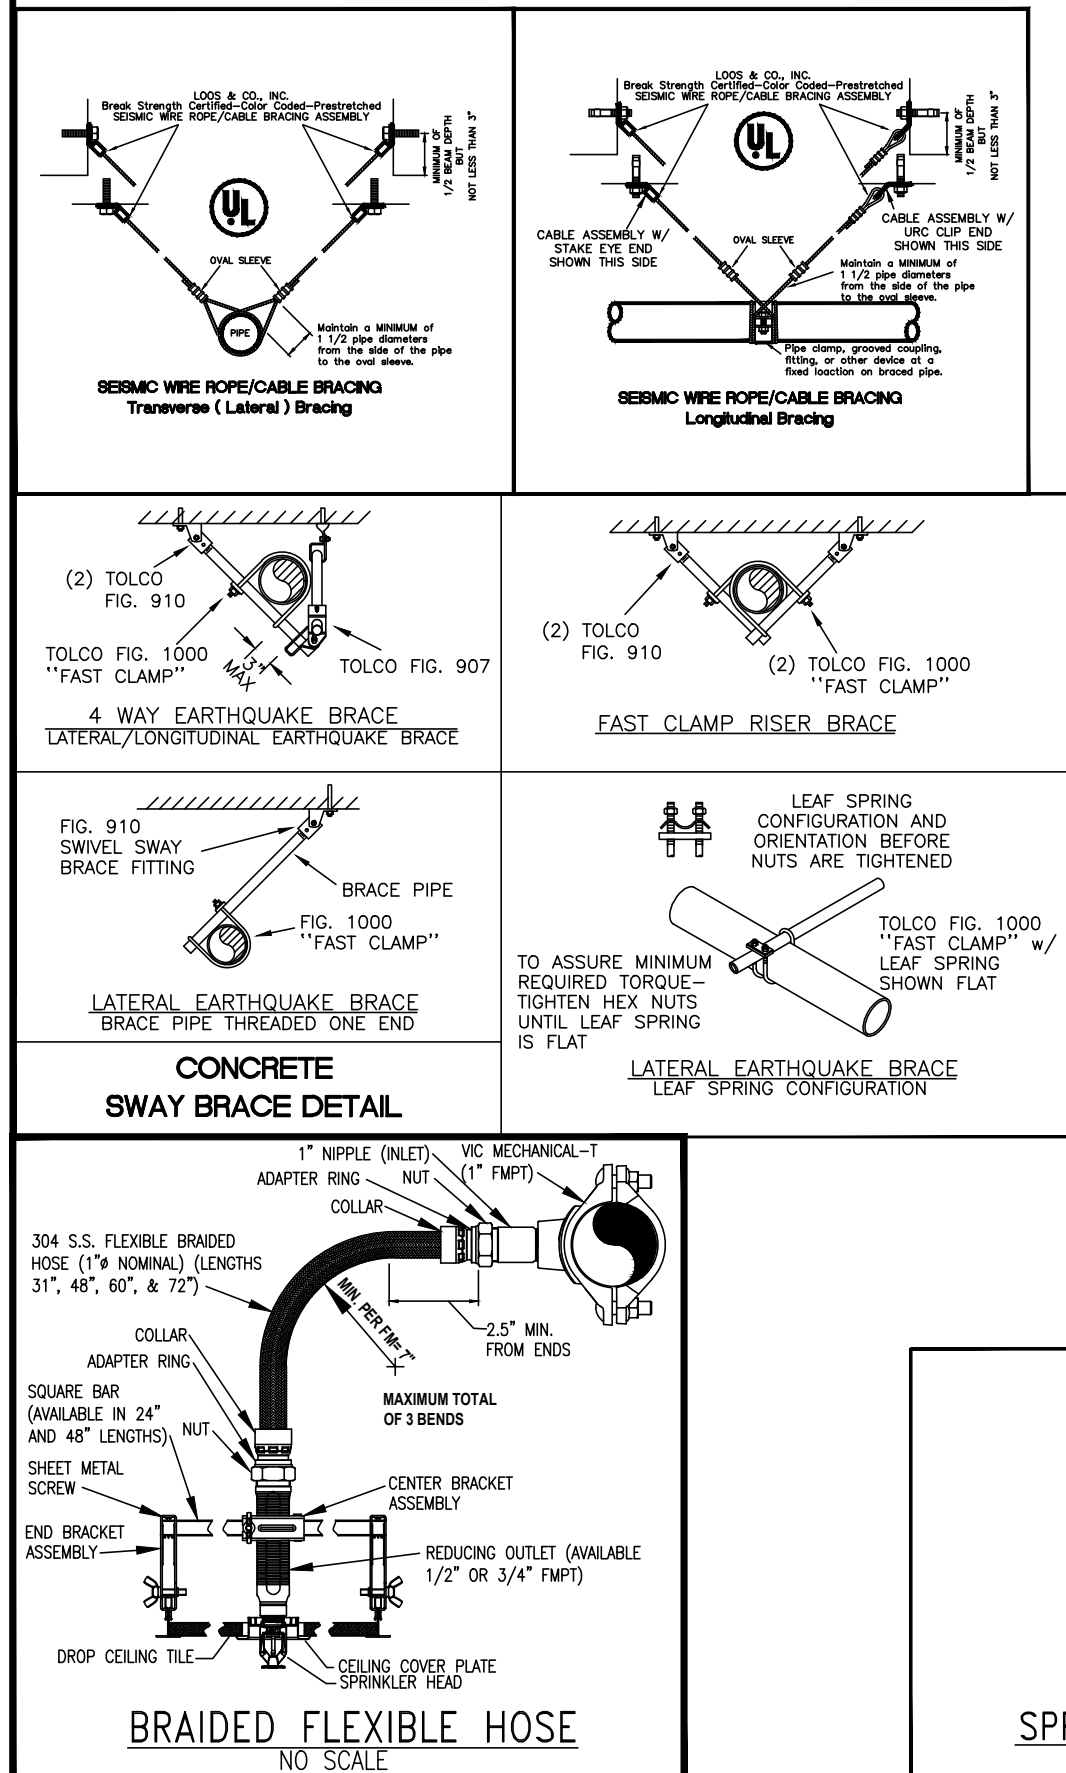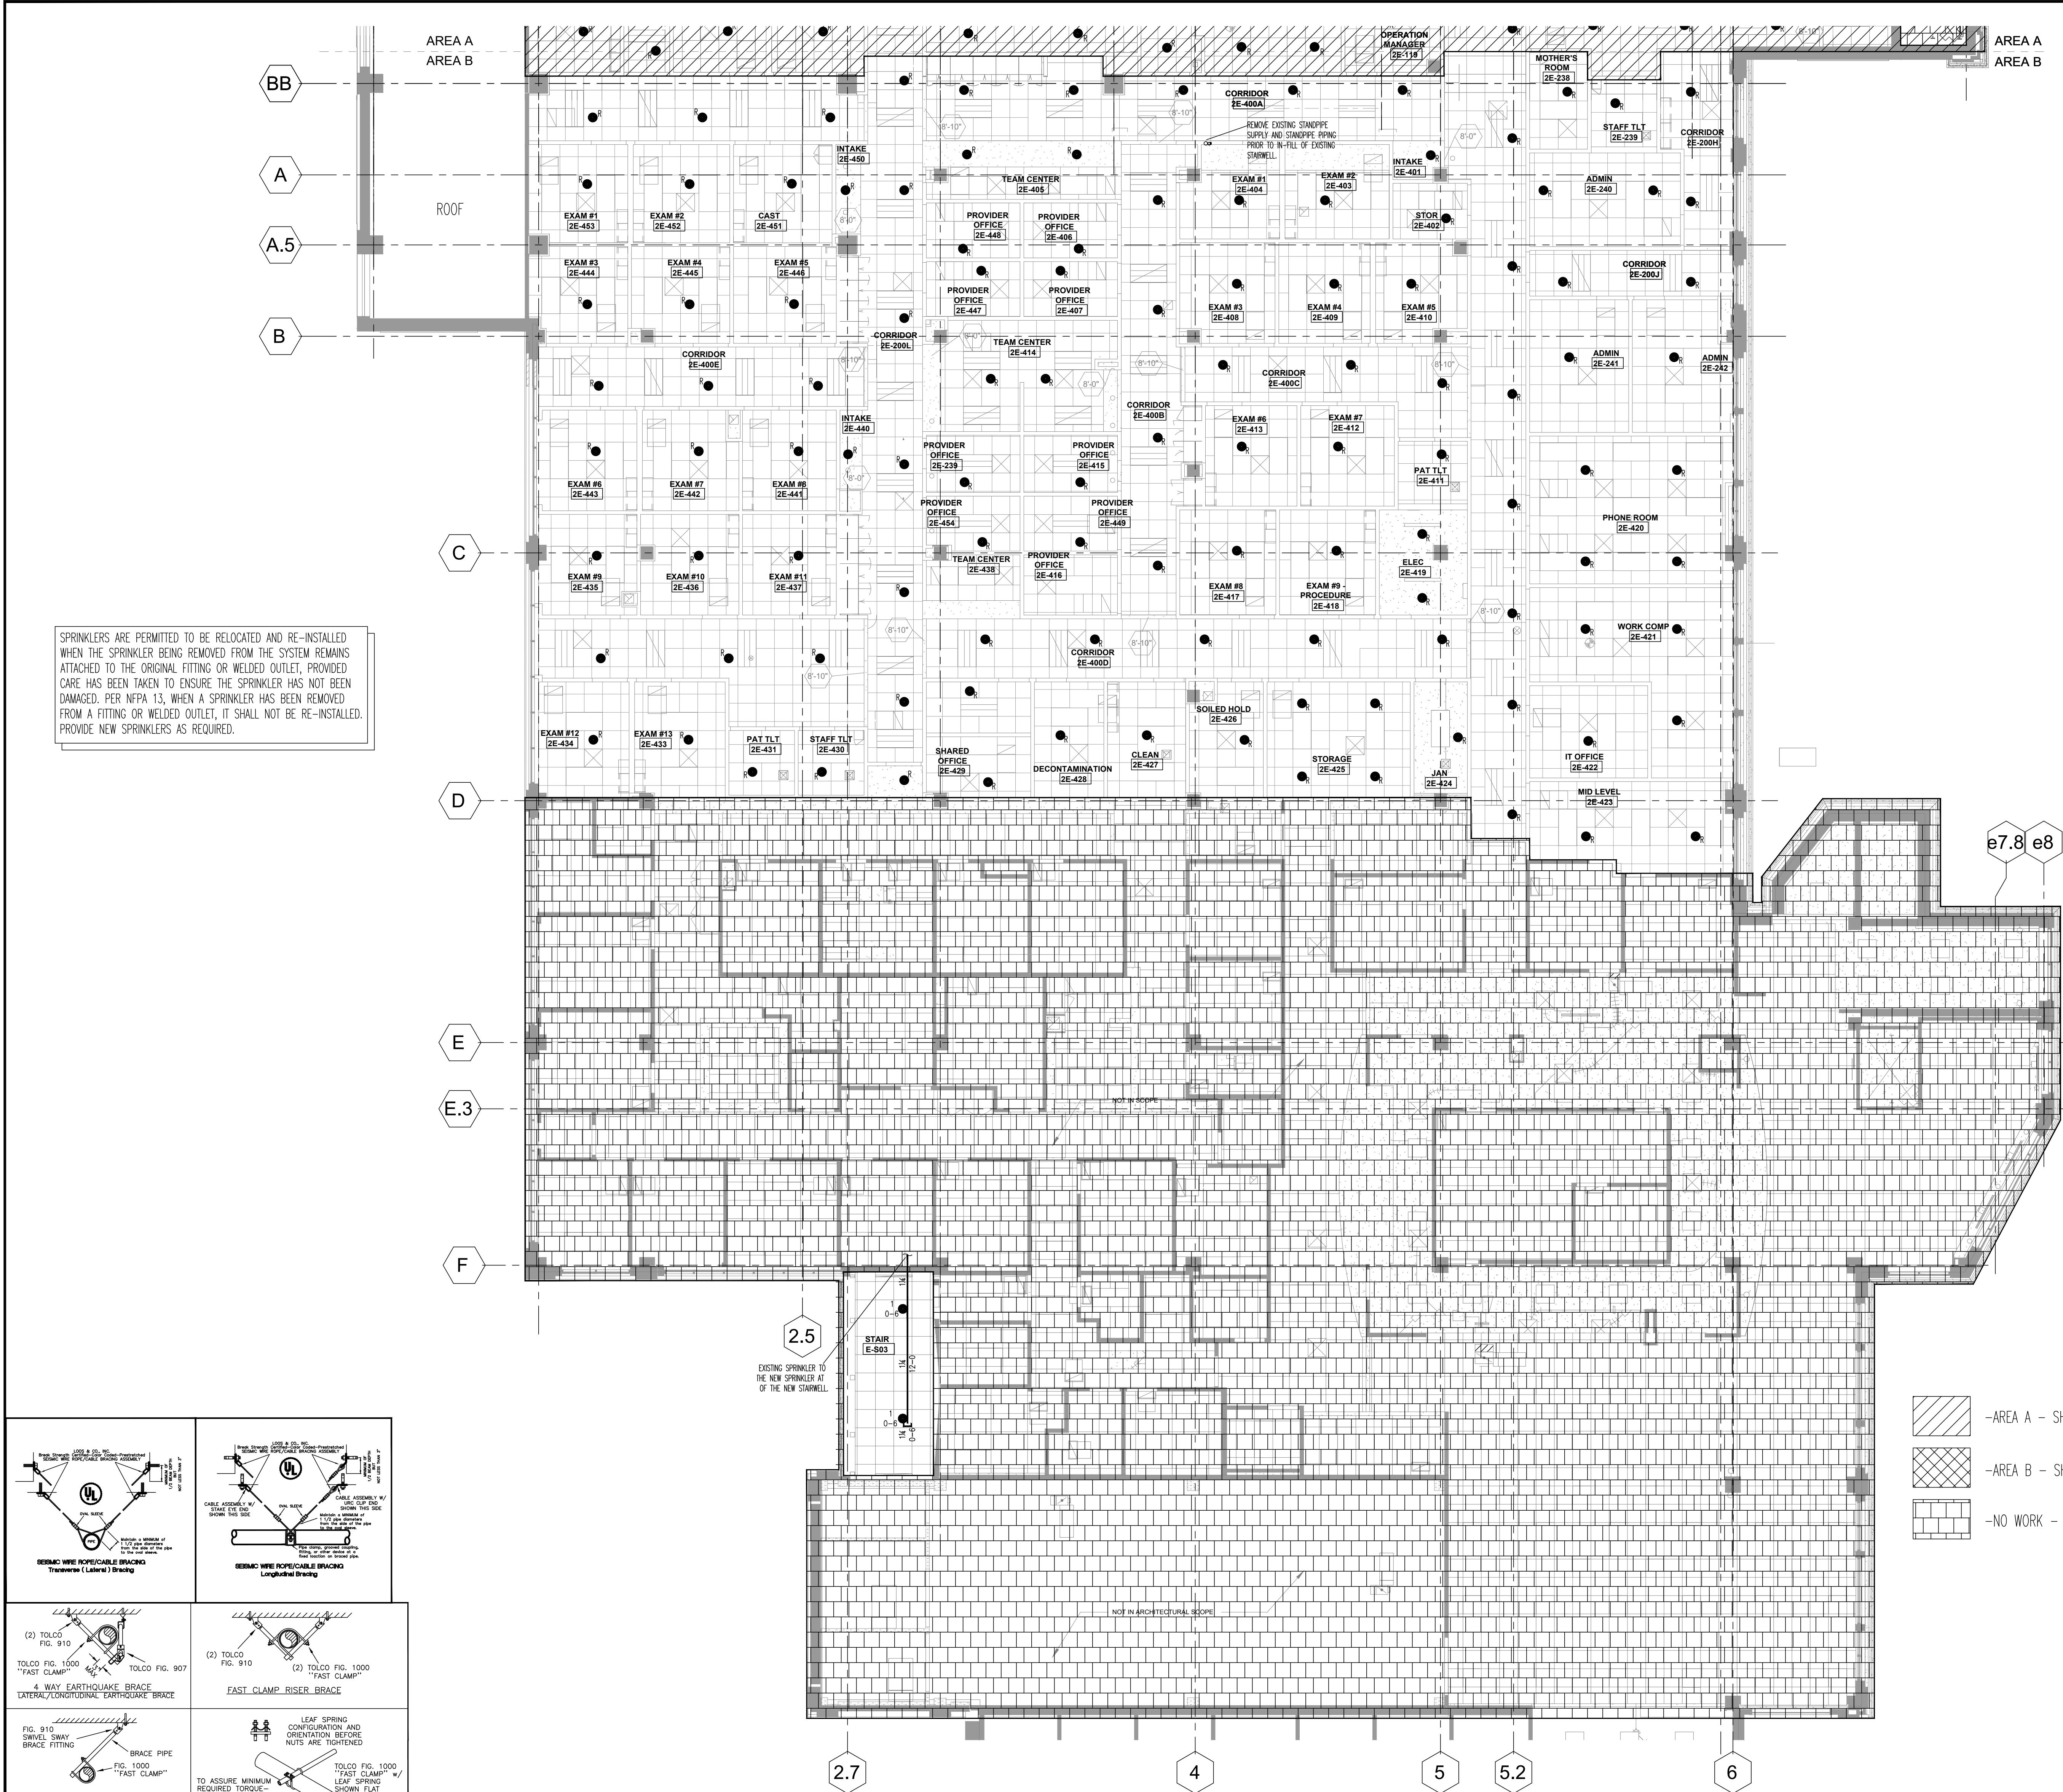

2nd FLOOR FIRE SPRINKLER PLAN - AREA B

- AREA A - SHEET FP3
- AREA B - SHEET FP4
- NO WORK - NOT IN CONTRACT

ALL SPRINKLER PIPING PASSING THROUGH FIRE RATED ASSEMBLIES SHALL BE FIREFSTOPPED BY OTHERS. FIRE STOPPING MATERIAL SHALL BE SUITABLE FOR THE PIPE MATERIAL IN USE AND THE ASSEMBLY PENETRATED.


SEALANTS USED FOR CPVC MATERIALS SHALL BE FBC SYSTEM COMPATIBLE.

SPRINKLER RELOCATION LEGEND	
SYMBOL	DESCRIPTION
	RELOCATED SPRINKLER FROM EXISTING OUTLET
	CHANGED EXISTING SPRINKLER FROM S.R. TO Q.R.
	ADDED SPRINKLER FROM EXISTING SPRINKLER SYSTEM
	NEW SPRINKLER BEING INSTALLED FROM NEW SYSTEM

LEGEND	
SYMBOL	DESCRIPTION
	EXISTING SPRINKLER TO REMAIN
	EXISTING RISER PIPE TO REMAIN
	FIRE SPRINKLER STANDPIPE
	POINT OF CONNECTION
	HANGER LOCATION
	PIPE END CAP

SPRINKLER LEGEND									
SYMBOL	SPRINKLER TYPE	SIN #	FINISH	TEMP.	ORIFICE	K-FACTOR	COUNT		
	VITACULIC Q.R. CONCEALED PENDENT	V5606	WHITE	155°	1/2"	5.6 K	116		
								TOTAL THIS SHEET	116
								TOTAL THIS JOB	1027

- PLAN NOTES:**
- ALL CEILING HEIGHTS TO BE 9'-0" ABOVE FINISHED FLOOR UNLESS NOTED OTHERWISE.
 - SPRINKLERS SHALL BE CENTERED IN THE NARROW DIMENSION OF CEILING TILES, AS SPECIFIED (211313-3.6.A).
 - ALL THREADED PIPING IS TO BE ALLIED "SCHEDULE 40" WITH THREADED CAST IRON FITTINGS.
 - ALL GROOVED PIPING IS TO BE SCH. 40 PIPE, ASTM A-795 WITH ROLLED GROOVED ENDS. ALL FITTINGS TO BE IRON GROOVED OR WELDED STEEL OUTLETS.
- DESIGN CRITERIA:**
- BUILDING CODE: SEE CODE SUMMARY
- OCCUPANCY: SEE CODE SUMMARY
- TYPE OF CONSTRUCTION: SEE CODE SUMMARY
- AREA OF CONSTRUCTION: SEE CODE SUMMARY
- PER NFPA 13, 2016 EDITION:
- SYSTEM TYPE: WET (EXISTING)
- CORRIDOR, PATIENT ROOMS, OFFICES, ETC..
- LIGHT HAZARD
- 0.10 GPM/S.F. FOR 1500 S.F.
- MAXIMUM 225 S.F. SPRINKLER SPACING
- 100 GPM HOSE ALLOWANCE
- MECHANICAL ROOMS, STORAGE ROOMS, ETC..
- ORDINARY HAZARD GROUP 1
- 0.20 GPM/S.F. FOR 1500 S.F.
- MAXIMUM 130 S.F. SPRINKLER SPACING
- 350 GPM HOSE ALLOWANCE
- FLOW TEST DATA:**
- DATE: 12-18-2023 / 11:15AM
- INFO FROM: CITY OF LEE'S SUMMIT
- STATID: 104 PSI
- RESIDUAL: 92 PSI
- FLOW: 2300 GPM
- LOCATION: 100 NE ST. LUKE'S BLVD.
- GENERAL NOTES:**
- ALL FITTINGS CONFORM TO SECTION 2-4 OF NFPA PAMPHLET 13.
- VALVES ON CONNECTIONS TO WATER SUPPLIES, SECTIONAL CONTROL VALVES AND OTHER VALVES IN SUPPLY LINES TO SPRINKLERS SHALL BE SUPERVISED OPEN BY AN APPROVED METHOD.
- IT IS THE OWNER'S RESPONSIBILITY TO PROVIDE ADEQUATE HEAD TO KEEP THE SPRINKLER SYSTEM FROM FREEZING.
- ALL ELECTRICAL WIRING OF ALARM BELLS, FLOW SWITCHES AND TAMPER SWITCHES (IF REQUIRED) TO BE DONE BY OTHERS.
- THE SPRINKLER SYSTEM TO BE INSTALLED IN ACCORDANCE WITH NFPA 13.
- HANGERS TO BE SPACED TO MEET NFPA REQUIREMENTS
- PER NFPA 13, SECTION 8.6.3.2.4, WITHIN SMALL ROOMS AS DEFINED IN SECTION 3.3.20, SPRINKLERS SHALL BE PERMITTED TO BE LOCATED NOT MORE THAN 9 FT. FROM ANY SINGLE WALL, AND SPRINKLER SPACING LIMITATIONS OF SECTION 8.6.3 AND AREA LIMITATIONS OF TABLE 8.6.2.2.1(a) SHALL NOT BE EXCEEDED. JFS MAY MODIFY HEADS SHOWN ON THIS DRAWING TO COMPLY WITH THIS RULE.
- ± = CENTER LINE OF PIPE BELOW TOP OF STEEL
- EL = CENTER LINE OF PIPE ABOVE FINISHED FLOOR
- CONSTRUCTION:**
- CONCRETE SLABS, CONCRETE BEAMS AND TEES
- CODE NOTE:**
- 8.6.5.2.2.1
- IN LIGHT HAZARD OCCUPANCIES, PRIVACY CURTAINS SHALL NOT BE CONSIDERED OBSTRUCTIONS WHERE ALL OF THE FOLLOWING AREA MET:
- THE CURTAINS ARE SUPPORTED BY FABRIC MESH OR CEILING TRACK.
 - OPENINGS IN THE MESH ARE EQUAL TO 70 PERCENT OR GREATER.
 - THE MESH EXTENDS A MINIMUM OF 22 INCHES DOWN FROM CEILING.
- CODE SUMMARY:**
- Project Construction Purpose:** New 3 story addition and partial renovation of existing ASC Building
- Project Address:** Saint Luke's East Hospital
120 NE Saint Luke's Blvd
Lee's Summit, MO 64063
- Code Information:**
2016 International Building Code
2018 International Plumbing Code
2015 International Mechanical Code
2017 National Electrical Code (NFPA 70)
2018 International Fire Code
2012 Life Safety Code (NFPA 101 Chapter 20)
2009 ICC/ANSI A117.1 as amended and adopted by the City of Lee's Summit
2010 ADA Standards for Accessible Design / Americans with Disabilities Act of 1990
- State of Missouri Dept. of Health & Environment references the following codes:**
2012 NFPA 101 Life Safety Code (LSC)
2018 FGI Guidelines for Design & Construction of Hospitals & Outpatient Facilities 1979 19-CSR-30
Note: If code requirements overlap, the most stringent shall apply.
- Owner Information:**
Saint Luke's East Hospital
120 NE Saint Luke's Blvd
Lee's Summit, MO 64063
- Designer Information:**
ACI Build Architects
1710 Wyandotte St.
Kansas City, MO 64108
Phone: (816) 763-9600
- Local Authority:**
Responding Fire Service: Lee's Summit Fire Department
Local Building Inspection: Lee's Summit, MO - Codes Administration Department
- Type of Construction:** I-A
- Area of Renovation and Addition**
- | | |
|----------------------------|---------------|
| 1st floor addition | 16,000+/- SF |
| 1st floor renovation | 23,601+/- SF |
| 2nd floor addition | 16,700+/- SF |
| 2nd floor renovation | 28,098+/- SF |
| 3rd floor addition | 27,514+/- SF |
| Total addition: | 62,214+/- SF |
| Total renovation: | 51,699+/- SF |
| Total of new construction: | 113,913+/- SF |
- Occupancy Group:** B - Ambulatory Healthcare
Max Travel Distance: 200' (NFPA 101 20.2.6.2.1)
- Occupant Load:** 150SP/OCC (table 1004.5)
- | | |
|-----------------------------|-----|
| 1st floor: 41,601/150 = | 278 |
| 2nd floor: 44,798/150 = | 299 |
| 3rd floor: 27,514/150 = | 184 |
| Total Number of Occupants = | 761 |
- Required Fire Resistance Ratings (in hours)**
Per NFPA 101 A.8.2.1.2:
- | | |
|----------------------------|----------|
| Exterior Bearing Walls | 3 HR |
| Interior Bearing Walls | 3 HR |
| Primary Structural Frame | 3 HR |
| Floor Construction | 2 HR |
| Roof Construction | 1 1/2 HR |
| Interior Non-bearing Walls | 0 HR |
| Shaft Enclosure | 2 HR |
| Stair Enclosure | 2 HR |
- Fire Separation: (table 508.4)**
2HR separation between tenants B-2
1HR separation between tenants B-3

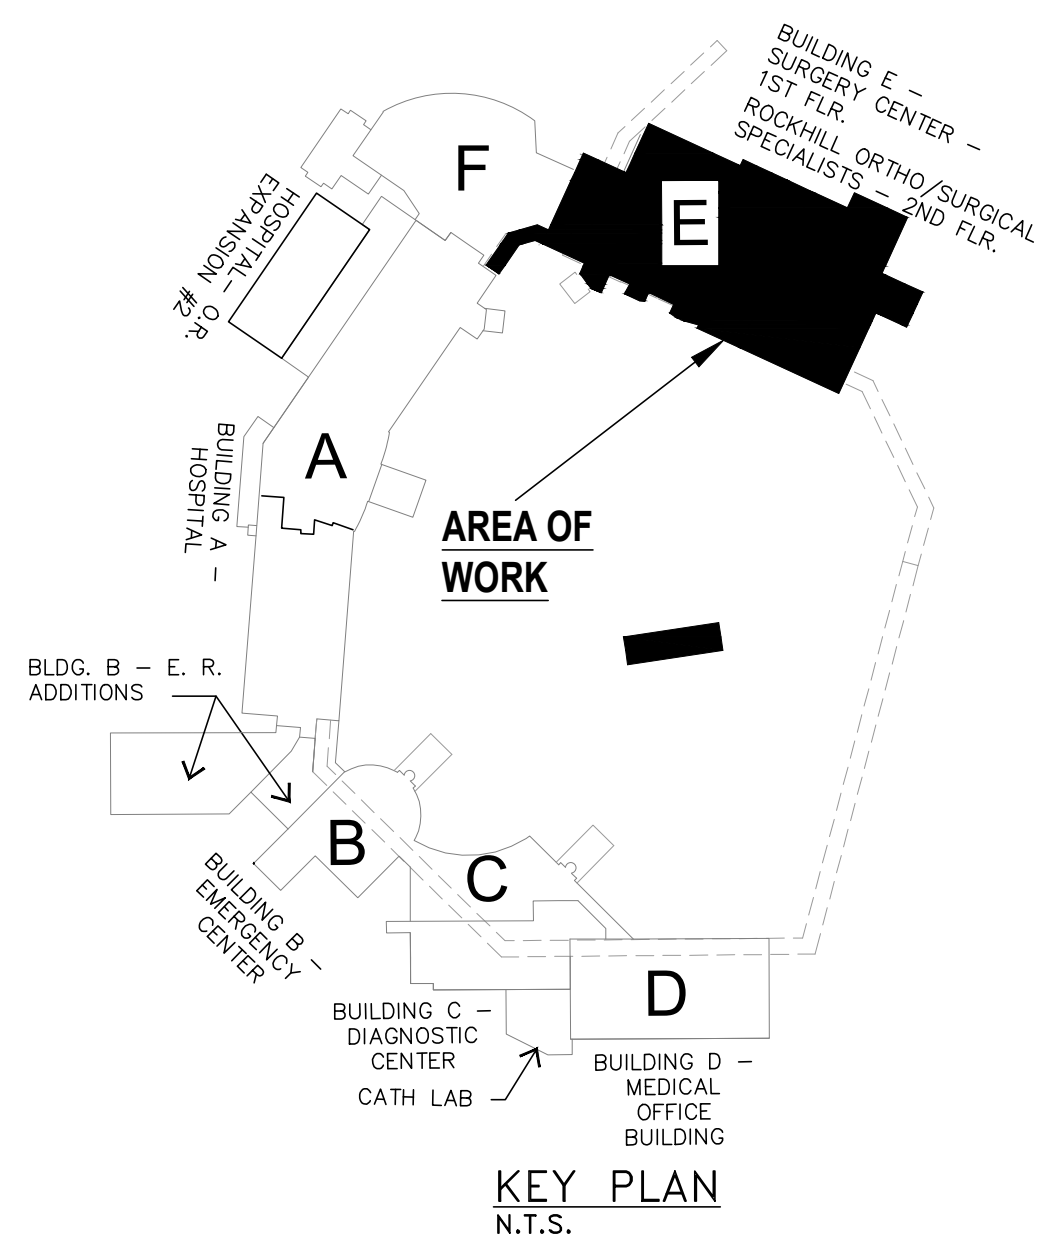

JAYHAWK FIRE SPRINKLER CO., INC.
1201 E. 12TH ST., SUITE 100
Olathe, Kansas 66061
PHONE: (816) 763-9600
FAX: (816) 777-0036
COURTESY: JAYHAWK


MAJESTY CONSTRUCTION
7850 SAINT LUKE DRIVE
OVERLAND PARK, KANSAS 66204

SAINT LUKE'S HEALTH SYSTEM
ASC EXPANSION

100 NE Saint Luke's Blvd.
Lee's Summit, MO 64066

WALTER A. WARREN
REGISTERED PROFESSIONAL ENGINEER
NUMBER E-24557
03/09/2024
Warren KTD, LLC

PROJECT NO. **20543M**
DRAWN BY: **TJA** CHECKED BY: **DO**
PROJECT MANAGER: **TS**
APPROVAL
DATE: **01/15/2024** REVISION DATE: **02/28/2024**
DRAWING NUMBER
FP-4
FIRE PROTECTION
HEAD RELOCATION
2ND FLR. - AREA B
SHEET: **4 OF 6**



PLAN NOTES:

- ALL CEILING HEIGHTS TO BE 9'-0" ABOVE FINISHED FLOOR UNLESS NOTED OTHERWISE.
- SPRINKLERS SHALL BE CENTERED IN THE NARROW DIMENSION OF CEILING TILES, AS SPECIFIED (21310-3.6.A).
- ALL THREADED PIPING IS TO BE ALLED "SCHEDULE 40" WITH THREADED CAST IRON FITTINGS.
- ALL GROOVED PIPING IS TO BE SCH. 40 PIPE, ASTM A-795 WITH ROLLED GROOVED ENDS. ALL FITTINGS TO BE IRON GROOVED OR WELDED STEEL OUTLETS.

GENERAL NOTES:

ALL FITTINGS CONFORM TO SECTION 2-4 OF NFPA HANDBOOK 13.

VALVES ON CONNECTIONS TO WATER SUPPLIES, SECTIONAL CONTROL VALVES AND OTHER VALVES IN SUPPLY PIPES TO SPRINKLERS SHALL BE SUPERVISED BY AN APPROVED METHOD.

IT IS THE OWNERS RESPONSIBILITY TO PROVIDE ADEQUATE HEAT TO KEEP THE SPRINKLER SYSTEM FROM FREEZING.

THE SPRINKLER SYSTEM TO BE INSTALLED IN ACCORDANCE WITH NFPA 13.

HANGERS TO BE SPACED TO MEET NFPA REQUIREMENTS.

PER NFPA 13, SECTION 8.6.3.2.4, WITHIN SMALL ROOMS AS DEFINED IN SECTION 3.3.2.3, SPRINKLERS SHALL BE PERMITTED TO BE LOCATED NOT MORE THAN 9 FT. FROM ANY SINGLE WALL, AND SPRINKLER SPACING LIMITATIONS OF SECTION 8.6.3 AND AREA LIMITATIONS OF TABLE 8.6.2.2.1(a) SHALL NOT BE EXCEEDED. JFS MAY MODIFY HEADS SHOWN ON THIS DRAWING TO COMPLY WITH THIS RULE.

EL = CENTER LINE OF PIPE BELOW TOP OF STEEL

EL = CENTER LINE OF PIPE ABOVE FINISHED FLOOR

CONSTRUCTION:

CONCRETE SLAB, CONCRETE BEAMS AND TEES

CODE NOTE:

8.6.5.2.2.1
IN LIGHT HAZARD OCCUPANCIES, PRIVACY CURTAINS SHALL NOT BE CONSIDERED OBSTRUCTIONS WHERE ALL OF THE FOLLOWING AREA MET:
(1) THE CURTAINS ARE SUPPORTED BY FABRIC MESH ON CEILING TRACK.
(2) OPENINGS IN THE MESH ARE EQUAL TO 70 PERCENT OR GREATER.
(3) THE MESH EXTENDS A MINIMUM OF 22 INCHES DOWN FROM CEILING.

CODE SUMMARY:

Project Construction Purpose: New 3 story addition and partial renovation of existing ASC Building.

Project Address:
Saint Luke's East Hospital
120 NE Saint Luke's Blvd
Lee's Summit, MO 64063

Code Information:
2018 International Building Code
2018 International Plumbing Code
2018 International Mechanical Code
2017 National Electrical Code (NFPA 70)
2018 International Fire Code
2012 Life Safety Code (NFPA 101 Chapter 20)
2009 ICC/ANSI A117.1 as amended and adopted by the City of Lee's Summit
2010 ADA Standards for Accessible Design / Americans with Disabilities Act of 1990

State of Missouri Dept. of Health & Environment references the following codes:
2012 NFPA 101 Life Safety Code (LSC)
2018 FCI Guidelines for Design & Construction of Hospitals & Outpatient Facilities
1979 19-CSR-30
Note: If code requirements overlap, the most stringent shall apply.

Owner Information:
Saint Luke's East Hospital
120 NE Saint Luke's Blvd
Lee's Summit, MO 64063

Designer Information:
ACI Global Architects
1710 Wyandotte St.
Kansas City, MO 64108
Phone: (816) 763-9000

Local Authority:
Responding Fire Service: Lee's Summit Fire Department
Local Building Inspection: Lee's Summit, MO-Codes Administration Department

Type of Construction: I-A

Area of Renovation and Addition

Area	1st floor addition	2nd floor renovation	3rd floor renovation	3rd floor addition	Total addition	Total renovation	Total of new construction
SF	18,000+	23,801+	16,700+	28,089+	62,214+	51,889+	113,914+

Occupancy Group: B - Ambulatory Healthcare
Max Travel Distance: 200' (NFPA 101 20.2.6.2.1)

Occupant Load: 1505/IOCC (table 1004.5)

Floor	1st floor	2nd floor	3rd floor	Total
Occupant Load	41,601/150 = 278	44,758/150 = 299	27,514/150 = 184	761

Required Fire Resistance Ratings (in hours)
Per NFPA 101 A.5.2.1.2:

Component	Rating
Exterior Bearing Walls	3 HR
Interior Bearing Walls	3 HR
Primary Structural Frame	3 HR
Floor Construction	2 HR
Roof Construction	1 1/2 HR
Interior Non-bearing Walls	0 HR
Shaft Enclosure	2 HR
Stair Enclosure	2 HR

Fire Separation: (table 508.4)
2 HR separation between tenants I-B
1 HR separation between tenants B-B

Saint Luke's East
Lee's Summit

SAINT LUKE'S HEALTH SYSTEM

ASC EXPANSION

100 NE Saint Luke's Blvd.
Lee's Summit, MO 64066

SEAL

WALTER A. WARREN

NUMBER E-24557

03/09/2024

Warren KTD, LLC

PROJECT NO. 20543M

DESIGN BY: TJA

CHECKED BY: DO

PROJECT MANAGER: TS

APPROVAL

DATE: 01/15/2024

DATE: 02/28/2024












FP-5

FIRE PROTECTION

NEW ADDITION

3RD FLOOR AREA

5 OF 6

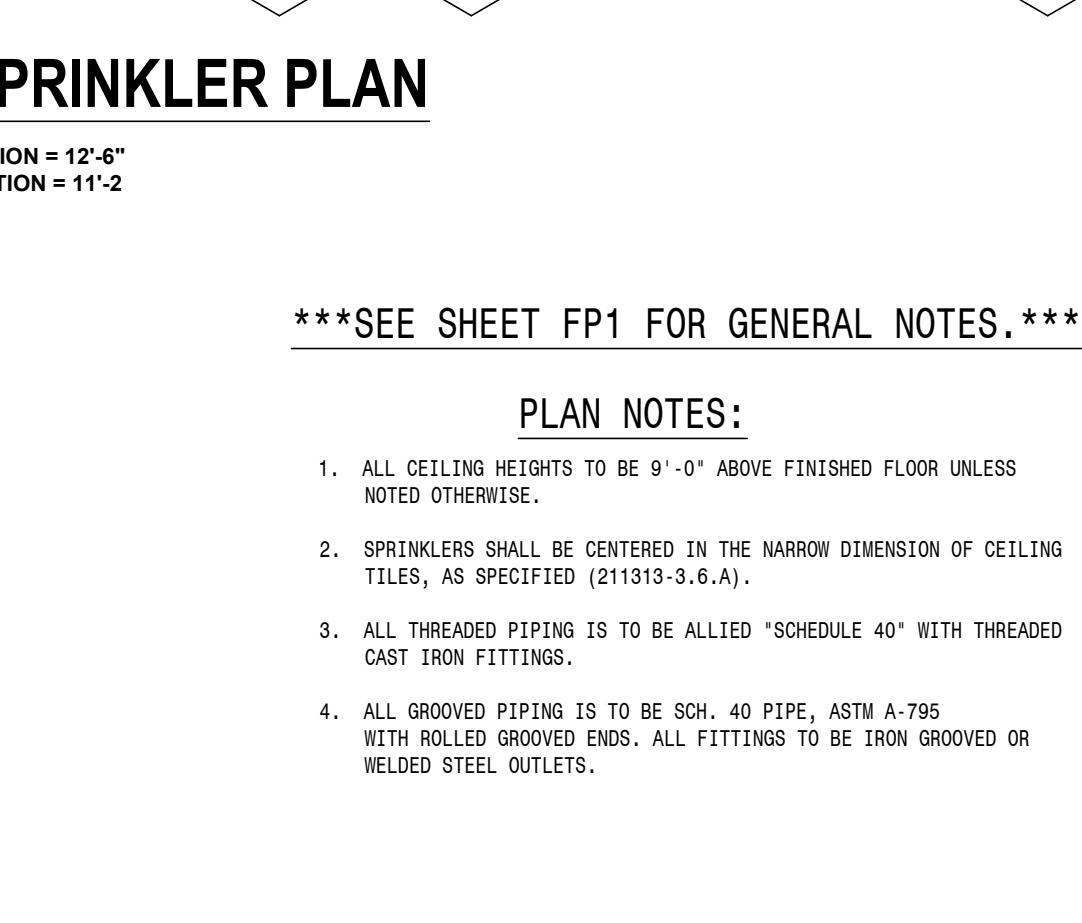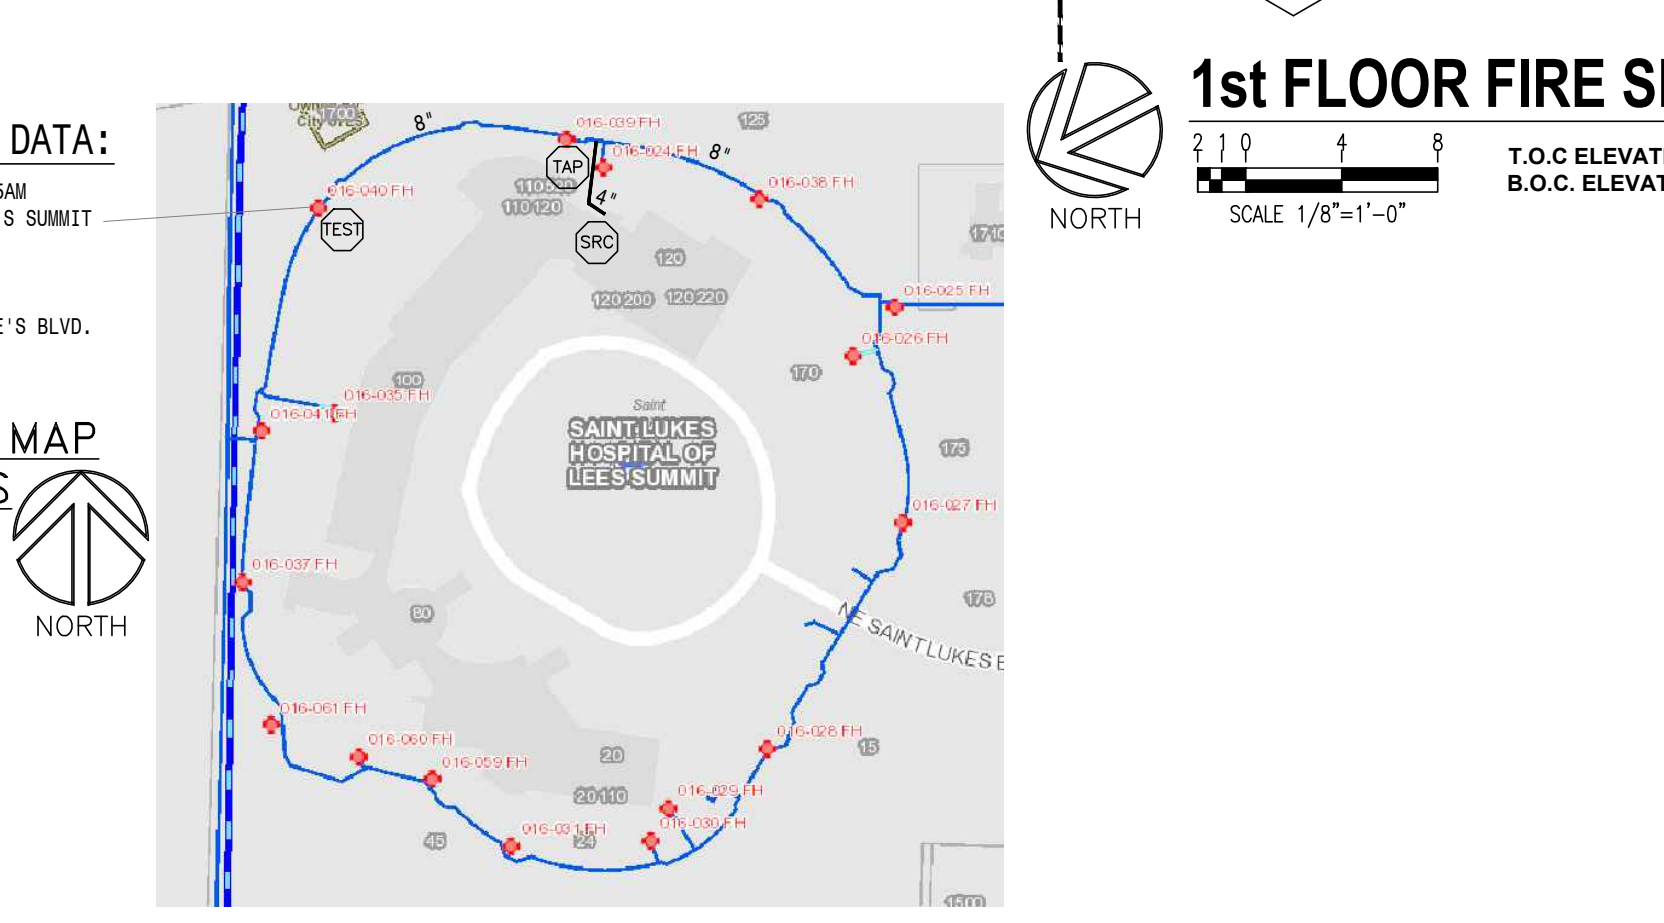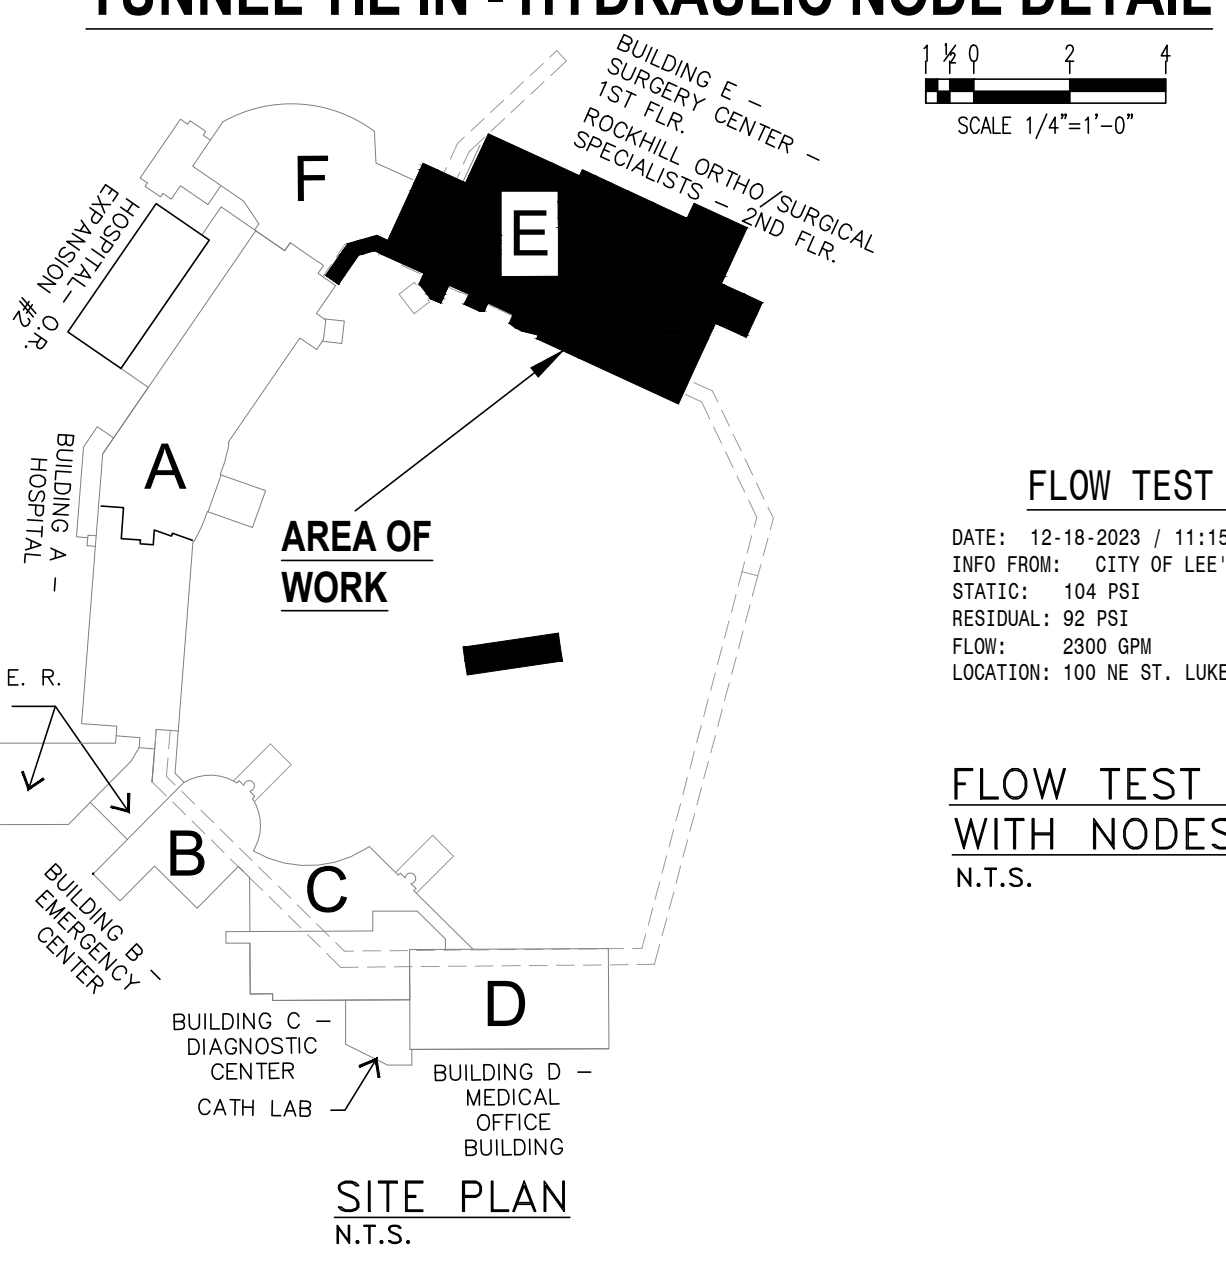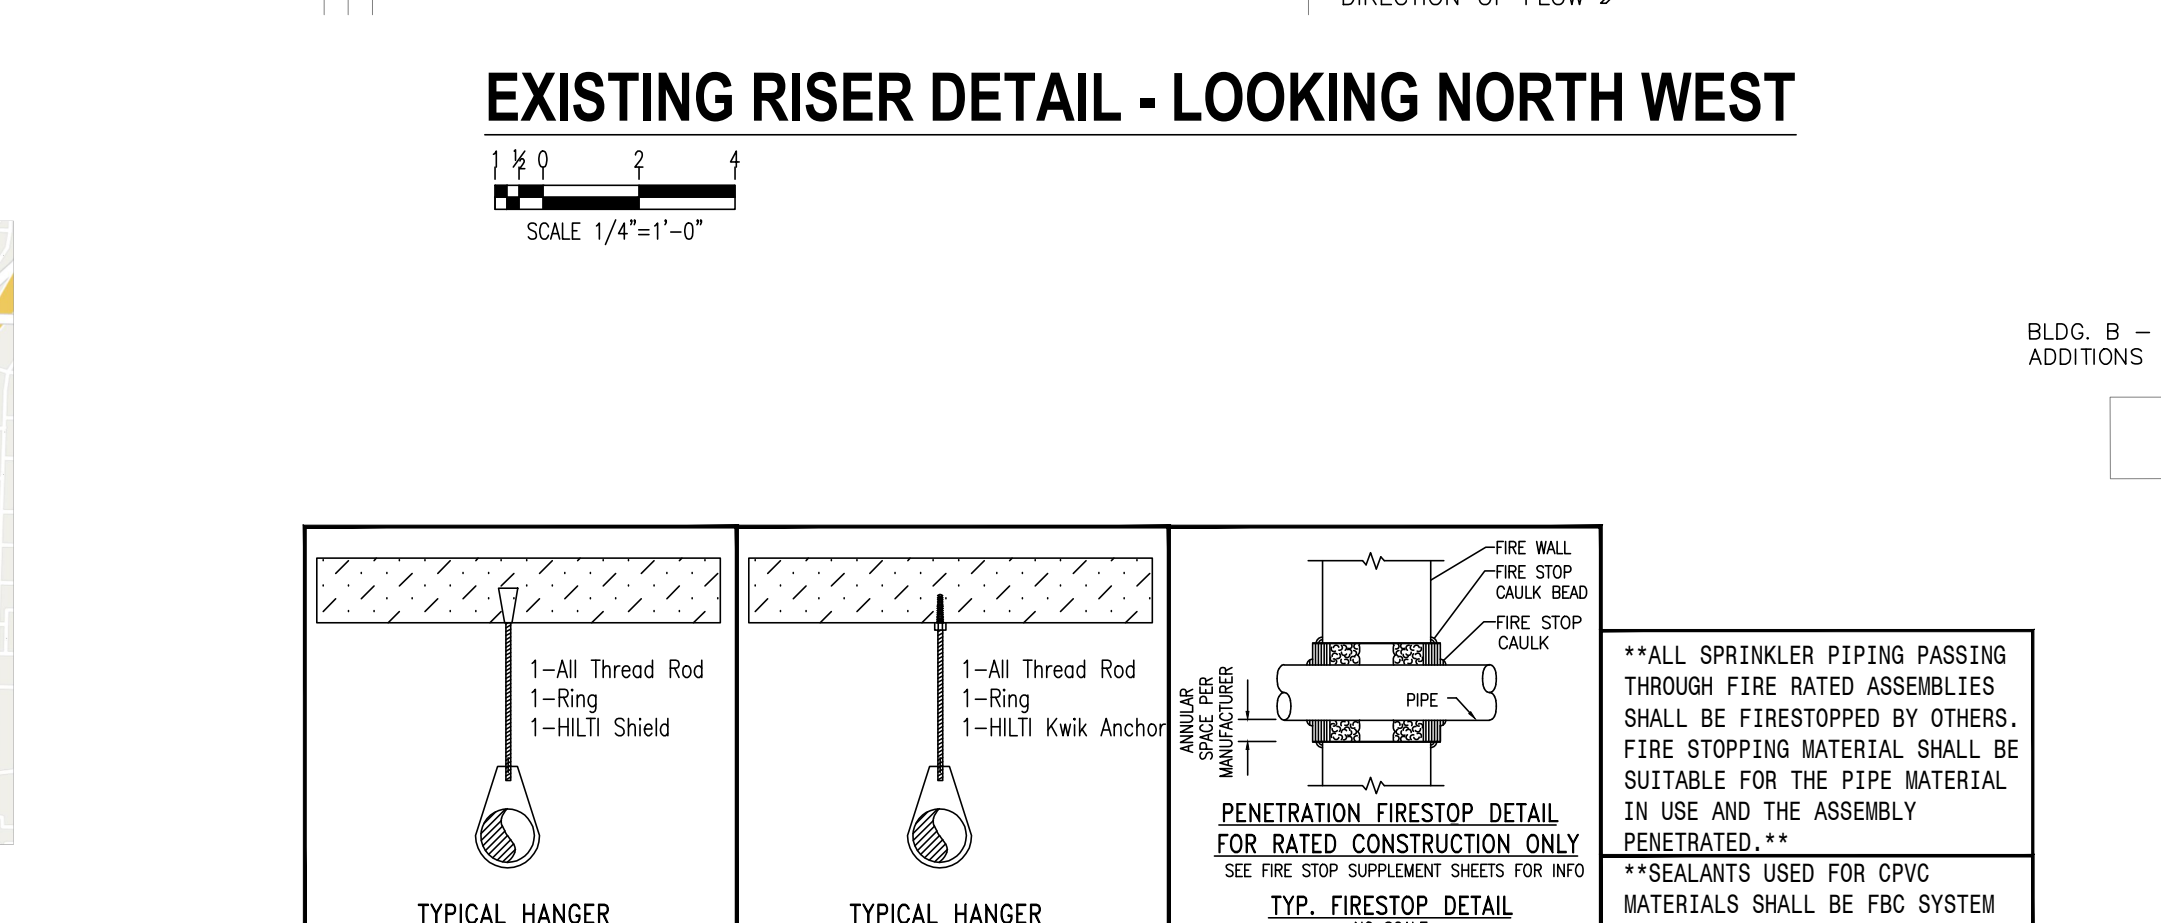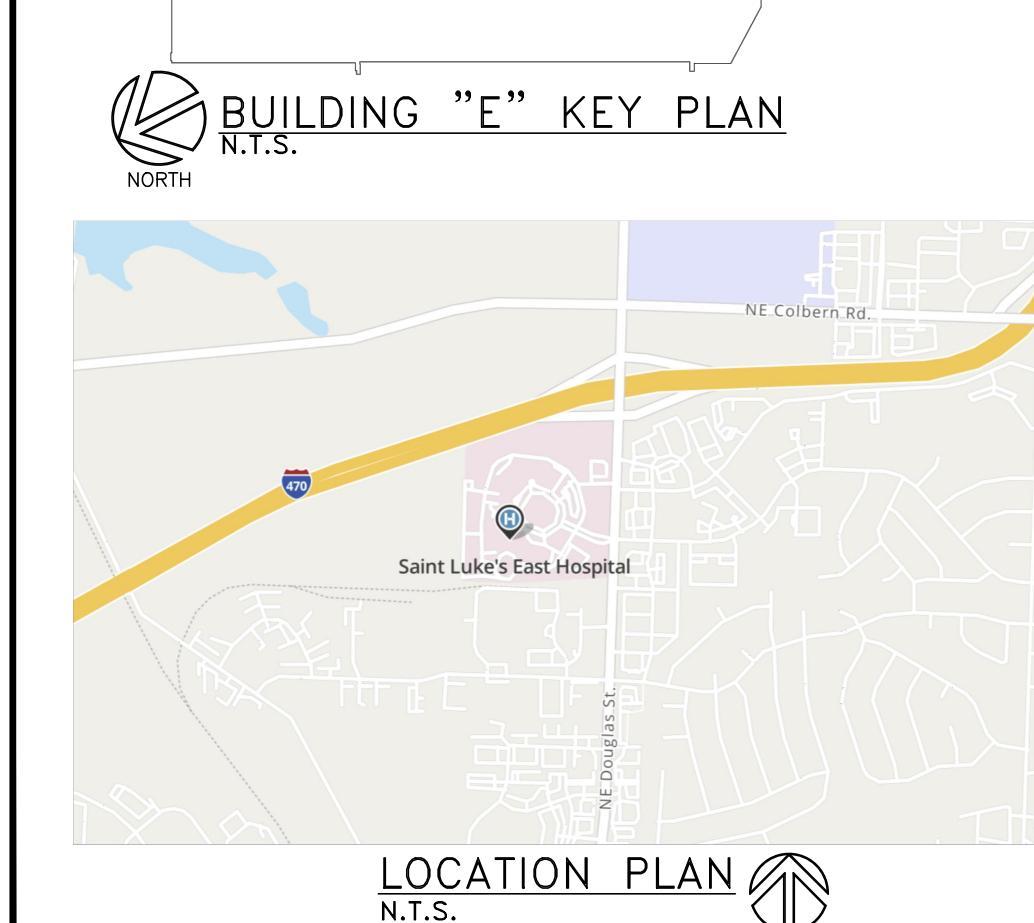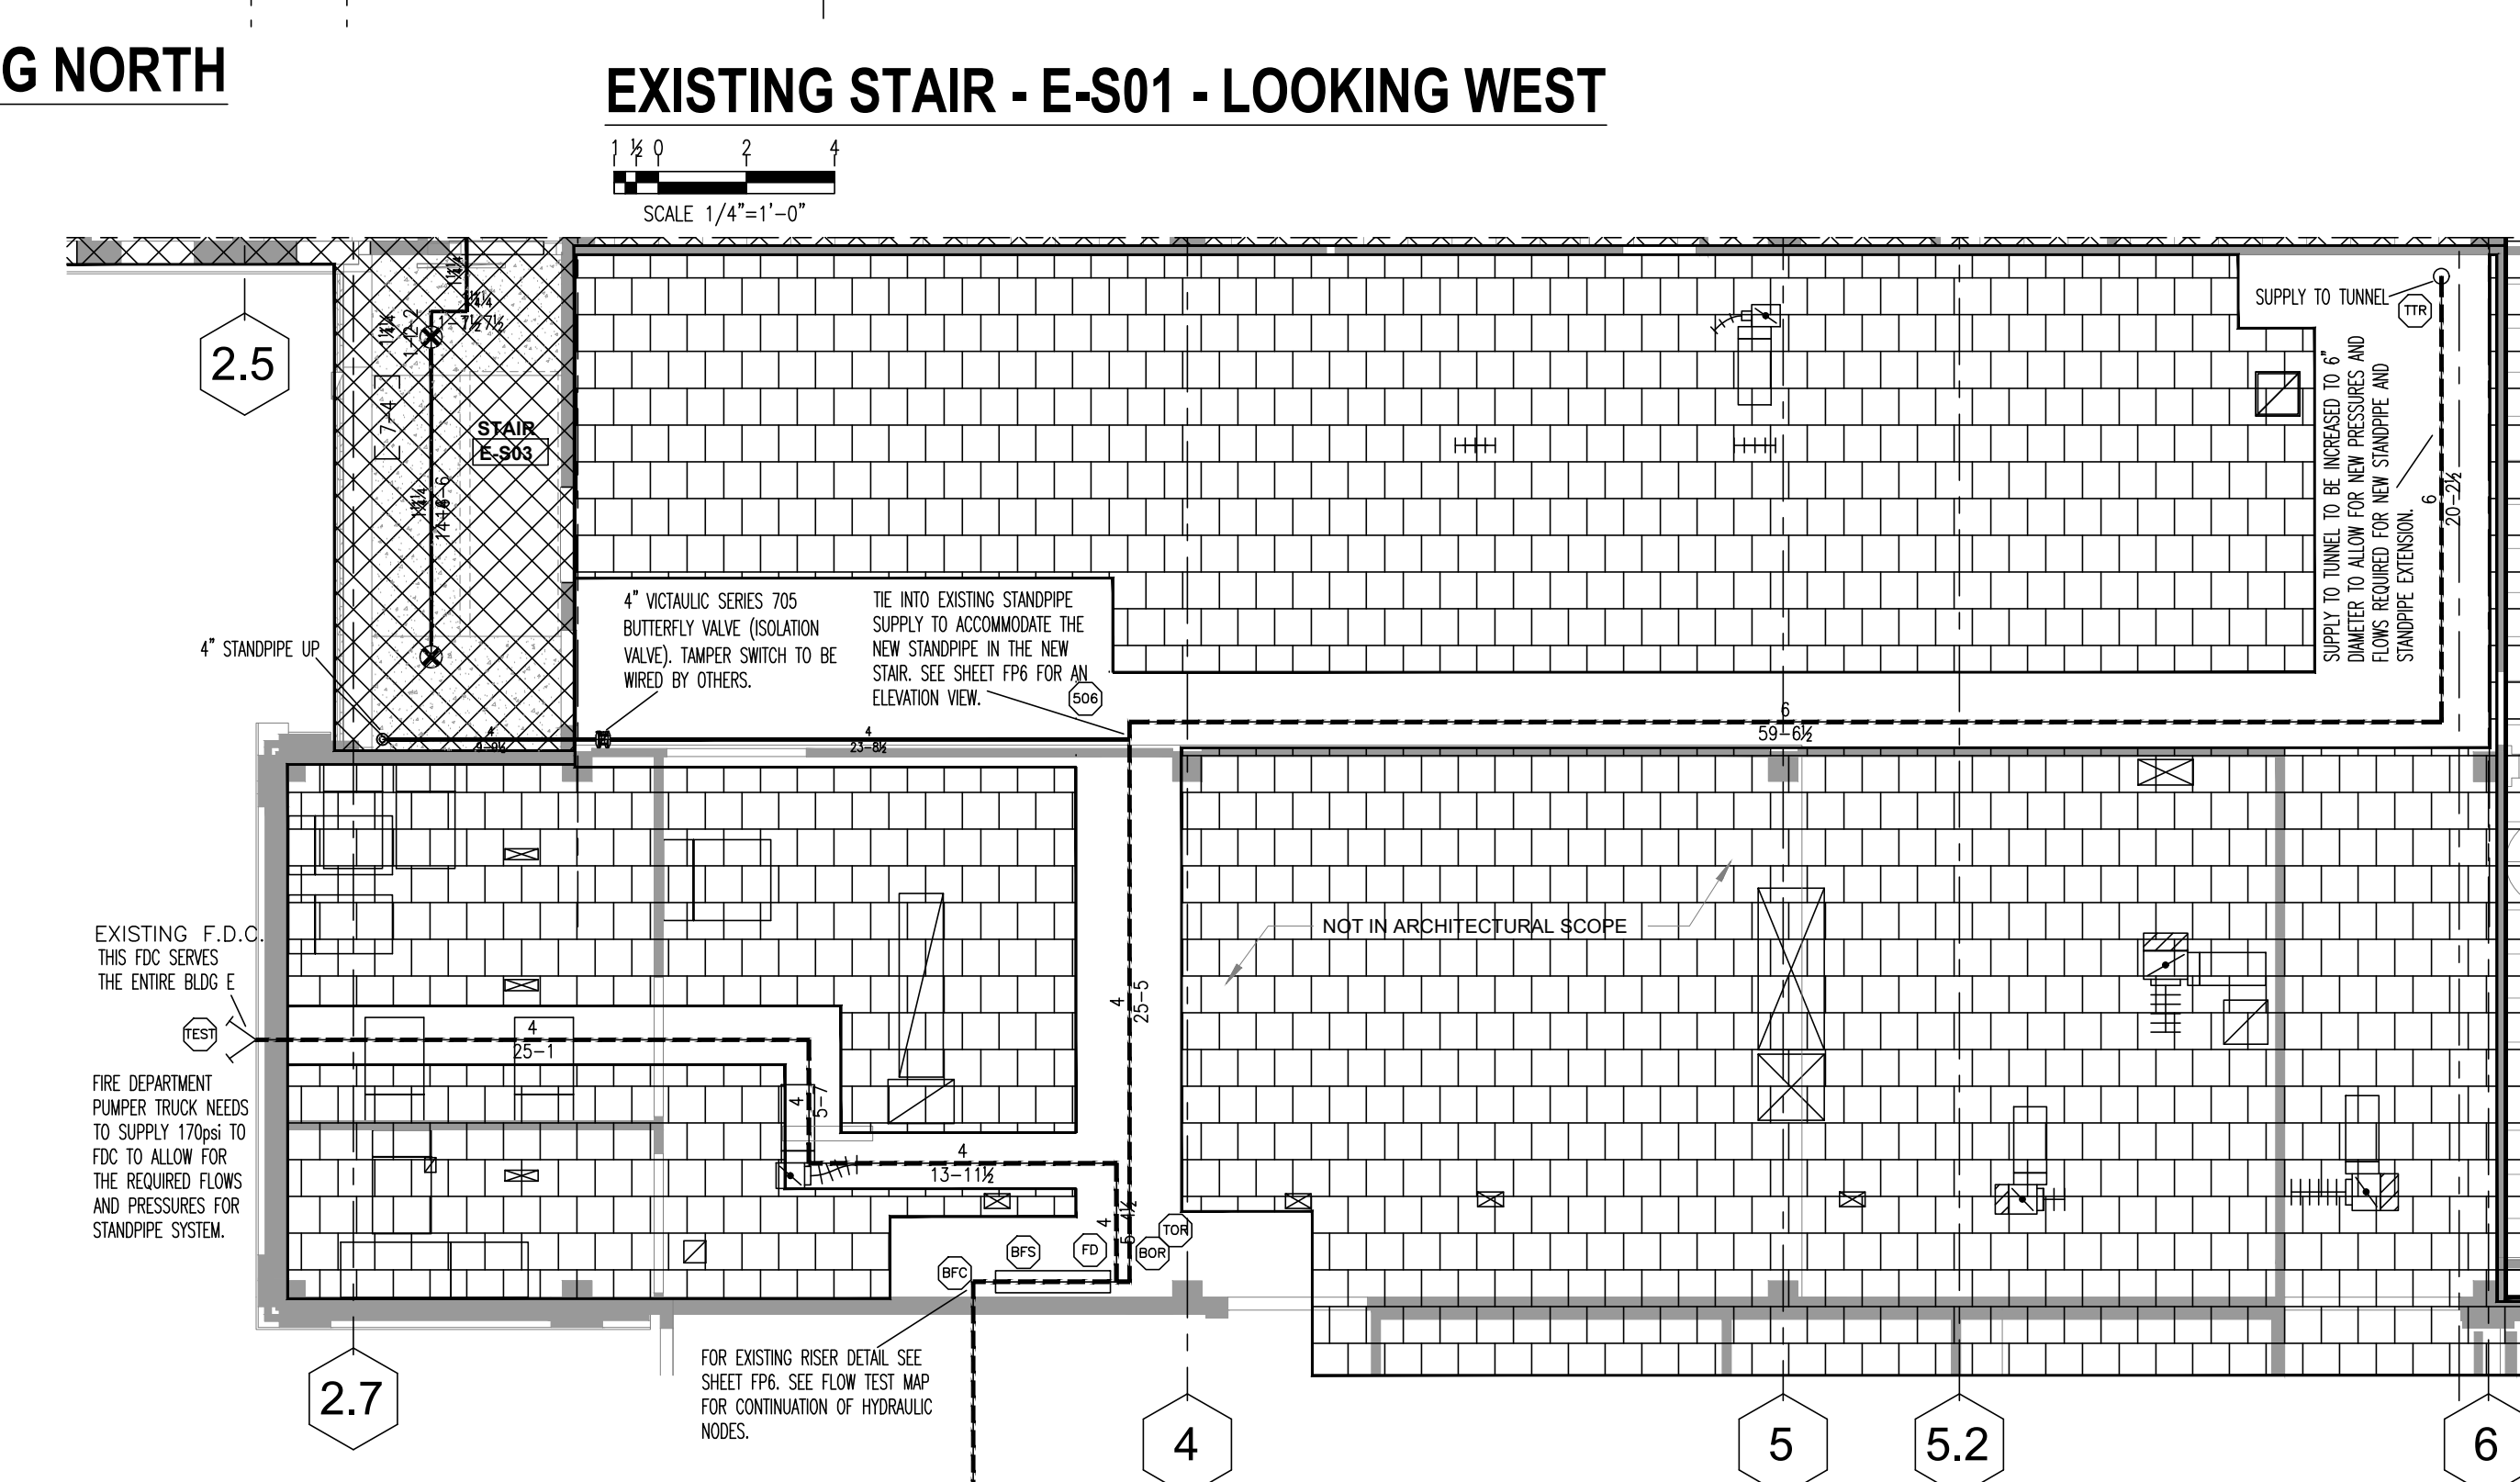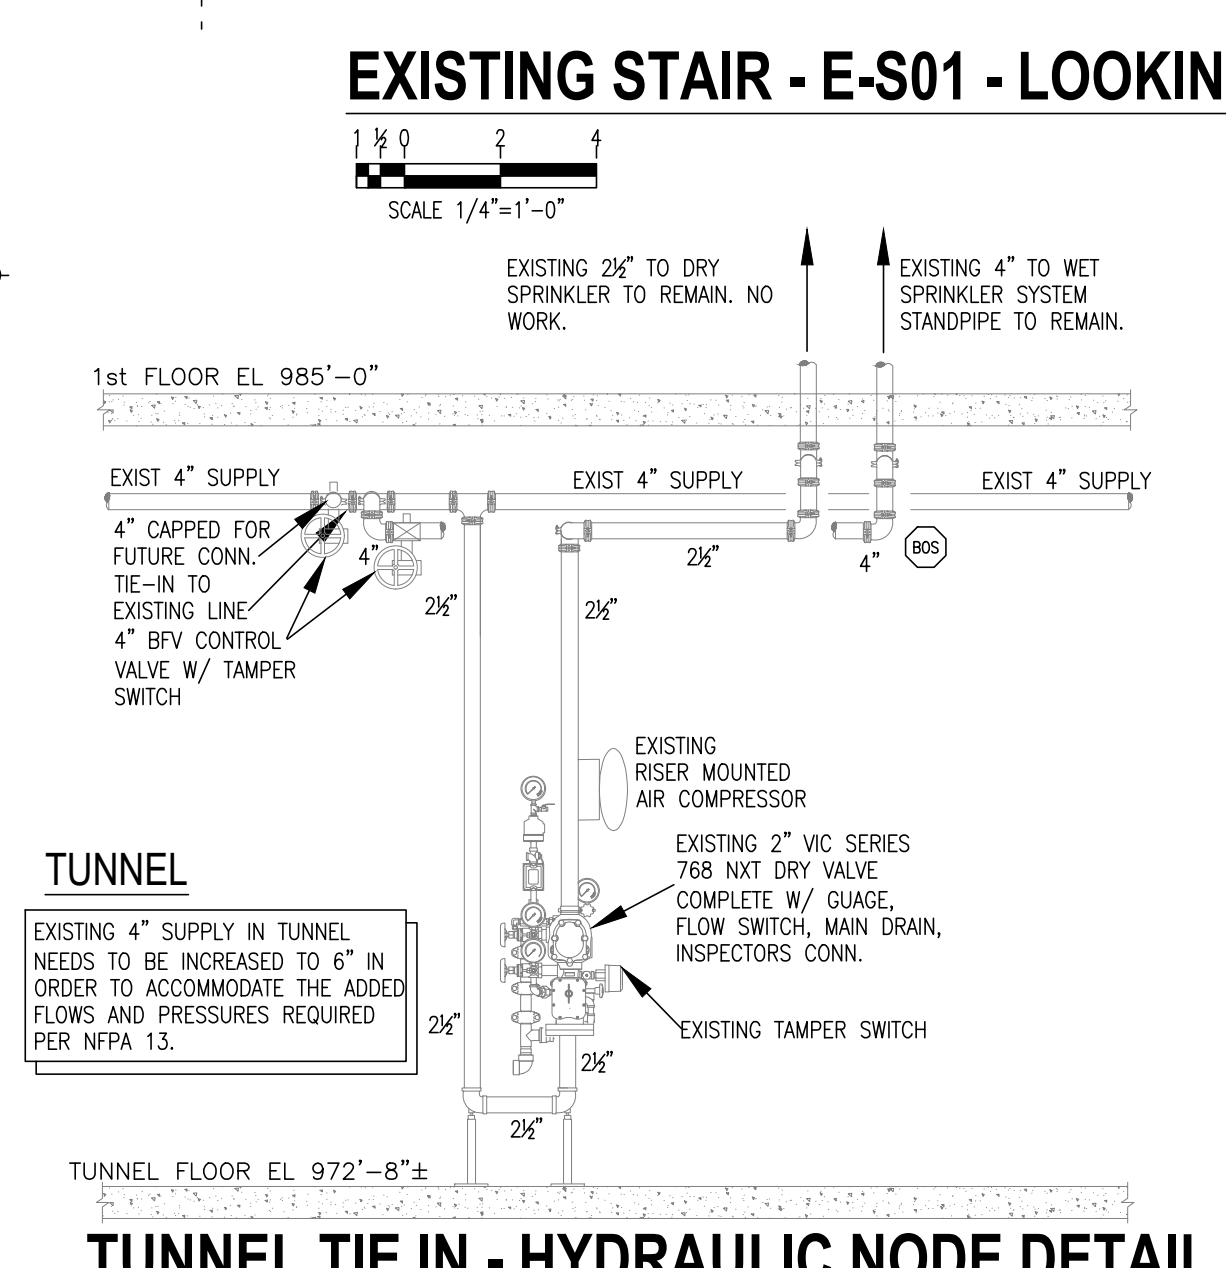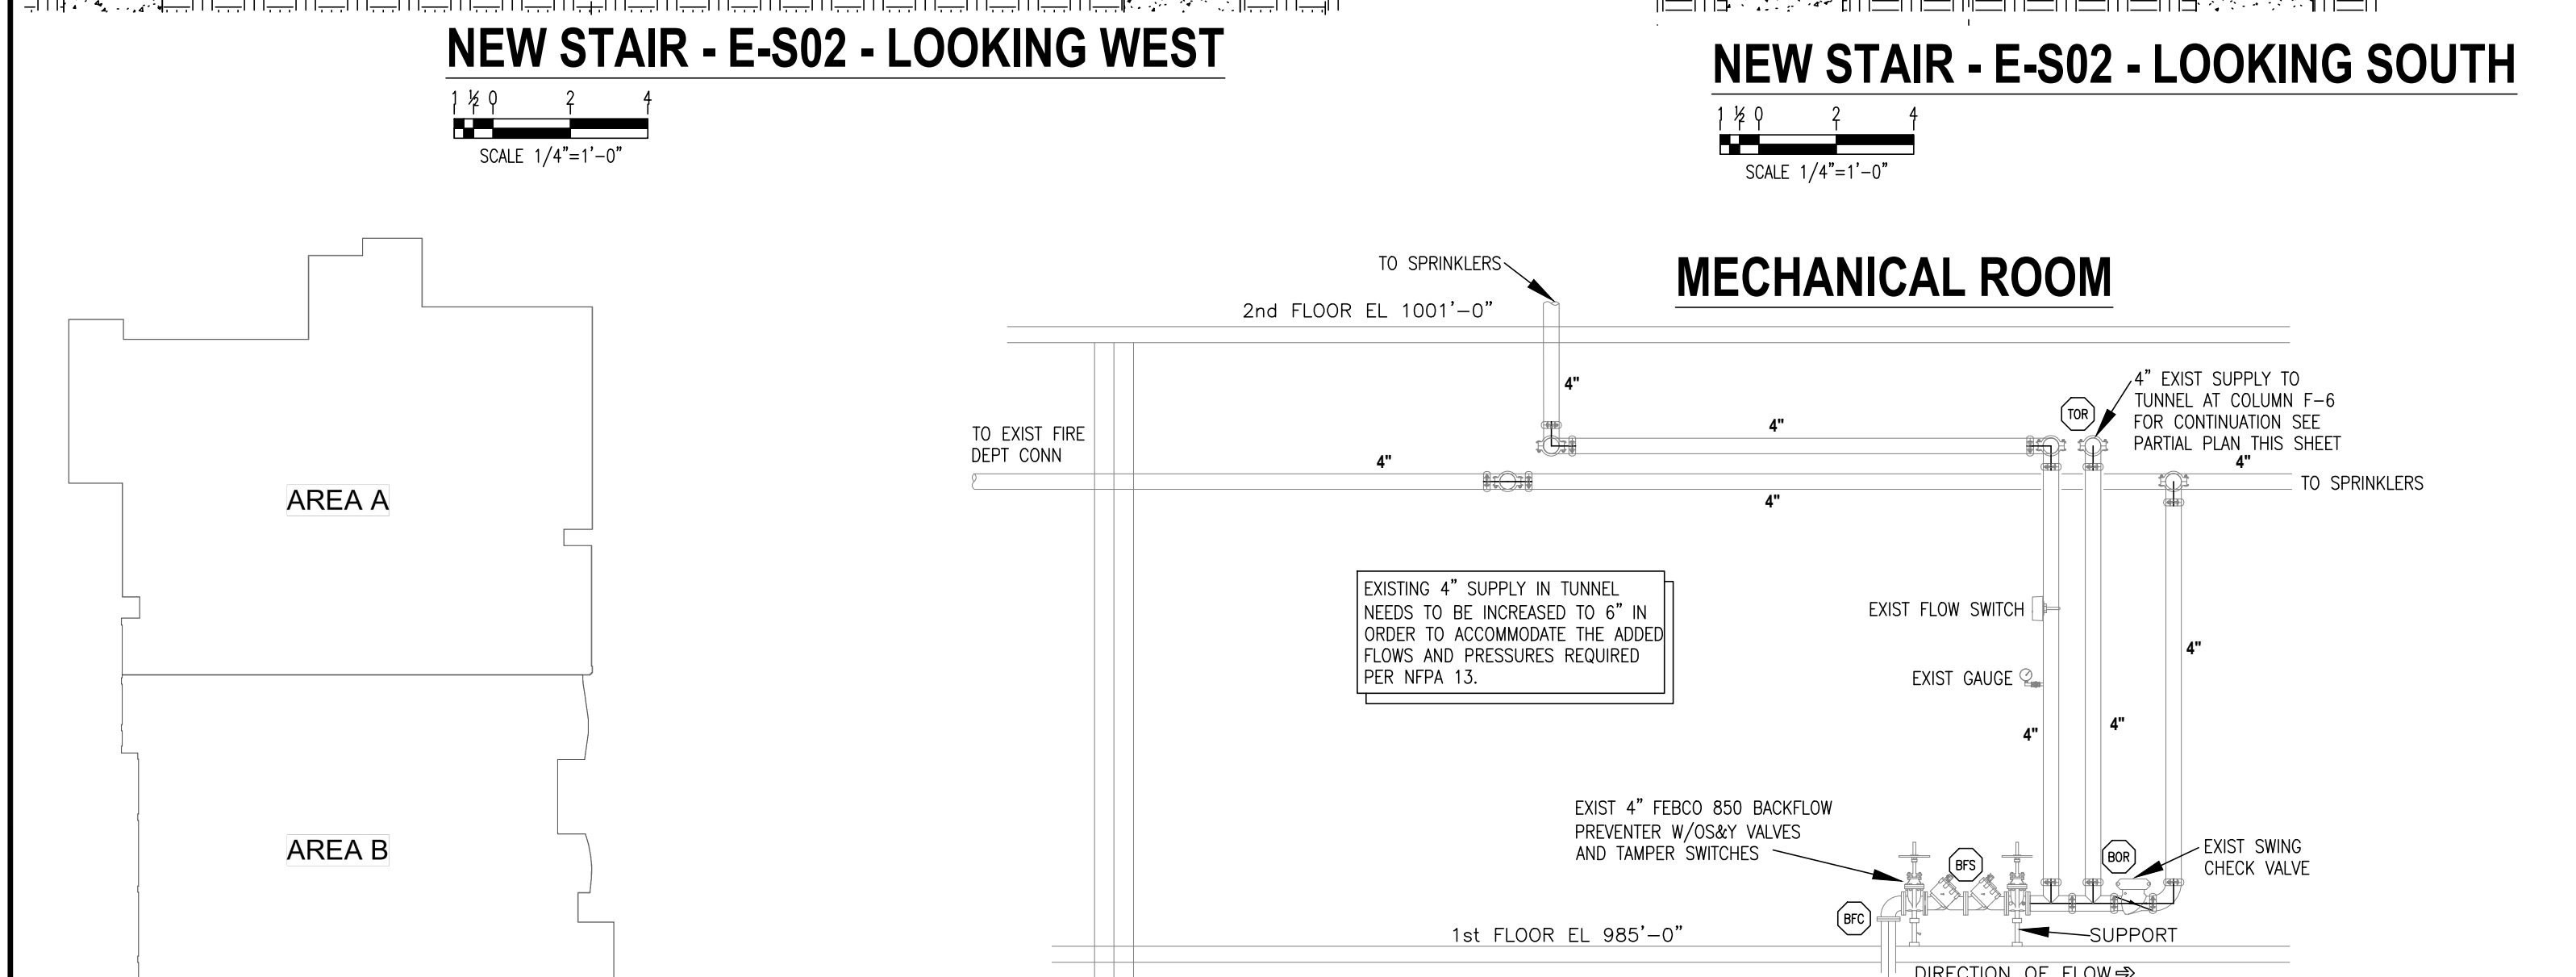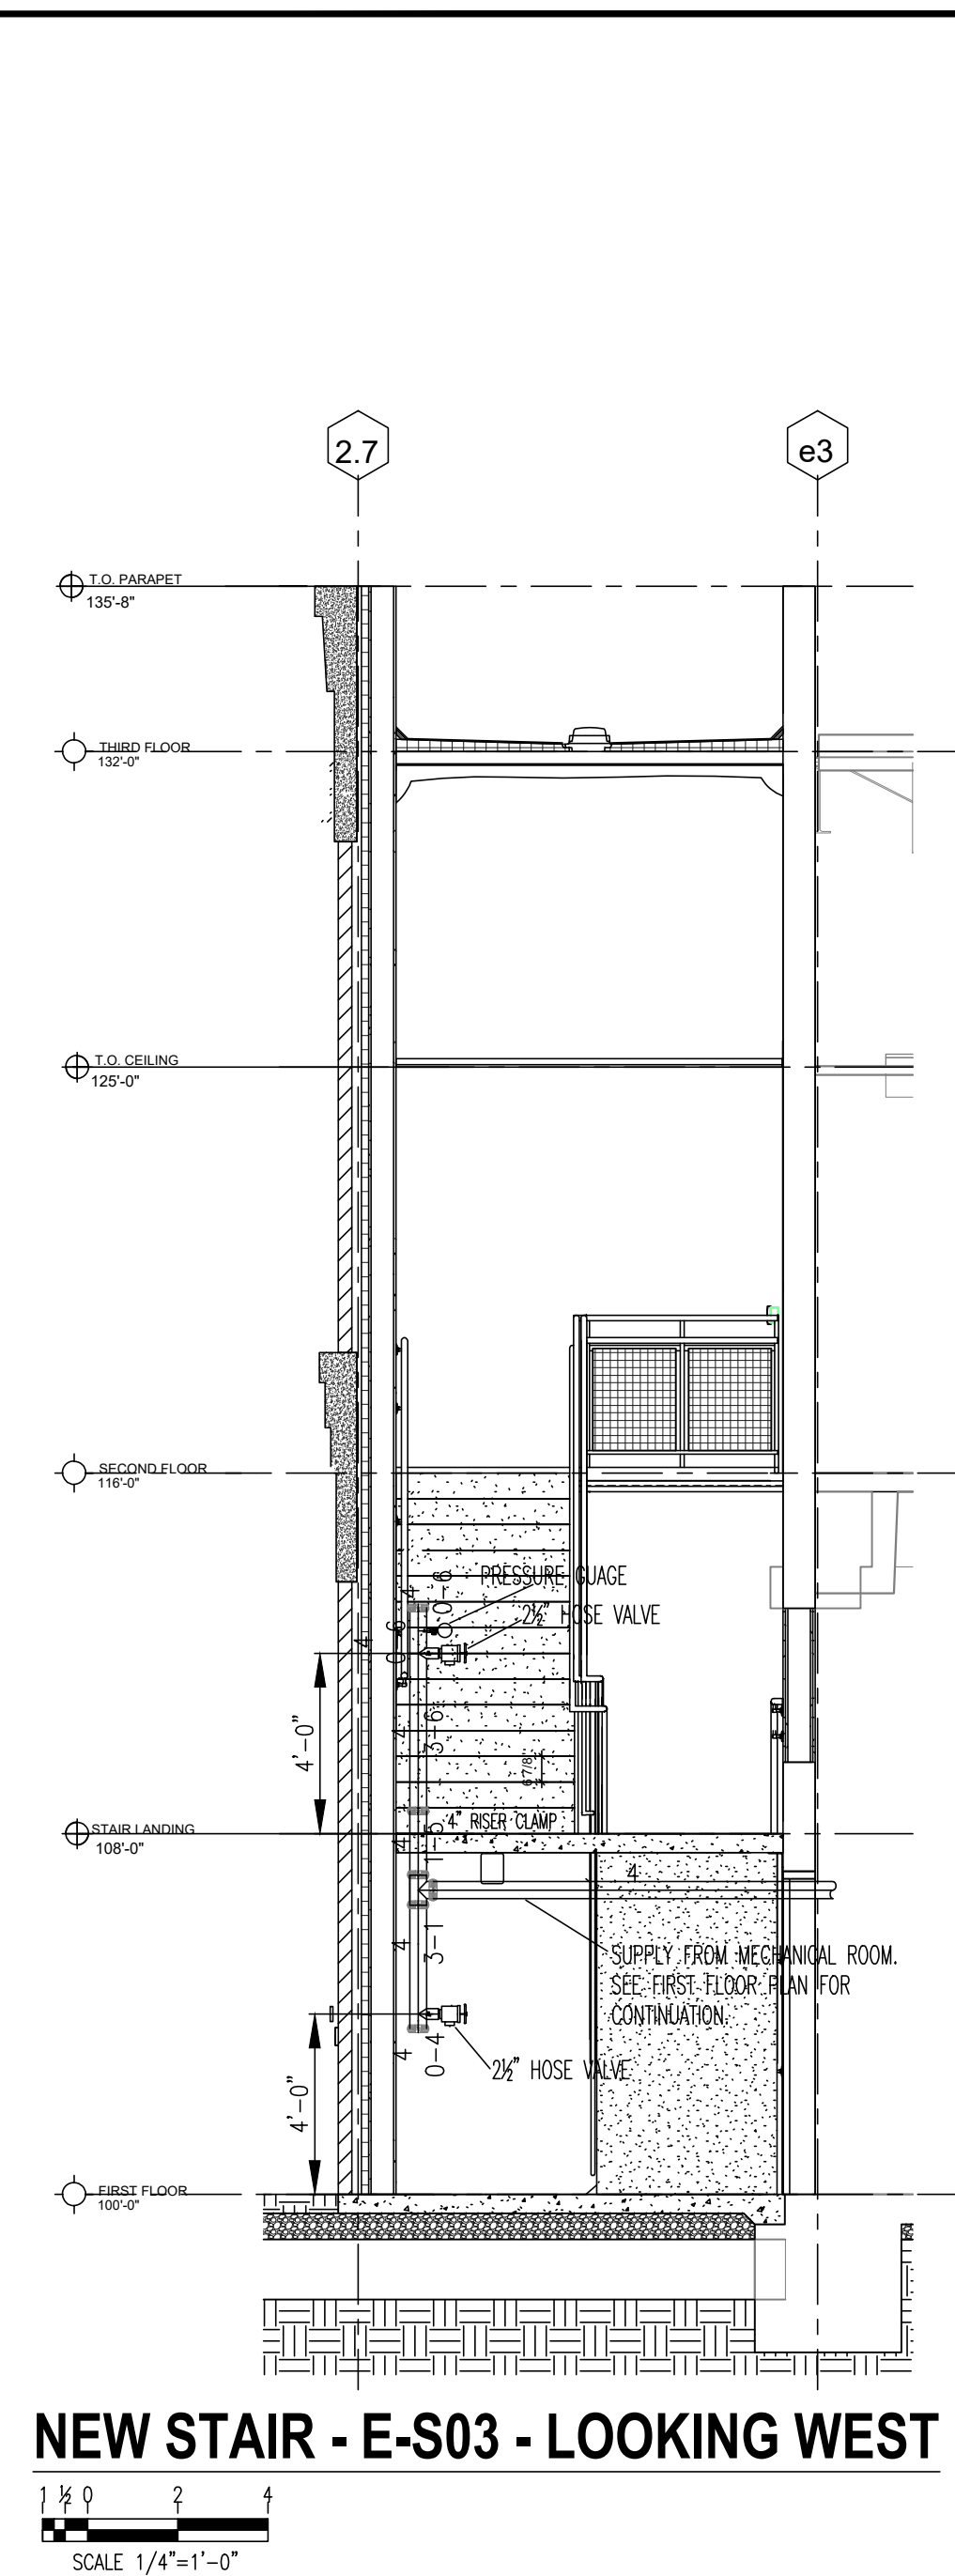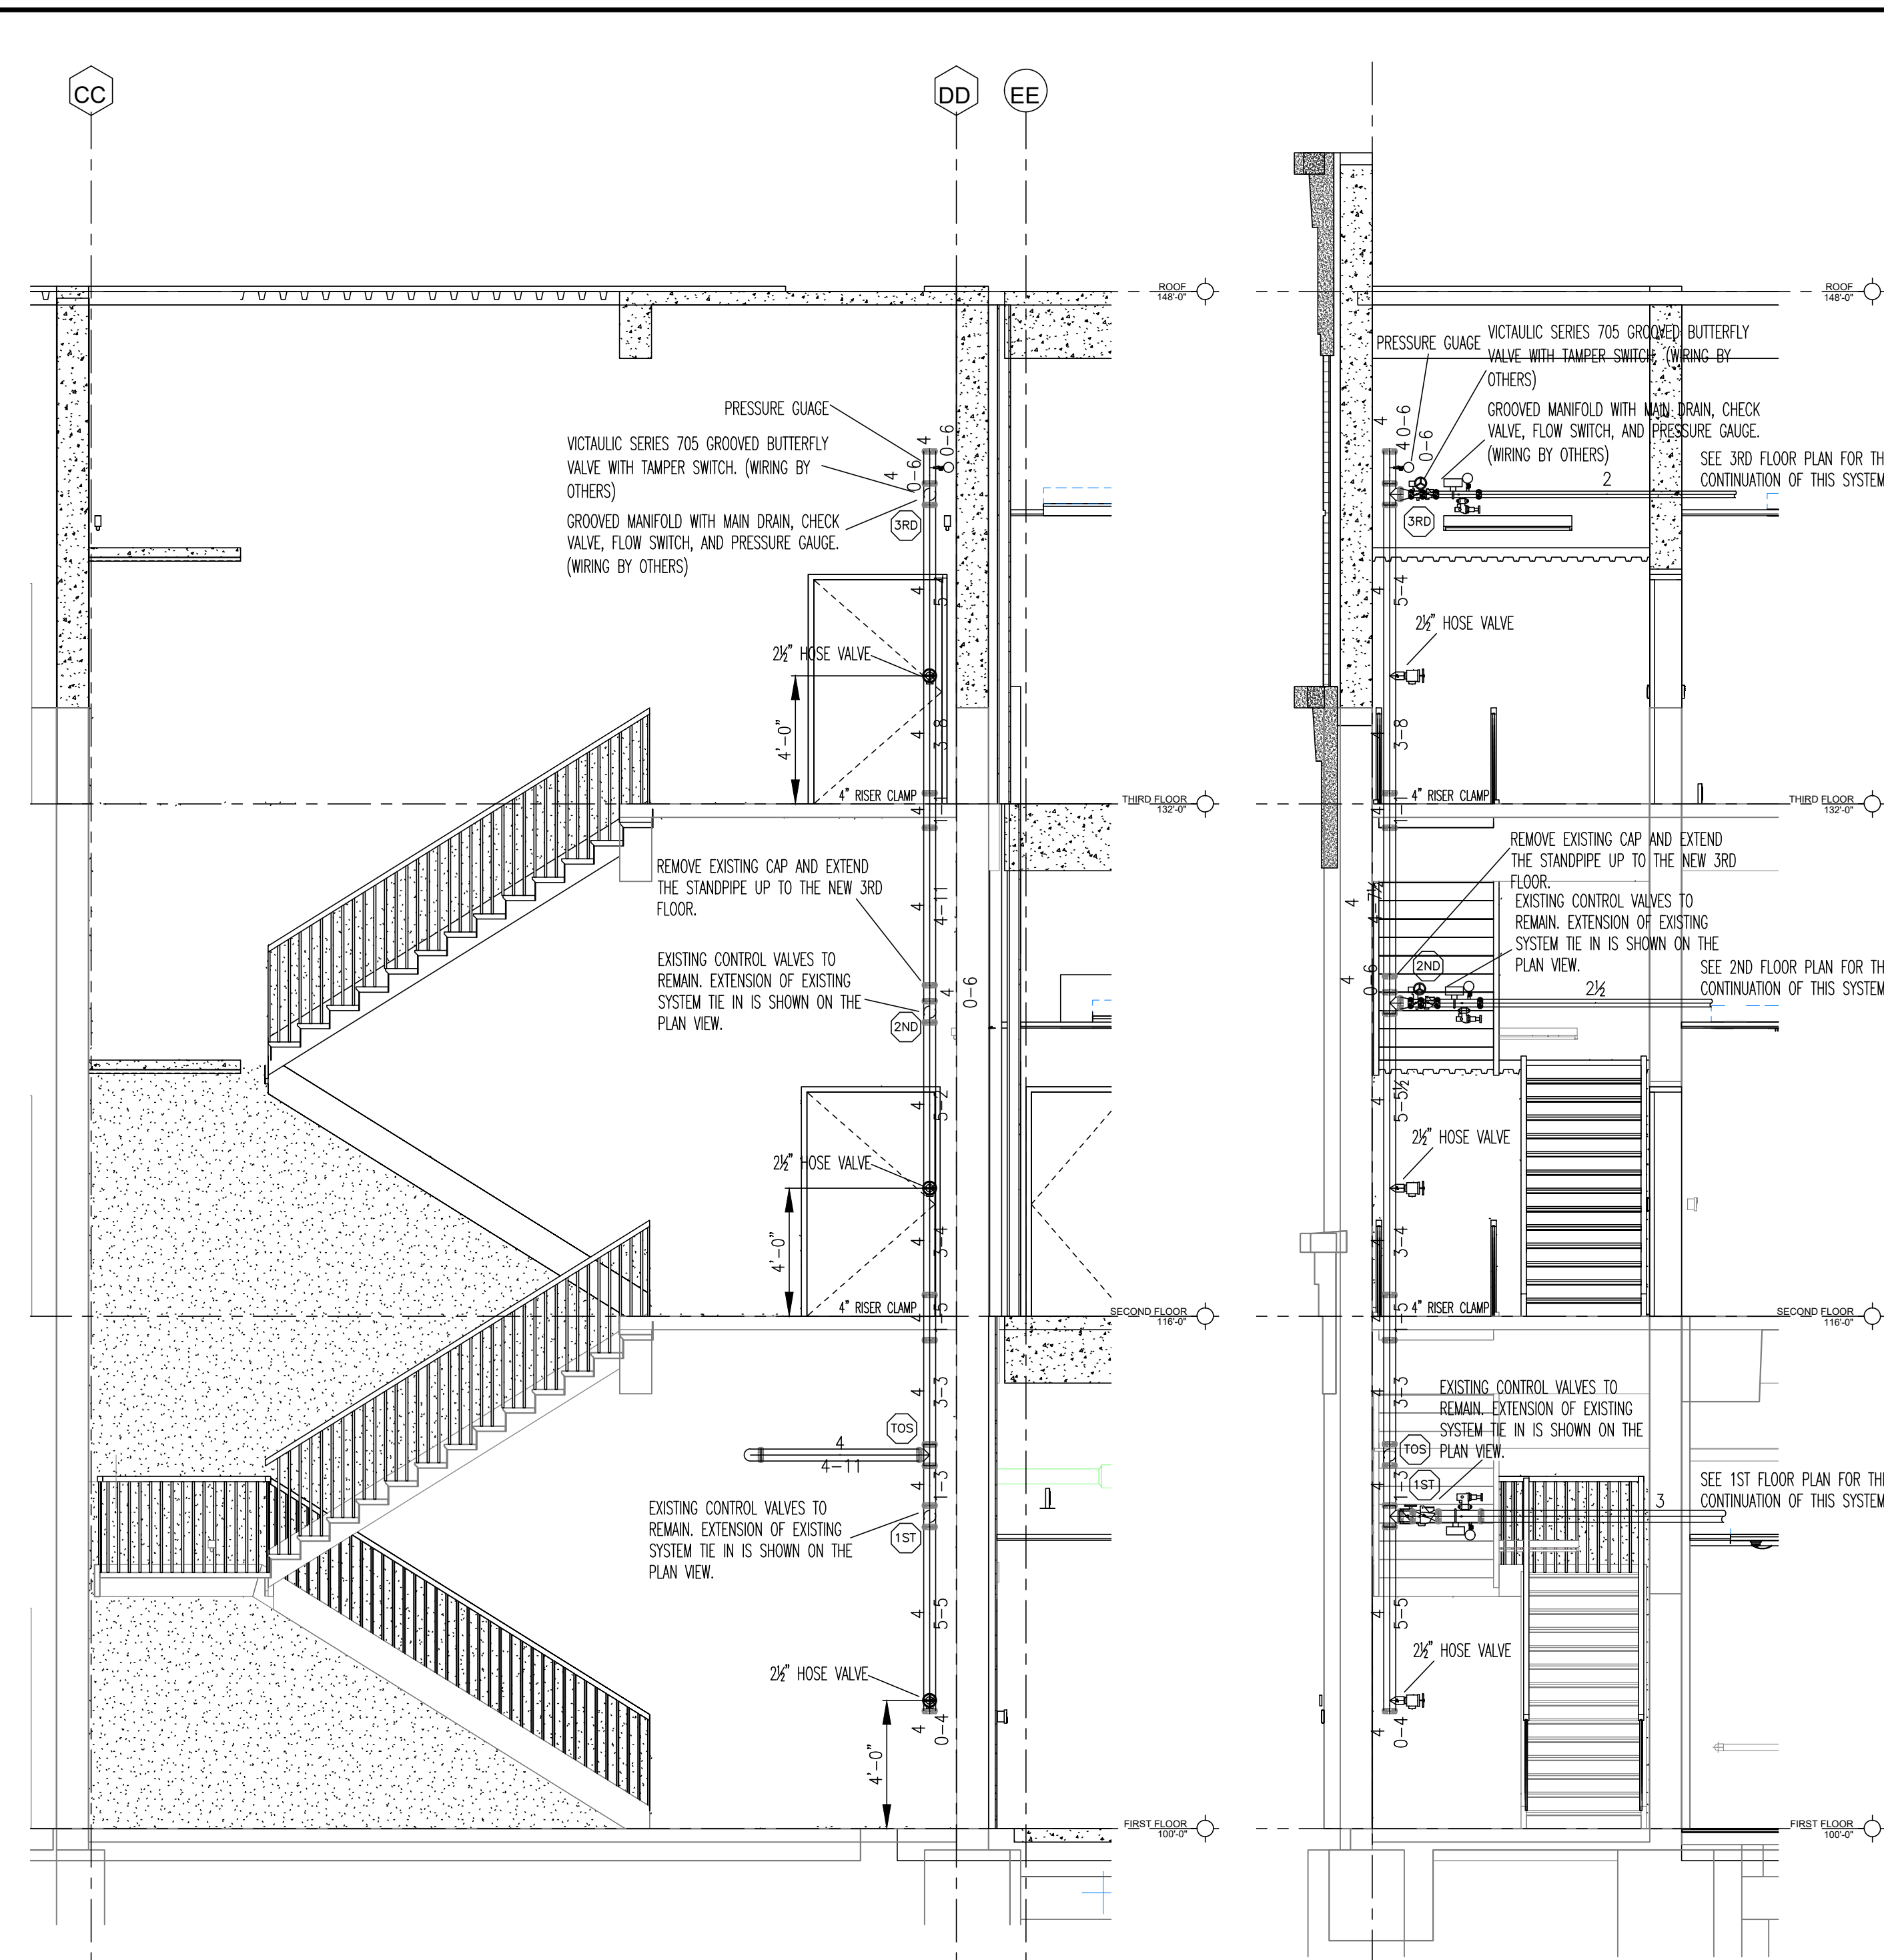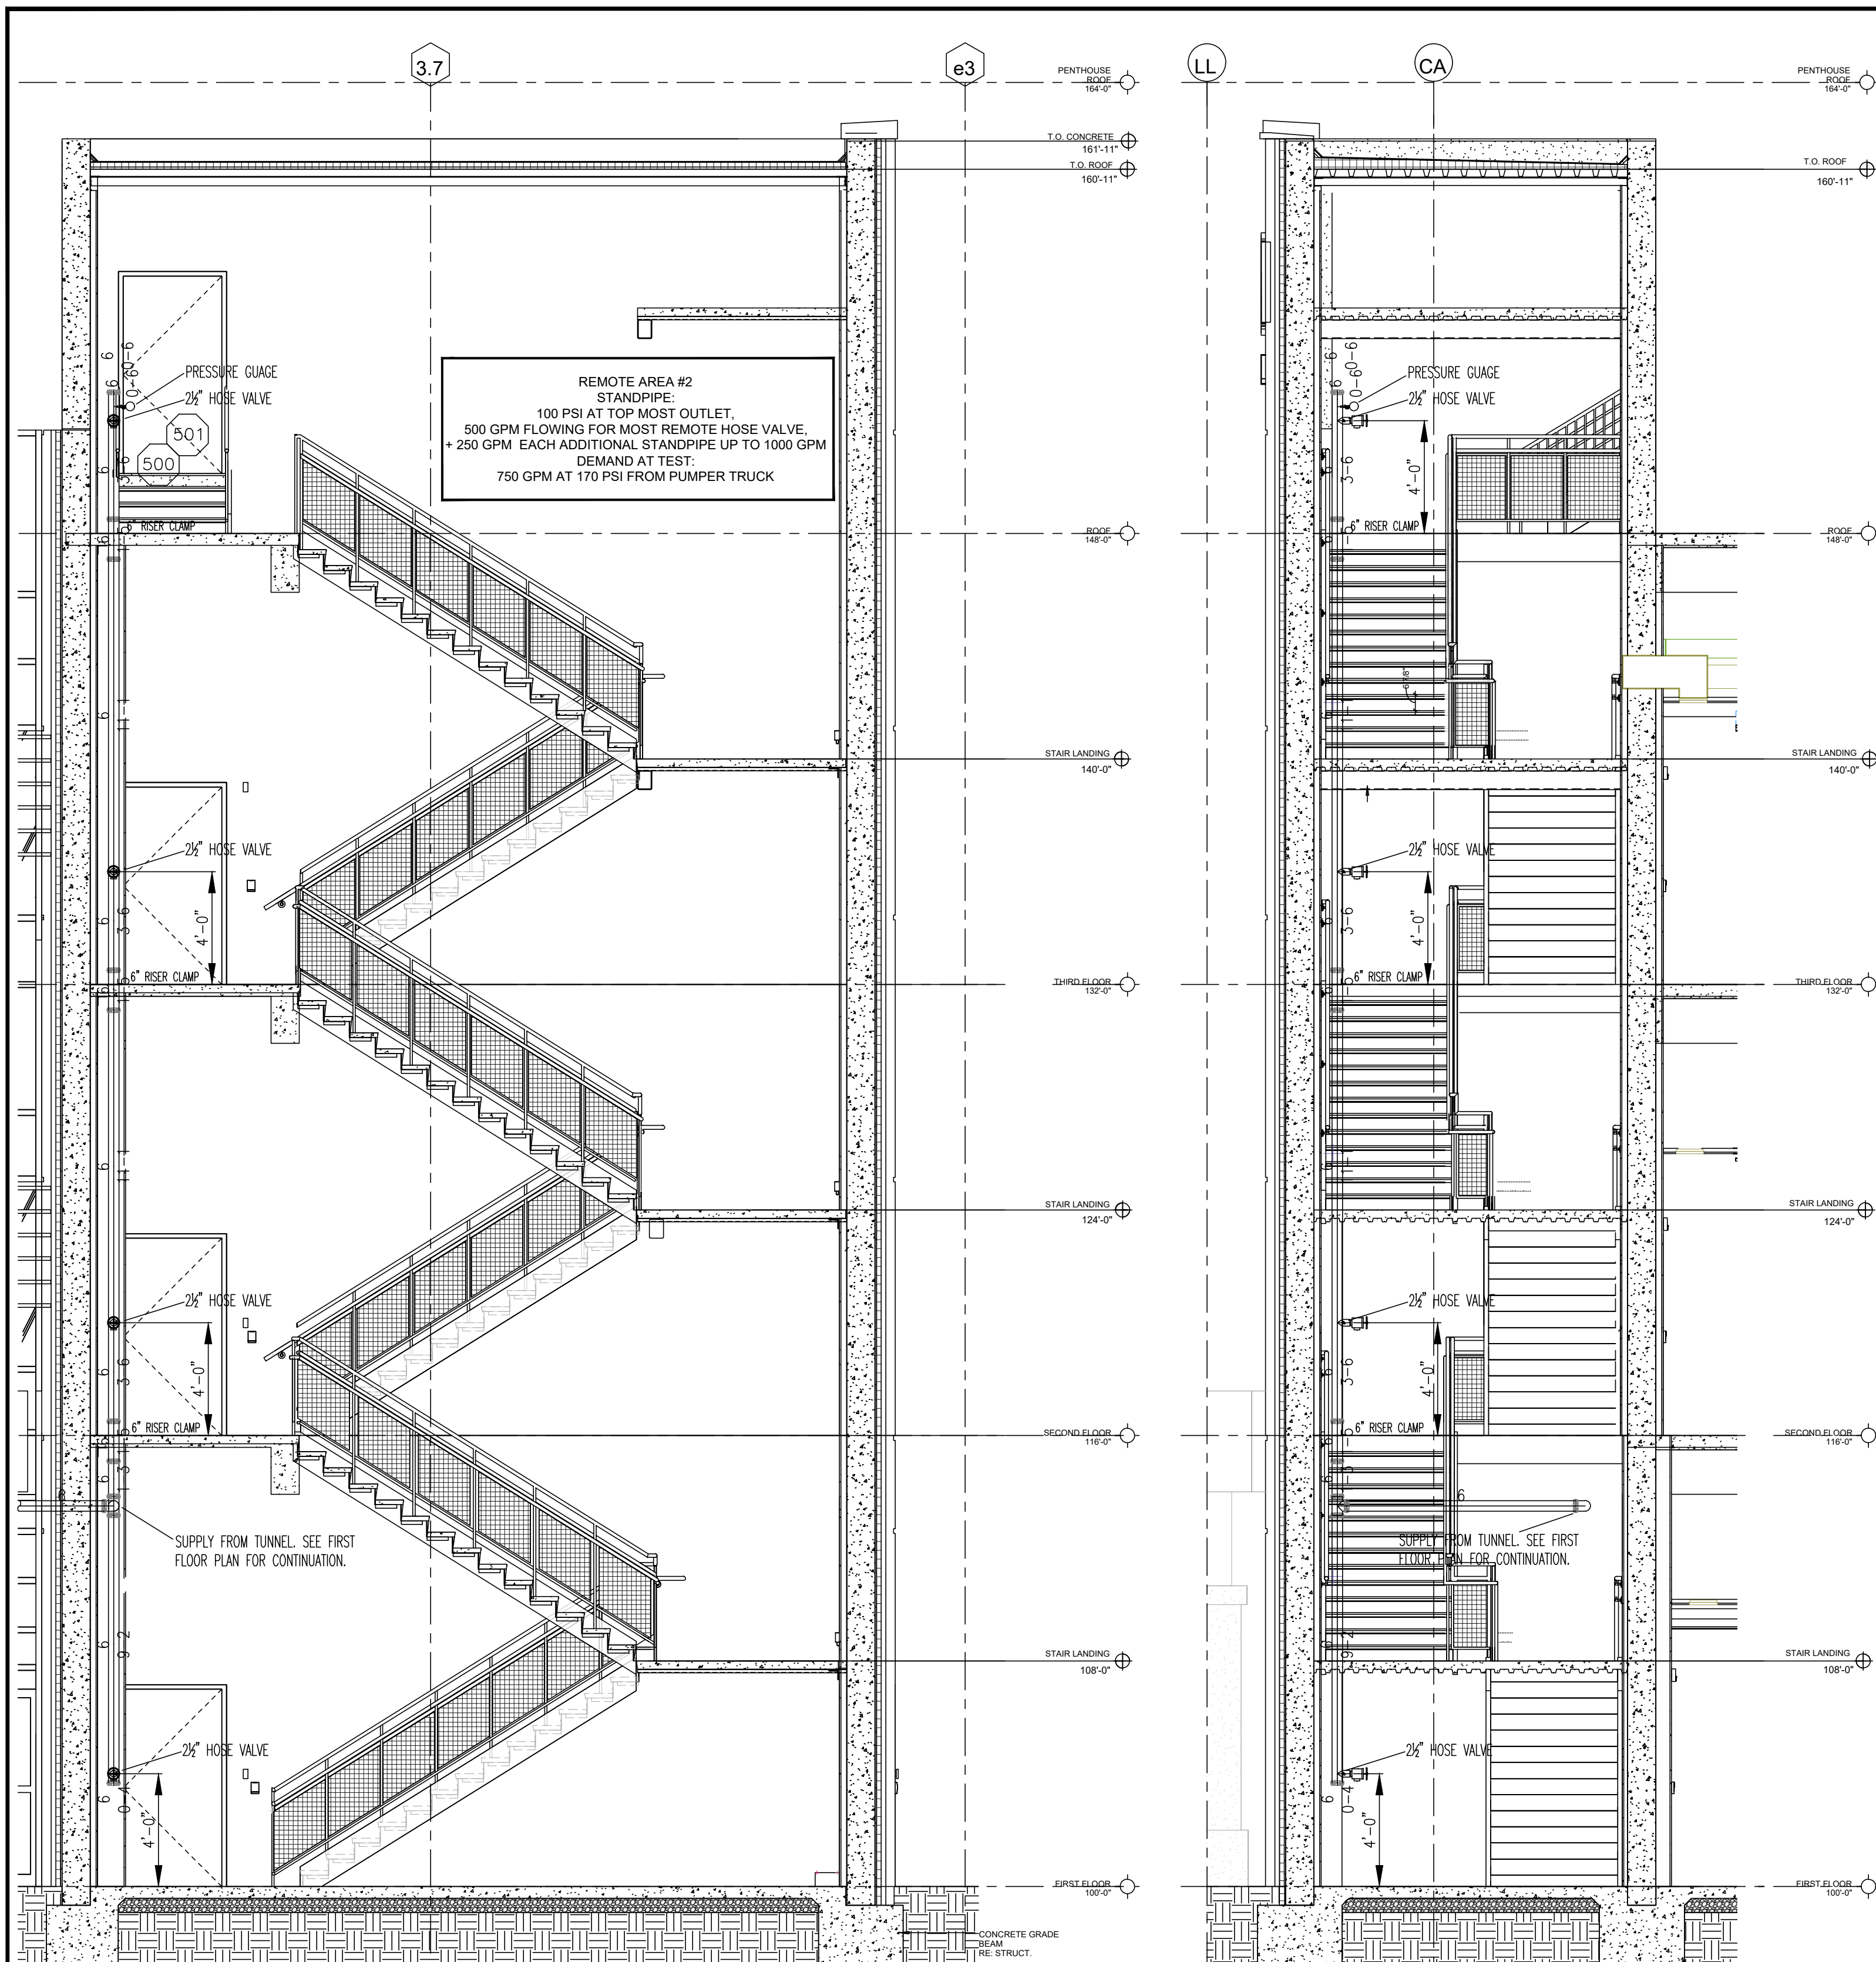

JAYHAWK
FIRE SPRINKLER CO., INC.
1200 E. 12TH AVE., SUITE 100
Olathe, Kansas 66061
TEL: 1-816-777-0036
FAX: 1-816-777-0036

MADEBY CONSTRUCTION
7850 SAINT LUKE BLVD
OVERLAND PARK, KANSAS 66204

SAINT LUKE'S HEALTH SYSTEM
ASC EXPANSION

100 NE Saint Luke's Blvd.
Lee's Summit, MO 64086

FP-6
FIRE PROTECTION
STANDPIPE AND DETAILS

9 OF 9



Hydraulic Calculations by HydraCALC

JAYHAWK FIRE SPRINKLER CO. INC
12030 S. HEDGE LANE TERRACE
OLATHE, KS 66061
913-422-3770
785-232-0975

Job Name : SLE ASC Expansion - 1st Floor (Approval)
Drawing : FP1
Location : 100 NE SAINT LUKE'S BLVD
Remote Area : 1
Contract : 20543M
Data File : SLE ASC Expansion - 1st Floor (Approval) Area 1.WXF

HYDRAULIC CALCULATIONS
for

JOB NAME SLE ASC Expansion - 1st Floor (Approval)
Location 100 NE SAINT LUKE'S BLVD
Drawing # FP1
Contract # 20543M
Date 02/27/2024

DESIGN

Remote area # 1
Remote area location 1ST FLR. AHU ROOM, RESOURCE ROOM
Occupancy classification ORDINARY HAZARD GROUP II / LIGHT HAZARD
Density .20 & .10 - Gpm/SqFt
Area of application 1500 - SqFt
Coverage/sprinkler VARIES - SqFt
Type of sprinkler calculated VICTUALIC Q.R. UPRIGHT & PENDENT
Sprinklers calculated 15
In-rack demand NA - GPM
Hose streams 250 - GPM
Total water required (including hose streams) 583.836 - GPM @ 65.686 - Psi
Type of system WET
Volume of system (dry or pre-action) NA - Gal

WATER SUPPLY INFORMATION

Test date 12-18-2023
Location ONSITE
Source of info CITY OF LEE'S SUMMIT

CONTRACTOR INFO JAYHAWK FIRE SPRINKLER CO. INC

Address 12030 S. HEDGE LANE TERRACE / OLATHE, KS 66061 / 913-422-377
Phone # 785-232-0975
Name of designer TJA
Authority having jurisdiction CITY OF LEE'S SUMMIT / LEE'S SUMMIT FIRE DEPT.
NOTES: NA

text1(35) - invisible

Water Supply Curve

JAYHAWK FIRE SPRINKLER CO. INC
SLE ASC Expansion - 1st Floor (Approval)


Page 2
Date

City Water Supply:

C1 - Static Pressure : 104
C2 - Residual Pressure: 92
C2 - Residual Flow : 2300

Demand:

D1 - Elevation : 9.706
D2 - System Flow : 333.836
D2 - System Pressure : 65.686
Hose (Demand) : 250
D3 - System Demand : 583.836
Safety Margin : 37.364

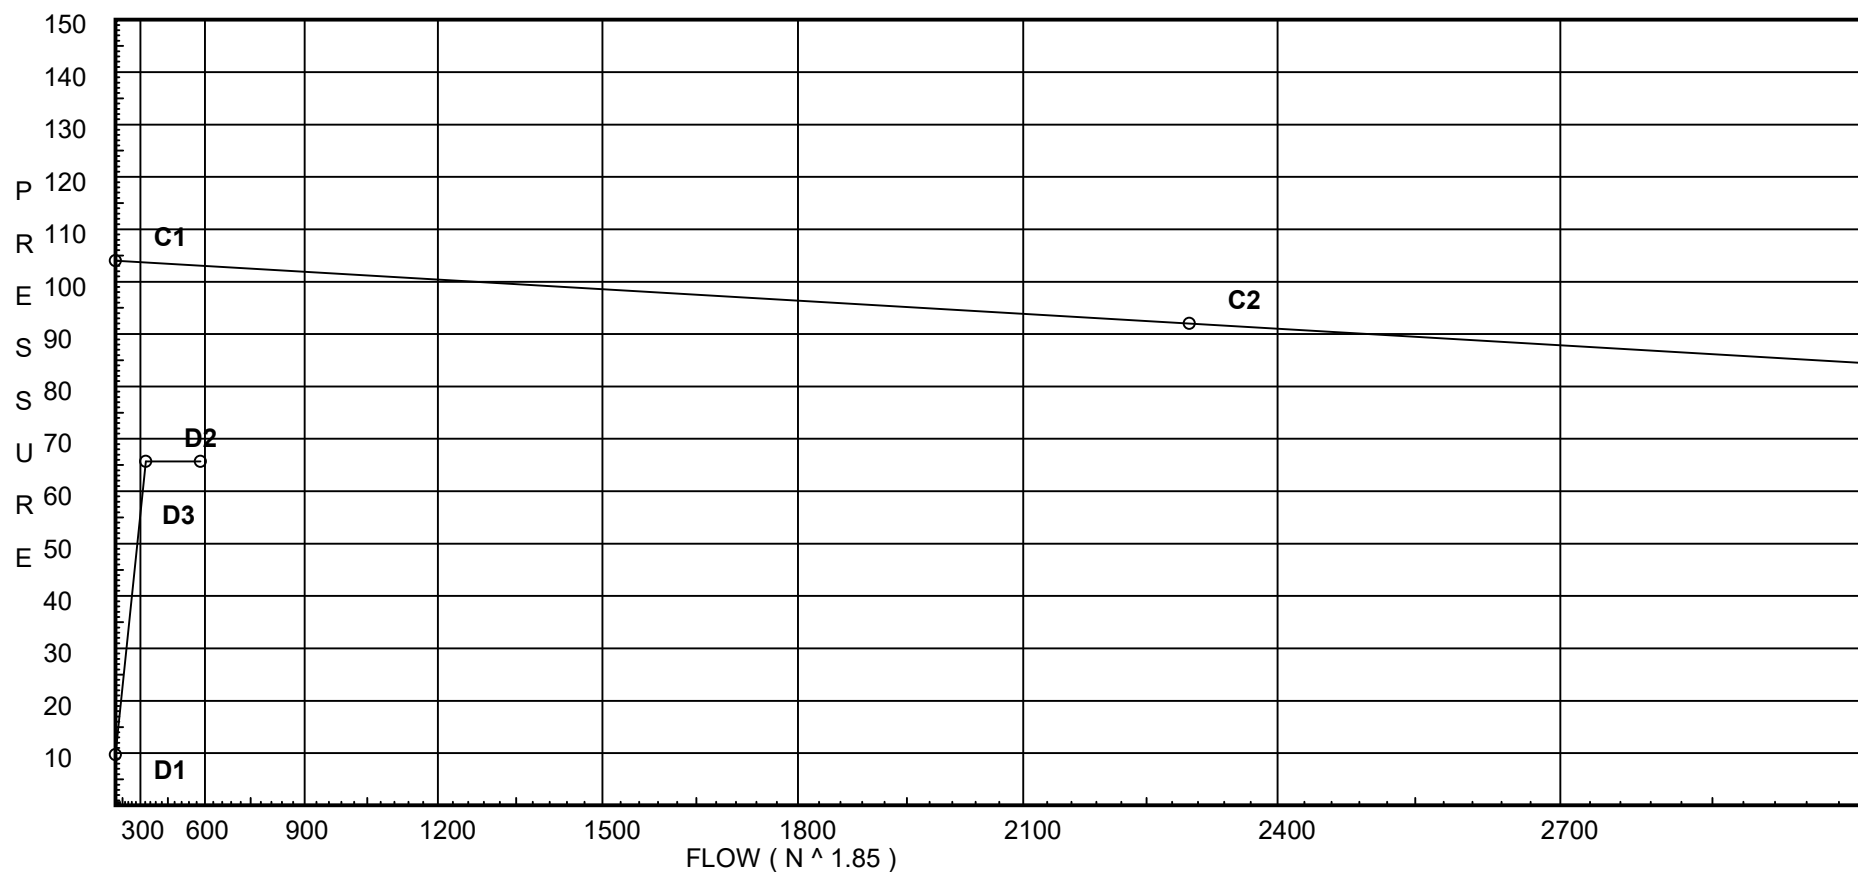

Fittings Used Summary

JAYHAWK FIRE SPRINKLER CO. INC
SLE ASC Expansion - 1st Floor (Approval)

Page 3
Date

Fitting Legend

Abbrev.	Name	1/2	3/4	1	1 1/4	1 1/2	2	2 1/2	3	3 1/2	4	5	6	8	10	12	14	16	18	20	24
B	NFPA 13 Butterfly Valve	0	0	0	0	0	6	7	10	0	12	9	10	12	19	21	0	0	0	0	0
C	Roll Groove Coupling	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1
E	NFPA 13 90' Standard Elbow	1	2	2	3	4	5	6	7	8	10	12	14	18	22	27	35	40	45	50	61
Fsp	Flow Switch Potter VSR	Fitting generates a Fixed Loss Based on Flow																			
G	NFPA 13 Gate Valve	0	0	0	0	0	1	1	1	1	2	2	3	4	5	6	7	8	10	11	13
T	NFPA 13 90' Flow thru Tee	3	4	5	6	8	10	12	15	17	20	25	30	35	50	60	71	81	91	101	121
V	90' Ell Firelock #001	0	0	0	0	0	3.5	4.3	5	0	6.8	8.5	10	13	0	0	0	0	0	0	0
X	90'Tee-BranchFirelock002	0	0	0	0	0	8.5	10.8	13	0	16	21	25	33	0	0	0	0	0	0	0

Units Summary

Diameter Units Inches
Length Units Feet
Flow Units US Gallons per Minute
Pressure Units Pounds per Square Inch

Note: Fitting Legend provides equivalent pipe lengths for fittings types of various diameters. Equivalent lengths shown are standard for actual diameters of Sched 40 pipe and CFactors of 120 except as noted with *. The fittings marked with a * show equivalent lengths values supplied by manufacturers based on specific pipe diameters and CFactors and they require no adjustment. All values for fittings not marked with a * will be adjusted in the calculation for CFactors of other than 120 and diameters other than Sched 40 per NFPA.

Flow Summary - NFPA

JAYHAWK FIRE SPRINKLER CO. INC
SLE ASC Expansion - 1st Floor (Approval)

Page 4
Date

SUPPLY ANALYSIS

<i>Node at Source</i>	<i>Static Pressure</i>	<i>Residual Pressure</i>	<i>Flow</i>	<i>Available Pressure</i>	<i>Total Demand</i>	<i>Required Pressure</i>
TEST	104.0	92	2300.0	103.05	583.84	65.686

NODE ANALYSIS

<i>Node Tag</i>	<i>Elevation</i>	<i>Node Type</i>	<i>Pressure at Node</i>	<i>Discharge at Node</i>	<i>Notes</i>	
DP01	994.12	5.6	7.0	14.82	0.1	144
EQ01	995.29		6.73			
DP02	994.12	5.6	7.0	14.82	0.1	104
EQ02	996.29		6.37			
SP03	1005.54	8	7.0	21.17	0.2	100
EQ03	1004.7		8.21			
1	1004.7	7.39	8.21	21.17	K=K @ EQ03	
2	1004.7	7.39	8.59	21.65	K=K @ EQ03	
3	1004.7	7.39	9.99	23.35	K=K @ EQ03	
4	1004.7		12.17			
5	1004.7		12.21			
6	995.29		16.81			
7	995.29		16.97			
8	995.29		17.09			
A	995.29		30.64			
1ST	995.29		37.59			
TOS	978.12		45.76			
BOS	978.12		47.05			
TTR	995.29		45.9			
TOR	995.29		50.49			
BOR	987.29		54.97			
BFS	987.29		56.4			
BFC	987.29		60.53			
SRC	982.29		64.55			
TAP	982.29		65.25			
TEST	982.29		65.69	250.0		
9	1004.7	7.39	9.36	22.61	K=K @ EQ03	
10	1004.7	7.39	9.79	23.12	K=K @ EQ03	
11	995.29	5.71	14.39	21.67	K=K @ EQ01	
12	995.29		15.27			
13	995.29		15.75			
14	995.29	5.71	14.84	22.0	K=K @ EQ01	
15	1004.7	7.39	8.24	21.21	K=K @ EQ03	
16	1004.7	7.39	8.62	21.69	K=K @ EQ03	
17	1004.7	7.39	10.02	23.39	K=K @ EQ03	
18	1004.7	7.39	9.4	22.65	K=K @ EQ03	
19	1004.7	7.39	9.83	23.16	K=K @ EQ03	
20	995.29	5.71	14.64	21.85	K=K @ EQ01	
21	995.29		15.54			
22	995.29		16.02			
23	995.29	5.71	15.1	22.19	K=K @ EQ01	
24	996.29	5.87	14.2	22.12	K=K @ EQ02	

Flow Summary - NFPA

JAYHAWK FIRE SPRINKLER CO. INC
SLE ASC Expansion - 1st Floor (Approval)

Page 5
Date

NODE ANALYSIS (cont.)

<i>Node Tag</i>	<i>Elevation</i>	<i>Node Type</i>	<i>Pressure at Node</i>	<i>Discharge at Node</i>	<i>Notes</i>
25	996.29		15.14		

Final Calculations : Hazen-Williams

JAYHAWK FIRE SPRINKLER CO. INC
SLE ASC Expansion - 1st Floor (Approval)

Page 6
Date

Node1 to Node2	Elev1 Elev2	K Fact	Qa Qt	Nom Act	Fitting or Equiv Len	Pipe Ftngs Total	CFact Pf/Ft	Pt Pe Pf	*****	Notes	*****
DP01 to EQ01	994.12 995.29	5.60	14.82 14.82	1 1.049	E 2.0	1.170 2.000 3.170	120 0.0748	7.000 -0.507 0.237		Vel = 5.50	
EQ01			0.0 14.82					6.730		K Factor = 5.71	
DP02 to EQ02	994.12 996.29	5.60	14.82 14.82	1 1.049	E 2.0	2.170 2.000 4.170	120 0.0748	7.000 -0.940 0.312		Vel = 5.50	
EQ02			0.0 14.82					6.372		K Factor = 5.87	
SP03 to EQ03	1005.54 1004.7	8.00	21.17 21.17	1 1.049	T 5.0	0.830 5.000 5.830	120 0.1444	7.000 0.364 0.842		Vel = 7.86	
EQ03			0.0 21.17					8.206		K Factor = 7.39	
1 to 2	1004.7 1004.7	7.39	21.17 21.17	1.25 1.38		10.000 10.000	120 0.0380	8.206 0.0 0.380		K = K @ EQ03 Vel = 4.54	
2 to 3	1004.7 1004.7	7.39	21.65 42.82	1.25 1.38		10.000 10.000	120 0.1400	8.586 0.0 1.400		K = K @ EQ03 Vel = 9.18	
3 to 4	1004.7 1004.7	7.39	23.34 66.16	1.25 1.38	T 6.0	0.970 6.000 6.970	120 0.3131	9.986 0.0 2.182		K = K @ EQ03 Vel = 14.19	
4 to 5	1004.7 1004.7		45.73 111.89	4 4.026		10.000 10.000	120 0.0045	12.168 0.0 0.045		Vel = 2.82	
5 to 6	1004.7 995.29		112.11 224.0	4 4.026	2V 13.6	18.220 13.600 31.820	120 0.0162	12.213 4.075 0.517		Vel = 5.65	
6 to 7	995.29 995.29		43.67 267.67	4 4.026		7.440 7.440	120 0.0226	16.805 0.0 0.168		Vel = 6.75	
7 to 8	995.29 995.29		22.12 289.79	4 4.026		4.560 4.560	120 0.0263	16.973 0.0 0.120		Vel = 7.30	
8 to A	995.29 995.290		44.05 333.84	4 4.026	20V 2X 32.0	230.340 168.000 398.340	120 0.0340	17.093 0.0 13.542		Vel = 8.41	
A to 1ST	995.290 995.290		0.0 333.84	3 3.068	2V B C Fsp 10.0 10.0 1.0 0.0	10.000 21.000 31.000	120 0.1277	30.635 3.000 3.959		* * Fixed Loss = 3 Vel = 14.49	
1ST to TOS	995.290 978.120		0.0 333.84	4 4.026	T 20.0	1.500 20.000 21.500	120 0.0340	37.594 7.436 0.732		Vel = 8.41	
TOS to BOS	978.120 978.120		0.0 333.84	4 4.026	2E 20.0	17.920 20.000 37.920	120 0.0340	45.762 0.0 1.289		Vel = 8.41	

Final Calculations : Hazen-Williams

JAYHAWK FIRE SPRINKLER CO. INC
SLE ASC Expansion - 1st Floor (Approval)

Page 7
Date

Node1 to Node2	Elev1 Elev2	K Fact	Qa Qt	Nom Act	Fitting or Equiv Len	Pipe Ftngs Total	CFact Pf/Ft	Pt Pe Pf	*****	Notes	*****
BOS to TTR	978.120 995.290		0.0 333.84	4 4.026	E 3E	10.0 30.0	175.000 10.000 185.000	120 -7.436 6.289		Vel = 8.41	
TTR to TOR	995.290 995.290		0.0 333.84	4 4.026	3E 2E	30.0 20.0	104.750 30.000 134.750	120 0.0 4.581		Vel = 8.41	
TOR to BOR	995.290 987.290		0.0 333.84	4 4.026	2E T B	20.0 12.0	10.000 20.000 30.000	120 50.485 3.465		Vel = 8.41	
BOR to BFS	987.290 987.290		0.0 333.84	4 4.026	T B	20.0 12.0	10.000 32.000 42.000	120 54.970 0.0		Vel = 8.41	
BFS to BFC	987.290 987.290		0.0 333.84	4 4.026			4.000 4.000	120 56.398 4.000		* * Fixed Loss = 4 Vel = 8.41	
BFC to SRC	987.290 982.290		0.0 333.84	4 4.1	2E	29.067	50.000 29.067 79.067	140 60.534 2.166		Vel = 8.11	
SRC to TAP	982.290 982.290		0.0 333.84	6 6.16	T E G	43.037 20.084 4.304	150.000 67.425 217.425	140 64.549 0.0		Vel = 3.59	
TAP to TEST	982.290 982.290		0.0 333.84	8 8.27	T G 2E	55.354 6.326 56.936	450.000 118.616 568.616	140 65.250 0.0		Vel = 1.99	
TEST			250.00 583.84					65.686		Qa = 250.00 K Factor = 72.04	
9 to 10	1004.7 1004.7	7.39	22.61	1.25			10.000	120 9.363 0.0		K = K @ EQ03	
10 to 4	1004.7 1004.7	7.39	23.12	1.25	T	6.0	9.030 6.000 15.030	120 9.792 0.0		K = K @ EQ03	
4			45.73	1.38				0.1581 2.376		Vel = 9.81	
4			0.0 45.73					12.168		K Factor = 13.11	
11 to 12	995.29 995.29	5.71	21.67	1	T	5.0	0.830 5.000 5.830	120 14.394 0.0		K = K @ EQ01	
12 to 13	995.29 995.29		21.67	1.049			5.830	0.1509 0.880		Vel = 8.04	
12 to 13	995.29 995.29		0.0	1.25			12.000	120 15.274 0.0		Vel = 4.65	
13 to 6	995.29 995.29		21.67	1.38			12.000	0.0397 0.476		Vel = 4.65	
13 to 6	995.29 995.29		22.00	1.25	T	6.0	1.270 6.000 7.270	120 15.750 0.0		Vel = 9.37	
6			43.67	1.38				0.1451 1.055		Vel = 9.37	
6			0.0 43.67					16.805		K Factor = 10.65	
14 to 13	995.29 995.29	5.71	22.00	1	T	5.0	0.830 5.000 5.830	120 14.845 0.0		K = K @ EQ01	
13			22.0	1.049				0.1552 0.905		Vel = 8.17	

Final Calculations : Hazen-Williams

JAYHAWK FIRE SPRINKLER CO. INC
SLE ASC Expansion - 1st Floor (Approval)

Page 8
Date

Node1 to Node2	Elev1 Elev2	K Fact	Qa Qt	Nom Act	Fitting or Equiv	Len	Pipe Ftngs Total	CFact Pf/Ft	Pt Pe Pf	*****	Notes	*****
13			0.0 22.00						15.750		K Factor = 5.54	
15 to 16	1004.7 1004.7	7.39	21.21	1.25			10.000	120	8.237 0.0		K = K @ EQ03	
16 to 17	1004.7 1004.7	7.39	21.21	1.38			10.000	0.0382	0.382		Vel = 4.55	
16 to 17	1004.7 1004.7	7.39	21.69	1.25			10.000	120	8.619 0.0		K = K @ EQ03	
17 to 5	1004.7 1004.7	7.39	42.9	1.38			10.000	0.1404	1.404		Vel = 9.20	
17 to 5	1004.7 1004.7	7.39	23.39	1.25	T	6.0	0.970 6.000 6.970	120	10.023 0.0		K = K @ EQ03	
			66.29	1.38				0.3142	2.190		Vel = 14.22	
5			0.0 66.29						12.213		K Factor = 18.97	
18 to 19	1004.7 1004.7	7.39	22.65	1.25			10.000	120	9.398 0.0		K = K @ EQ03	
19 to 5	1004.7 1004.7	7.39	22.65	1.38			10.000	0.0431	0.431		Vel = 4.86	
19 to 5	1004.7 1004.7	7.39	23.16	1.25	T	6.0	9.030 6.000 15.030	120	9.829 0.0		K = K @ EQ03	
			45.81	1.38				0.1586	2.384		Vel = 9.83	
5			0.0 45.81						12.213		K Factor = 13.11	
20 to 21	995.29 995.29	5.71	21.85	1	T	5.0	0.830 5.000 5.830	120	14.643 0.0		K = K @ EQ01	
21 to 22	995.29 995.29		21.85	1.049				0.1533	0.894		Vel = 8.11	
21 to 22	995.29 995.29		0.0	1.25			12.000	120	15.537 0.0			
22 to 8	995.29 995.29		21.85	1.38			12.000	0.0402	0.483		Vel = 4.69	
22 to 8	995.29 995.29		22.20	1.25	T	6.0	1.270 6.000 7.270	120	16.020 0.0			
			44.05	1.38				0.1476	1.073		Vel = 9.45	
8			0.0 44.05						17.093		K Factor = 10.65	
23 to 22	995.29 995.29	5.71	22.19	1	T	5.0	0.830 5.000 5.830	120	15.101 0.0		K = K @ EQ01	
			22.19	1.049				0.1576	0.919		Vel = 8.24	
22			0.0 22.19						16.020		K Factor = 5.54	
24 to 25	996.29 996.29	5.87	22.12	1	T	5.0	1.000 5.000 6.000	120	14.199 0.0		K = K @ EQ02	
25 to 7	996.29 995.29		22.12	1.049				0.1567	0.940		Vel = 8.21	
25 to 7	996.29 995.29		0.0	1.25	3E T	9.0 6.0	18.980 15.000 33.980	120	15.139 0.433			
			22.12	1.38				0.0412	1.401		Vel = 4.74	
7			0.0 22.12						16.973		K Factor = 5.37	



Hydraulic Calculations by HydraCALC

JAYHAWK FIRE SPRINKLER CO. INC
12030 S. HEDGE LANE TERRACE
OLATHE, KS 66061
913-422-3770
785-232-0975

Job Name : SLE ASC Expansion - 2nd Floor (Approval)
Drawing : FP3
Location : 100 NE SAINT LUKE'S BLVD
Remote Area : 2
Contract : 20543M
Data File : SLE ASC Expansion - 2nd Floor (Approval) Area 2.WXF

HYDRAULIC CALCULATIONS
for

JOB NAME SLE ASC Expansion
Location 100 NE SAINT LUKE'S BLVD
Drawing # FP3
Contract # 20543M
Date 02/27/2024

DESIGN

Remote area # 2
Remote area location 2ND FLR. EXAM ROOMS AND CORRIDOR
Occupancy classification LIGHT HAZARD
Density .10 - Gpm/SqFt
Area of application 900 - SqFt
Coverage/sprinkler VARIES - SqFt
Type of sprinkler calculated VICTUALIC Q.R. PENDENT
Sprinklers calculated 10
In-rack demand NA - GPM
Hose streams 100 - GPM
Total water required (including hose streams) 324.098 - GPM @ 73.560 - Psi
Type of system WET
Volume of system (dry or pre-action) NA - Gal

WATER SUPPLY INFORMATION

Test date 12-18-2023
Location ONSITE
Source of info CITY OF LEE'S SUMMIT

CONTRACTOR INFO JAYHAWK FIRE SPRINKLER CO. INC
Address 12030 S. HEDGE LANE TERRACE / OLATHE, KS 66061 / 913-422-377
Phone # 785-232-0975
Name of designer TJA
Authority having jurisdiction CITY OF LEE'S SUMMIT / LEE'S SUMMIT FIRE DEPT.
NOTES: NA

text1(35) - invisible

Water Supply Curve

JAYHAWK FIRE SPRINKLER CO. INC
SLE ASC Expansion - 2nd Floor (Approval)


Page 2
Date

City Water Supply:

C1 - Static Pressure : 104
C2 - Residual Pressure: 92
C2 - Residual Flow : 2300

Demand:

D1 - Elevation : 12.993
D2 - System Flow : 224.098
D2 - System Pressure : 73.560
Hose (Demand) : 100
D3 - System Demand : 324.098
Safety Margin : 30.120

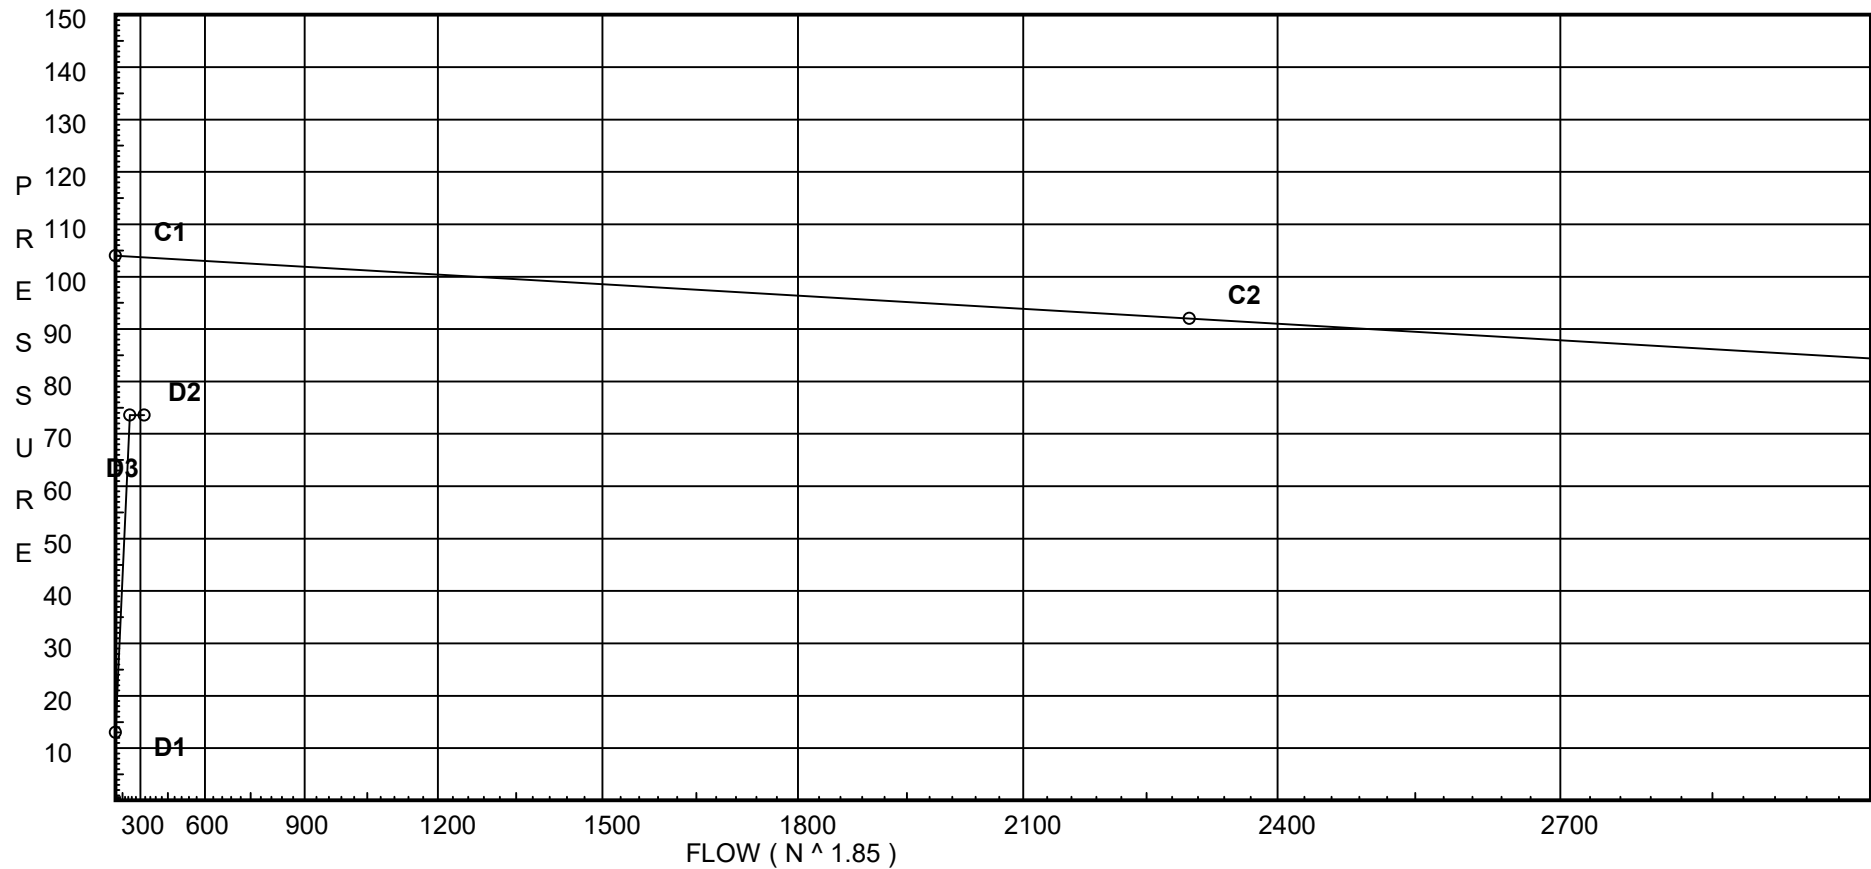

Fittings Used Summary

JAYHAWK FIRE SPRINKLER CO. INC
SLE ASC Expansion - 2nd Floor (Approval)

Page 3
Date

Fitting Legend

Abbrev.	Name	½	¾	1	1¼	1½	2	2½	3	3½	4	5	6	8	10	12	14	16	18	20	24
B	NFPA 13 Butterfly Valve	0	0	0	0	0	6	7	10	0	12	9	10	12	19	21	0	0	0	0	0
E	NFPA 13 90' Standard Elbow	1	2	2	3	4	5	6	7	8	10	12	14	18	22	27	35	40	45	50	61
G	NFPA 13 Gate Valve	0	0	0	0	0	1	1	1	1	2	2	3	4	5	6	7	8	10	11	13
T	NFPA 13 90' Flow thru Tee	3	4	5	6	8	10	12	15	17	20	25	30	35	50	60	71	81	91	101	121

Units Summary

Diameter Units	Inches
Length Units	Feet
Flow Units	US Gallons per Minute
Pressure Units	Pounds per Square Inch

Note: Fitting Legend provides equivalent pipe lengths for fittings types of various diameters. Equivalent lengths shown are standard for actual diameters of Sched 40 pipe and CFactors of 120 except as noted with *. The fittings marked with a * show equivalent lengths values supplied by manufacturers based on specific pipe diameters and CFactors and they require no adjustment. All values for fittings not marked with a * will be adjusted in the calculation for CFactors of other than 120 and diameters other than Sched 40 per NFPA.

Flow Summary - NFPA

JAYHAWK FIRE SPRINKLER CO. INC
SLE ASC Expansion - 2nd Floor (Approval)

Page 4
Date

SUPPLY ANALYSIS

<i>Node at Source</i>	<i>Static Pressure</i>	<i>Residual Pressure</i>	<i>Flow</i>	<i>Available Pressure</i>	<i>Total Demand</i>	<i>Required Pressure</i>
TEST	104.0	92	2300.0	103.68	324.1	73.56

NODE ANALYSIS

<i>Node Tag</i>	<i>Elevation</i>	<i>Node Type</i>	<i>Pressure at Node</i>	<i>Discharge at Node</i>	<i>Notes</i>	
DP05	1010.12	5.6	7.0	14.82	0.1	96
EQ05	1012.29		6.37			
DP06	1010.12	5.6	7.0	14.82	0.1	112
EQ06	1012.29		6.37			
DP02	1010.12	5.6	7.0	14.82	0.1	120
EQ02	1011.12		6.79			
DP01	1010.12	5.6	7.0	14.82	0.1	65
EQ01	1011.12		6.79			
DP04	1010.12	5.6	7.0	14.82	0.1	64
EQ04	1012.29		6.37			
DP08	1010.12	5.6	7.0	14.82	0.1	116
EQ08	1012.74		6.21			
DP07	1010.12	5.6	7.0	14.82	0.1	96
EQ07	1012.74		6.21			
DP03	1010.12	5.6	7.86	15.7	0.1	157
EQ03	1012.29		7.27			
200	1012.29	5.82	7.27	15.7	K=K @ EQ03	
201	1011.95		8.1			
202	1011.95		8.18			
203	1011.95		9.67			
204	1011.95		10.87			
205	1011.95		16.95			
206	1011.95		28.53			
207	1011.95		28.7			
208	1011.95		28.83			
2ND	995.29		54.89			
TOS	978.12		62.88			
BOS	978.12		63.5			
TTR	995.29		59.07			
TOR	995.29		61.27			
BOR	987.29		65.22			
BFS	987.29		65.9			
BFC	987.29		69.97			
SRC	982.29		73.02			
TAP	982.29		73.35			
TEST	982.29		73.56	100.0		
209	1012.29	5.87	7.25	15.81	K=K @ EQ04	
210	1011.95		8.1			
211	1011.12	5.69	9.01	17.06	K=K @ EQ02	
212	1011.95		9.58			
213	1012.29	5.87	9.85	18.42	K=K @ EQ05	
214	1012.29	5.87	15.48	23.09	K=K @ EQ05	

Flow Summary - NFPA

JAYHAWK FIRE SPRINKLER CO. INC
SLE ASC Expansion - 2nd Floor (Approval)

Page 5
Date

NODE ANALYSIS (cont.)

<i>Node Tag</i>	<i>Elevation</i>	<i>Node Type</i>	<i>Pressure at Node</i>	<i>Discharge at Node</i>	<i>Notes</i>
215	1011.12	5.69	18.78	24.64	K=K @ EQ01
216	1010.79		20.51		
217	1010.79		20.82		
218	1011.95		28.53		
219	1011.12	5.69	19.06	24.82	K=K @ EQ01
220	1012.74	5.95	20.64	27.01	K=K @ EQ07
221	1012.41		22.65		
222	1012.41		23.3		
223	1012.74	5.95	21.25	27.4	K=K @ EQ08
224	1012.29	5.87	26.37	30.14	K=K @ EQ06
225	1012.29		27.08		

Final Calculations : Hazen-Williams

JAYHAWK FIRE SPRINKLER CO. INC
SLE ASC Expansion - 2nd Floor (Approval)

Page 6
Date

Node1 to Node2	Elev1 Elev2	K Fact	Qa Qt	Nom Act	Fitting or Equiv Len	Pipe Ftngs Total	CFact Pf/Ft	Pt Pe Pf	*****	Notes	*****
DP05 to EQ05	1010.12 1012.29	5.60	14.82 14.82	1 1.049	E 2.0	2.170 2.000 4.170	120 0.0748	7.000 -0.940 0.312		Vel = 5.50	
EQ05			0.0 14.82					6.372		K Factor = 5.87	
DP06 to EQ06	1010.12 1012.29	5.60	14.82 14.82	1 1.049	E 2.0	2.170 2.000 4.170	120 0.0748	7.000 -0.940 0.312		Vel = 5.50	
EQ06			0.0 14.82					6.372		K Factor = 5.87	
DP02 to EQ02	1010.12 1011.12	5.60	14.82 14.82	1 1.049	E 2.0	1.000 2.000 3.000	120 0.0747	7.000 -0.433 0.224		Vel = 5.50	
EQ02			0.0 14.82					6.791		K Factor = 5.69	
DP01 to EQ01	1010.12 1011.12	5.60	14.82 14.82	1 1.049	E 2.0	1.000 2.000 3.000	120 0.0747	7.000 -0.433 0.224		Vel = 5.50	
EQ01			0.0 14.82					6.791		K Factor = 5.69	
DP04 to EQ04	1010.12 1012.29	5.60	14.82 14.82	1 1.049	E 2.0	2.170 2.000 4.170	120 0.0748	7.000 -0.940 0.312		Vel = 5.50	
EQ04			0.0 14.82					6.372		K Factor = 5.87	
DP08 to EQ08	1010.12 1012.74	5.60	14.82 14.82	1 1.049	E 2.0	2.620 2.000 4.620	120 0.0747	7.000 -1.135 0.345		Vel = 5.50	
EQ08			0.0 14.82					6.210		K Factor = 5.95	
DP07 to EQ07	1010.12 1012.74	5.60	14.82 14.82	1 1.049	E 2.0	2.620 2.000 4.620	120 0.0747	7.000 -1.135 0.345		Vel = 5.50	
EQ07			0.0 14.82					6.210		K Factor = 5.95	
DP03 to EQ03	1010.12 1012.29	5.60	15.70 15.7	1 1.049	E 2.0	2.170 2.000 4.170	120 0.0832	7.860 -0.940 0.347		Vel = 5.83	
EQ03			0.0 15.70					7.267		K Factor = 5.82	
200 to 201	1012.29 1011.95	5.82	15.70 15.7	1 1.049	E T 2.0 5.0	1.250 7.000 8.250	120 0.0832	7.267 0.147 0.686		K = K @ EQ03 Vel = 5.83	
201 to 202	1011.95 1011.95		0.0 15.7	1.25 1.38		3.800 3.800	120 0.0218	8.100 0.0 0.083		Vel = 3.37	
202 to 203	1011.95 1011.95		15.81 31.51	1.25 1.38	2T 12.0	6.690 12.000 18.690	120 0.0793	8.183 0.0 1.483		Vel = 6.76	

Final Calculations : Hazen-Williams

JAYHAWK FIRE SPRINKLER CO. INC
SLE ASC Expansion - 2nd Floor (Approval)

Page 7
Date

Node1 to Node2	Elev1 Elev2	K Fact	Qa Qt	Nom Act	Fitting or Eqiv	Len	Pipe Ftngs Total	CFact Pf/Ft	Pt Pe Pf	*****	Notes	*****
203 to 204	1011.95 1011.95		17.06 48.57	1.25 1.38			6.800 6.800	120 0.1768	9.666 0.0 1.202		Vel = 10.42	
204 to 205	1011.95 1011.95		18.42 66.99	1.25 1.38	2E	6.0	13.000 6.000 19.000	120 0.3203	10.868 0.0 6.086		Vel = 14.37	
205 to 206	1011.95 1011.95		23.09 90.08	1.25 1.38	2E T	6.0 6.0	8.890 12.000 20.890	120 0.5540	16.954 0.0 11.574		Vel = 19.32	
206 to 207	1011.95 1011.95		49.46 139.54	3 3.068			6.920 6.920	120 0.0254	28.528 0.0 0.176		Vel = 6.06	
207 to 208	1011.95 1011.95		30.14 169.68	3 3.068			3.430 3.430	120 0.0364	28.704 0.0 0.125		Vel = 7.36	
208 to 2ND	1011.95 995.290		54.42 224.1	3 3.068	14E	98.0	210.520 98.000 308.520	120 0.0611	28.829 7.215 18.848		Vel = 9.73	
2ND to TOS	995.290 978.120		0.0 224.1	4 4.026	T	20.0	14.167 20.000 34.167	120 0.0163	54.892 7.436 0.556		Vel = 5.65	
TOS to BOS	978.120 978.120		0.0 224.1	4 4.026	2E	20.0	17.920 20.000 37.920	120 0.0163	62.884 0.0 0.617		Vel = 5.65	
BOS to TTR	978.120 995.290		0.0 224.1	4 4.026	E	10.0	175.000 10.000 185.000	120 0.0163	63.501 -7.436 3.009		Vel = 5.65	
TTR to TOR	995.290 995.290		0.0 224.1	4 4.026	3E	30.0	104.750 30.000 134.750	120 0.0163	59.074 0.0 2.191		Vel = 5.65	
TOR to BOR	995.290 987.290		0.0 224.1	4 4.026	2E	20.0	10.000 20.000 30.000	120 0.0163	61.265 3.465 0.488		Vel = 5.65	
BOR to BFS	987.290 987.290		0.0 224.1	4 4.026	T B	20.0 12.0	10.000 32.000 42.000	120 0.0163	65.218 0.0 0.683		Vel = 5.65	
BFS to BFC	987.290 987.290		0.0 224.1	4 4.026			4.000 4.000	120 0.0162	65.901 4.000 0.065		* * Fixed Loss = 4 Vel = 5.65	
BFC to SRC	987.290 982.290		0.0 224.1	4 4.1	2E	29.067	50.000 29.067 79.067	140 0.0112	69.966 2.166 0.884		Vel = 5.45	
SRC to TAP	982.290 982.290		0.0 224.1	6 6.16	T E G	43.037 20.084 4.304	150.000 67.425 217.425	140 0.0015	73.016 0.0 0.336		Vel = 2.41	
TAP to TEST	982.290 982.290		0.0 224.1	8 8.27	T G 2E	55.354 6.326 56.936	450.000 118.616 568.616	140 0.0004	73.352 0.0 0.208		Vel = 1.34	

Final Calculations : Hazen-Williams

JAYHAWK FIRE SPRINKLER CO. INC
SLE ASC Expansion - 2nd Floor (Approval)

Page 8
Date

Node1 to Node2	Elev1 Elev2	K Fact	Qa Qt	Nom Act	Fitting or Equiv Len	Pipe Ftngs Total	CFact Pf/Ft	Pt Pe Pf	*****	Notes	*****
			100.00 324.10					73.560	Qa = 100.00 K Factor = 37.79		
209 to 210	1012.29 1011.95	5.87	15.81	1	E T 2.0 5.0	1.250 7.000 8.250	120	7.255 0.147 0.695	K = K @ EQ04		
210 to 202	1011.95 1011.95		15.81 0.0	1.049 1.25		3.910 3.910	0.0842 120	8.097 0.0	Vel = 5.87		
202			15.81	1.38		3.910	0.0220	0.086	Vel = 3.39		
			0.0 15.81					8.183	K Factor = 5.53		
211 to 212	1011.12 1011.95	5.69	17.06	1	E T 2.0 5.0	2.560 7.000 9.560	120	9.008 -0.359 0.927	K = K @ EQ02		
212 to 203	1011.95 1011.95		17.06 0.0	1.049 1.25		3.540 3.540	0.0970 120	0.927 9.576 0.0	Vel = 6.33		
203			17.06	1.38		3.540	0.0254	0.090	Vel = 3.66		
			0.0 17.06					9.666	K Factor = 5.49		
213 to 204	1012.29 1011.95	5.87	18.42	1	E T 2.0 5.0	0.830 7.000 7.830	120	9.846 0.147 0.875	K = K @ EQ05		
204			18.42	1.049		7.830	0.1117	0.875	Vel = 6.84		
			0.0 18.42					10.868	K Factor = 5.59		
214 to 205	1012.29 1011.95	5.87	23.09	1	E T 2.0 5.0	0.830 7.000 7.830	120	15.478 0.147 1.329	K = K @ EQ05		
205			23.09	1.049		7.830	0.1697	1.329	Vel = 8.57		
			0.0 23.09					16.954	K Factor = 5.61		
215 to 216	1011.12 1010.79	5.69	24.64	1	E T 2.0 5.0	1.320 7.000 8.320	120	18.778 0.143 1.592	K = K @ EQ01		
216 to 217	1010.79 1010.79		24.64 0.0	1.049 1.25		6.100 6.100	0.1913 120	1.592 20.513 0.0	Vel = 9.15		
217			24.64	1.38		6.100	0.0503	0.307	Vel = 5.29		
217 to 218	1010.79 1011.95		24.82	1.25	6E T 18.0 6.0	20.920 24.000 44.920	120	20.820 -0.502 8.208	Vel = 10.61		
218 to 206	1011.95 1011.95		0.0	3		0.500	120	28.526 0.0			
206			49.46	3.068		0.500	0.0040	0.002	Vel = 2.15		
			0.0 49.46					28.528	K Factor = 9.26		
219 to 217	1011.12 1010.79	5.69	24.82	1	E T 2.0 5.0	1.320 7.000 8.320	120	19.062 0.143 1.615	K = K @ EQ01		
217			24.82	1.049		8.320	0.1941	1.615	Vel = 9.21		
			0.0 24.82					20.820	K Factor = 5.44		

Final Calculations : Hazen-Williams

JAYHAWK FIRE SPRINKLER CO. INC
SLE ASC Expansion - 2nd Floor (Approval)

Page 9
Date

Node1 to Node2	Elev1 Elev2	K Fact	Qa Qt	Nom Act	Fitting or Equiv	Len	Pipe Ftngs Total	CFact Pf/Ft	Pt Pe Pf	*****	Notes	*****
220 to 221	1012.74 1012.41	5.95	27.01 27.01	1 1.049	E T	2.0 5.0	1.250 7.000 8.250	120 0.2269	20.638 0.143 1.872	K = K @ EQ07 Vel = 10.03		
221 to 222	1012.41 1012.41		0.0 27.01	1.25 1.38			10.910 10.910	120 0.0597	22.653 0.0 0.651	Vel = 5.79		
222 to 208	1012.41 1011.95		27.40 54.41	1.25 1.38	2E T	6.0 6.0	12.430 12.000 24.430	120 0.2180	23.304 0.199 5.326	Vel = 11.67		
208			0.0 54.41						28.829	K Factor = 10.13		
223 to 222	1012.74 1012.41	5.95	27.40 27.4	1 1.049	E T	2.0 5.0	1.220 7.000 8.220	120 0.2331	21.245 0.143 1.916	K = K @ EQ08 Vel = 10.17		
222			0.0 27.40						23.304	K Factor = 5.68		
224 to 225	1012.29 1012.29	5.87	30.14 30.14	1 1.049	E	2.0	0.540 2.000 2.540	120 0.2780	26.369 0.0 0.706	K = K @ EQ06 Vel = 11.19		
225 to 207	1012.29 1011.95		0.0 30.14	1 1.049	T	5.0	0.330 5.000 5.330	120 0.2780	27.075 0.147 1.482	Vel = 11.19		
207			0.0 30.14						28.704	K Factor = 5.63		



Hydraulic Calculations by HydraCALC

JAYHAWK FIRE SPRINKLER CO. INC
12030 S. HEDGE LANE TERRACE
OLATHE, KS 66061
913-422-3770
785-232-0975

Job Name : SLE ASC Expansion - 3rd Floor (Approval)
Drawing : FP5
Location : 100 NE SAINT LUKE'S BLVD
Remote Area : 3
Contract : 20543M
Data File : SLE ASC Expansion - 3rd Floor (Approval) Area 3.WXF

HYDRAULIC CALCULATIONS
for

JOB NAME SLE ASC Expansion
Location 100 NE SAINT LUKE'S BLVD
Drawing # FP5
Contract # 20543M
Date 02/27/2024

DESIGN

Remote area # 3
Remote area location 3RD FLR. EXAM ROOMS AND CORRIDOR
Occupancy classification LIGHT HAZARD
Density .10 - Gpm/SqFt
Area of application 1100 - SqFt
Coverage/sprinkler VARIES - SqFt
Type of sprinkler calculated VICTUALIC Q.R. PENDENT
Sprinklers calculated 12
In-rack demand NA - GPM
Hose streams 100 - GPM
Total water required (including hose streams) 307.171 - GPM @ 70.602 - Psi
Type of system WET
Volume of system (dry or pre-action) NA - Gal

WATER SUPPLY INFORMATION

Test date 12-18-2023
Location ONSITE
Source of info CITY OF LEE'S SUMMIT

CONTRACTOR INFO JAYHAWK FIRE SPRINKLER CO. INC
Address 12030 S. HEDGE LANE TERRACE / OLATHE, KS 66061 / 913-422-377
Phone # 785-232-0975
Name of designer TJA
Authority having jurisdiction CITY OF LEE'S SUMMIT / LEE'S SUMMIT FIRE DEPT.
NOTES: NA

text1(35) - invisible

Water Supply Curve

JAYHAWK FIRE SPRINKLER CO. INC
SLE ASC Expansion - 3rd Floor (Approval)


Page 2
Date

City Water Supply:

C1 - Static Pressure : 98
C2 - Residual Pressure: 90
C2 - Residual Flow : 1334

Demand:

D1 - Elevation : 19.923
D2 - System Flow : 207.171
D2 - System Pressure : 70.602
Hose (Demand) : 100
D3 - System Demand : 307.171
Safety Margin : 26.869

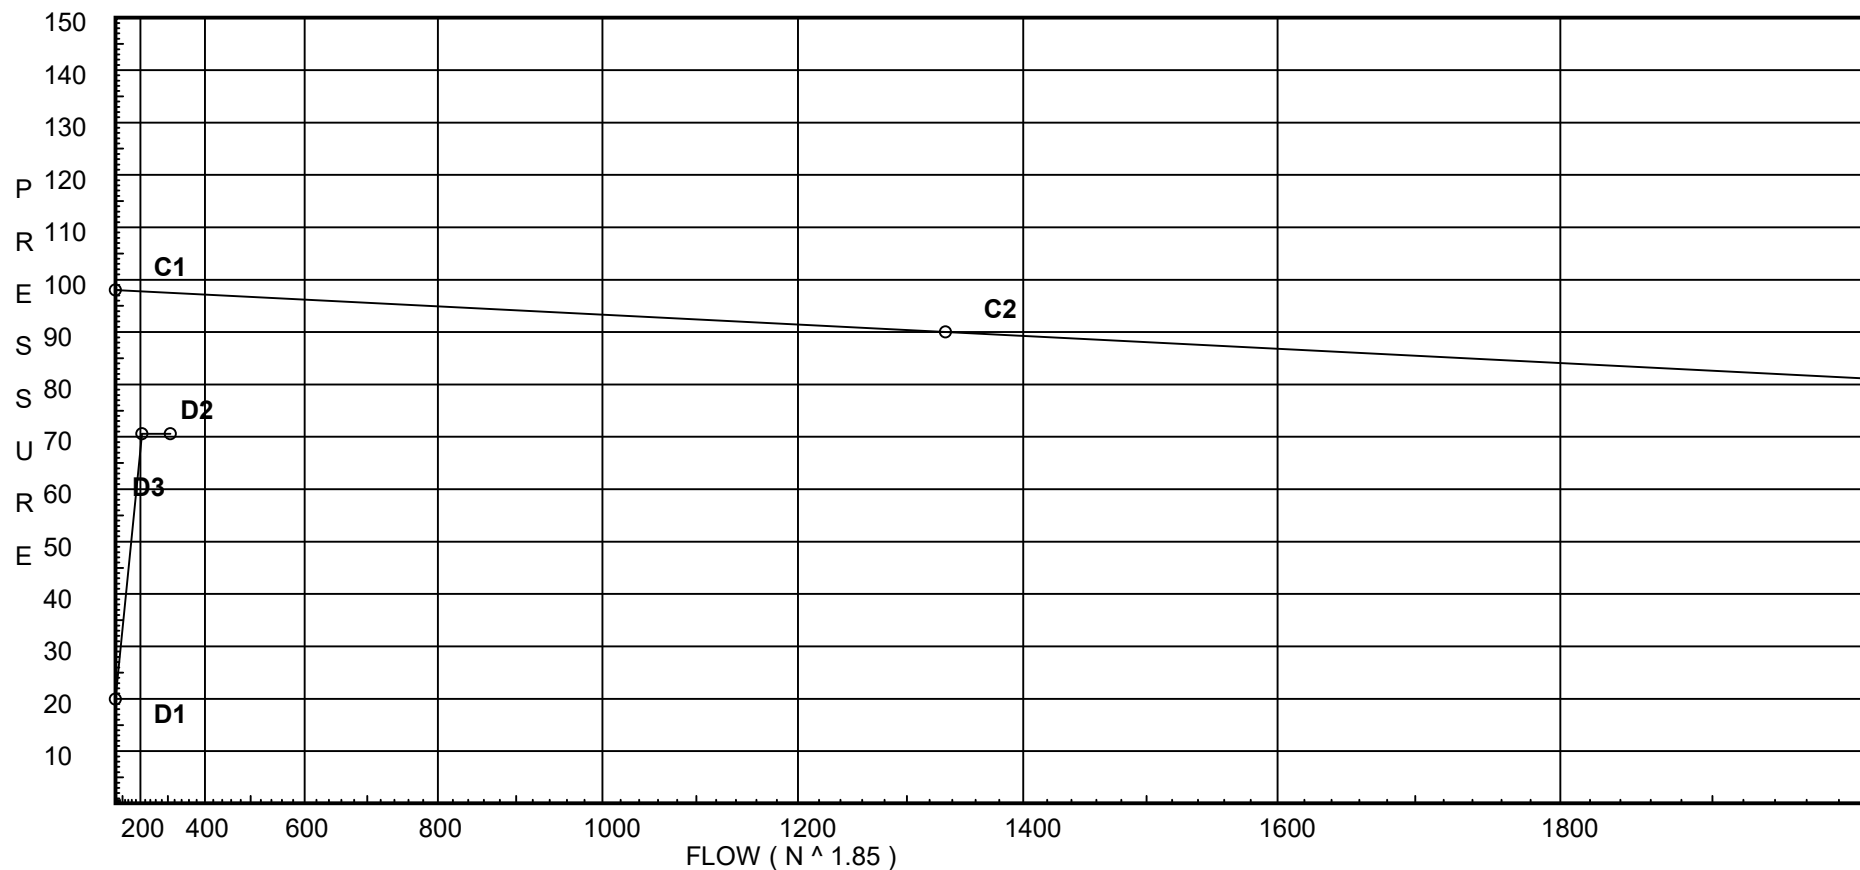

Fittings Used Summary

JAYHAWK FIRE SPRINKLER CO. INC
SLE ASC Expansion - 3rd Floor (Approval)

Page 3
Date

Fitting Legend

Abbrev.	Name	½	¾	1	1¼	1½	2	2½	3	3½	4	5	6	8	10	12	14	16	18	20	24
B	NFPA 13 Butterfly Valve	0	0	0	0	0	6	7	10	0	12	9	10	12	19	21	0	0	0	0	0
E	NFPA 13 90' Standard Elbow	1	2	2	3	4	5	6	7	8	10	12	14	18	22	27	35	40	45	50	61
Fsp	Flow Switch Potter VSR	Fitting generates a Fixed Loss Based on Flow																			
G	NFPA 13 Gate Valve	0	0	0	0	0	1	1	1	1	2	2	3	4	5	6	7	8	10	11	13
S	NFPA 13 Swing Check	0	0	5	7	9	11	14	16	19	22	27	32	45	55	65					
T	NFPA 13 90' Flow thru Tee	3	4	5	6	8	10	12	15	17	20	25	30	35	50	60	71	81	91	101	121

Units Summary

Diameter Units	Inches
Length Units	Feet
Flow Units	US Gallons per Minute
Pressure Units	Pounds per Square Inch

Note: Fitting Legend provides equivalent pipe lengths for fittings types of various diameters. Equivalent lengths shown are standard for actual diameters of Sched 40 pipe and CFactors of 120 except as noted with *. The fittings marked with a * show equivalent lengths values supplied by manufacturers based on specific pipe diameters and CFactors and they require no adjustment. All values for fittings not marked with a * will be adjusted in the calculation for CFactors of other than 120 and diameters other than Sched 40 per NFPA.

Flow Summary - NFPA

JAYHAWK FIRE SPRINKLER CO. INC
SLE ASC Expansion - 3rd Floor (Approval)

Page 4
Date

SUPPLY ANALYSIS

<i>Node at Source</i>	<i>Static Pressure</i>	<i>Residual Pressure</i>	<i>Flow</i>	<i>Available Pressure</i>	<i>Total Demand</i>	<i>Required Pressure</i>
TEST	98.0	90	1334.0	97.471	307.17	70.602

NODE ANALYSIS

<i>Node Tag</i>	<i>Elevation</i>	<i>Node Type</i>	<i>Pressure at Node</i>	<i>Discharge at Node</i>	<i>Notes</i>	
DP08	1026.12	5.6	7.0	14.82	0.1	114
EQ08	1028.29		6.37			
DP07	1026.12	5.6	8.16	16.0	0.1	160
EQ07	1028.29		7.58			
DP02	1026.12	5.6	7.0	14.82	0.1	112
EQ02	1028.37		6.34			
DP10	1026.12	5.6	7.0	14.82	0.1	126
EQ10	1028.29		6.37			
DP06	1026.12	5.6	7.0	14.82	0.1	70
EQ06	1028.29		6.37			
DP03	1026.12	5.6	7.0	14.82	0.1	65
EQ03	1028.37		6.34			
DP05	1026.12	5.6	11.15	18.7	0.1	187
EQ05	1028.29		10.69			
DP04	1026.12	5.6	7.0	14.82	0.1	110
EQ04	1028.37		6.34			
DP01	1026.12	5.6	7.0	14.82	0.1	109
EQ01	1028.37		6.34			
DP09	1026.12	5.6	7.0	14.82	0.1	84
EQ09	1028.29		6.37			
300	1028.29	5.72	10.74	18.74	K=K @ EQ05	
301	1027.95		11.82			
302	1027.95		11.95			
303	1027.95		15.28			
304	1027.45		16.04			
305	1027.45		16.55			
306	1027.45		17.03			
307	1027.45		17.37			
308A	1027.45		18.3			
308	1027.45		19.23			
309	1027.45		19.75			
310	1027.45		20.56			
311	1027.45		21.52			
312	1027.45		21.9			
313	1027.45		23.14			
314	1027.45		23.68			
315	1027.45		24.07			
316	1027.45		24.99			
317	1026.79		30.16			
318	1026.79		30.58			
3RD	995.29		53.16			
TOS	978.12		61.07			

Flow Summary - NFPA

JAYHAWK FIRE SPRINKLER CO. INC
SLE ASC Expansion - 3rd Floor (Approval)

Page 5
Date

NODE ANALYSIS (cont.)

Node Tag	Elevation	Node Type	Pressure at Node	Discharge at Node	Notes
BOS	978.12		61.61		
TTR	995.29		56.77		
TOR	995.29		58.67		
BOR	987.29		62.55		
BFS	987.29		63.14		
BFC	987.29		67.2		
SRC	982.29		70.13		
TAP	982.29		70.42		
TEST	982.29		70.6	100.0	
319	1028.29	5.72	10.86	18.85	K=K @ EQ05
320	1028.29	5.72	10.92	18.9	K=K @ EQ05
321	1027.95		11.96		
322	1027.95		14.87		
323	1026.95		15.73		
324	1027.95		15.86		
325	1027.95		16.41		
326	1027.95		16.85		
327	1027.95		17.21		
328A	1027.95		18.35		
328	1027.95		18.83		
329	1027.95		19.32		
330	1027.95		19.83		
331	1027.95		21.05		
332	1027.95		21.46		
333	1027.95		21.74		
334	1027.95		22.07		
335	1027.95		22.32		
336	1027.95		22.45		
337	1027.95		22.48		
338	1027.79		29.68		
339	1027.95		15.23		
340	1027.95		9.07		
341	1027.95		8.6		
342	1027.95		8.45		
343	1027.95		8.49		
344	1027.95		9.3		
345	1027.95		14.42		
346	1026.95		15.69		
347	1028.29	5.87	7.48	16.05	K=K @ EQ08
348	1028.29	5.81	7.58	16.0	K=K @ EQ07
349	1028.29	5.87	7.75	16.34	K=K @ EQ09
350	1028.29	5.87	8.28	16.89	K=K @ EQ06
351	1028.29	5.87	8.18	16.79	K=K @ EQ10
352	1028.37	5.88	8.27	16.91	K=K @ EQ02
353	1028.04		9.28		
354	1028.04		9.57		
355	1028.37	5.88	8.37	17.02	K=K @ EQ03
356	1028.04		9.28		
357	1028.04		9.65		
358	1028.37	5.88	8.64	17.3	K=K @ EQ01
359	1028.37	5.88	8.73	17.38	K=K @ EQ04

Flow Summary - NFPA

JAYHAWK FIRE SPRINKLER CO. INC
SLE ASC Expansion - 3rd Floor (Approval)

Page 6
Date

NODE ANALYSIS (cont.)

<i>Node Tag</i>	<i>Elevation</i>	<i>Node Type</i>	<i>Pressure at Node</i>	<i>Discharge at Node</i>	<i>Notes</i>
360	1027.95		22.9		
361	1027.95		29.24		

Final Calculations : Hazen-Williams

JAYHAWK FIRE SPRINKLER CO. INC
SLE ASC Expansion - 3rd Floor (Approval)

Page 7
Date

Node1 to Node2	Elev1 Elev2	K Fact	Qa Qt	Nom Act	Fitting or Eqiv	Len	Pipe Ftngs Total	CFact Pf/Ft	Pt Pe Pf	*****	Notes	*****
DP08 to EQ08	1026.12 1028.29	5.60	14.82 14.82	1 1.049	E	2.0	2.170 2.000 4.170	120 0.0748	7.000 -0.940 0.312		Vel = 5.50	
EQ08			0.0 14.82						6.372		K Factor = 5.87	
DP07 to EQ07	1026.12 1028.29	5.60	16.00 16.0	1 1.049	E	2.0	2.170 2.000 4.170	120 0.0863	8.163 -0.940 0.360		Vel = 5.94	
EQ07			0.0 16.00						7.583		K Factor = 5.81	
DP02 to EQ02	1026.12 1028.37	5.60	14.82 14.82	1 1.049	E	2.0	2.250 2.000 4.250	120 0.0746	7.000 -0.974 0.317		Vel = 5.50	
EQ02			0.0 14.82						6.343		K Factor = 5.88	
DP10 to EQ10	1026.12 1028.29	5.60	14.82 14.82	1 1.049	E	2.0	2.170 2.000 4.170	120 0.0748	7.000 -0.940 0.312		Vel = 5.50	
EQ10			0.0 14.82						6.372		K Factor = 5.87	
DP06 to EQ06	1026.12 1028.29	5.60	14.82 14.82	1 1.049	E	2.0	2.170 2.000 4.170	120 0.0748	7.000 -0.940 0.312		Vel = 5.50	
EQ06			0.0 14.82						6.372		K Factor = 5.87	
DP03 to EQ03	1026.12 1028.37	5.60	14.82 14.82	1 1.049	E	2.0	2.250 2.000 4.250	120 0.0746	7.000 -0.974 0.317		Vel = 5.50	
EQ03			0.0 14.82						6.343		K Factor = 5.88	
DP05 to EQ05	1026.12 1028.29	5.60	18.70 18.7	1 1.049	E	2.0	2.170 2.000 4.170	120 0.1149	11.151 -0.940 0.479		Vel = 6.94	
EQ05			0.0 18.70						10.690		K Factor = 5.72	
DP04 to EQ04	1026.12 1028.37	5.60	14.82 14.82	1 1.049	E	2.0	2.250 2.000 4.250	120 0.0746	7.000 -0.974 0.317		Vel = 5.50	
EQ04			0.0 14.82						6.343		K Factor = 5.88	
DP01 to EQ01	1026.12 1028.37	5.60	14.82 14.82	1 1.049	E	2.0	2.250 2.000 4.250	120 0.0746	7.000 -0.974 0.317		Vel = 5.50	
EQ01			0.0 14.82						6.343		K Factor = 5.88	
DP09 to EQ09	1026.12 1028.29	5.60	14.82 14.82	1 1.049	E	2.0	2.170 2.000 4.170	120 0.0748	7.000 -0.940 0.312		Vel = 5.50	

Final Calculations : Hazen-Williams

JAYHAWK FIRE SPRINKLER CO. INC
SLE ASC Expansion - 3rd Floor (Approval)

Page 8
Date

Node1 to Node2	Elev1 Elev2	K Fact	Qa Qt	Nom Act	Fitting or Equiv	Len	Pipe Ftngs Total	CFact Pf/Ft	Pt Pe Pf	*****	Notes	*****
EQ09			0.0 14.82						6.372		K Factor = 5.87	
300 to 301	1028.29 1027.95	5.72	18.74	1	E T	2.0 5.0	1.080 7.000 8.080	120	10.736 0.147 0.932		K = K @ EQ05	
301 to 302	1027.95 1027.95		18.74	1.049			14.000	120	11.815 0.0		Vel = 6.96	
302 to 303	1027.95 1027.95		-8.50	1.25			14.000	120	0.0099 0.139		Vel = 2.20	
303 to 304	1027.95 1027.45		18.85	1.25	T	6.0	42.650 6.000 48.650	120	11.954 0.0		Vel = 6.24	
304 to 305	1027.95 1027.45		29.09	1.38			13.100 12.000 25.100	120	15.283 0.217 0.540		Vel = 4.82	
305 to 306	1027.45 1027.45		71.97	2.469	2E	12.0	11.880	120	16.040 0.0		Vel = 7.04	
306 to 307	1027.45 1027.45		33.08	2.5			11.880	120	0.0433 0.514		Vel = 6.90	
307 to 308A	1027.45 1027.450		105.05	2.469			11.420	120	16.554 0.0		Vel = 6.81	
308A to 309	1027.450 1027.45		-2.07	2.5			8.250	120	17.031 0.0		Vel = 6.68	
309 to 310	1027.45 1027.45		101.59	2.469			8.250	120	0.0407 0.336		Vel = 6.39	
310 to 311	1027.45 1027.45		-1.88	2.5	2E	12.0	11.730 12.000 23.730	120	17.367 0.0		Vel = 6.61	
311 to 312	1027.45 1027.45		99.71	2.469			13.750 12.000 25.750	120	18.300 0.0		Vel = 6.85	
312 to 313	1027.45 1027.45		-4.31	2.5	2E	12.0	13.350	120	19.234 0.0		Vel = 7.22	
313 to 314	1027.45 1027.45		95.4	2.469			13.350	120	0.0363 0.934		Vel = 7.49	
314 to 315	1027.45 1027.45		3.28	2.5			19.770	120	20.562 0.0		Vel = 7.76	
315 to 316	1027.45 1027.45		102.15	2.469			9.170 12.000 21.170	120	21.522 0.0		Vel = 7.87	
316 to 317	1027.45 1027.45		5.52	2.5	2E	12.0	7.830	120	21.902 0.0		Vel = 8.55	
317 to 318	1027.45 1027.45		107.67	2.469			7.830	120	0.0485 0.380			
318 to 319	1027.45 1027.45		4.15	2.5			11.890 12.000 23.890	120	21.902 0.0			
319 to 320	1027.45 1027.45		111.82	2.469			10.170	120	23.140 0.0			
320 to 321	1027.45 1027.45		3.91	2.5	2E	12.0	6.200	120	23.682 0.0			
321 to 322	1027.45 1027.45		115.73	2.469			6.200	120	0.0621 0.385			

Final Calculations : Hazen-Williams

JAYHAWK FIRE SPRINKLER CO. INC
SLE ASC Expansion - 3rd Floor (Approval)

Page 9
Date

Node1 to Node2	Elev1 Elev2	K Fact	Qa Qt	Nom Act	Fitting or Eqiv	Len	Pipe Ftngs Total	CFact Pf/Ft	Pt Pe Pf	*****	Notes	*****
315 to 316	1027.45 1027.45		11.05 138.57	2.5 2.469			12.820 12.820	120 0.0723	24.067 0.0 0.927		Vel = 9.29	
316 to 317	1027.45 1026.79		13.38 151.95	2.5 2.469	3E	18.0	38.950 18.000 56.950	120 0.0857	24.994 0.286 4.883		Vel = 10.18	
317 to 318	1026.79 1026.79		26.78 178.73	2.5 2.469			3.560 3.560	120 0.1157	30.163 0.0 0.412		Vel = 11.98	
318 to 3RD	1026.79 995.290		28.44 207.17	2.5 2.469	E B S Fsp	6.0 7.0 14.0 0.0	12.030 27.000 39.030	120 0.1521	30.575 16.643 5.938		* * Fixed Loss = 3 Vel = 13.88	
3RD to TOS	995.290 978.120		0.0 207.17	4 4.026	T	20.0	14.167 20.000 34.167	120 0.0141	53.156 7.436 0.481		Vel = 5.22	
TOS to BOS	978.120 978.120		0.0 207.17	4 4.026	2E	20.0	17.920 20.000 37.920	120 0.0141	61.073 0.0 0.533		Vel = 5.22	
BOS to TTR	978.120 995.290		0.0 207.17	4 4.026	E	10.0	175.000 10.000 185.000	120 0.0141	61.606 -7.436 2.602		Vel = 5.22	
TTR to TOR	995.290 995.290		0.0 207.17	4 4.026	3E	30.0	104.750 30.000 134.750	120 0.0141	56.772 0.0 1.895		Vel = 5.22	
TOR to BOR	995.290 987.290		0.0 207.17	4 4.026	2E	20.0	10.000 20.000 30.000	120 0.0141	58.667 3.465 0.422		Vel = 5.22	
BOR to BFS	987.290 987.290		0.0 207.17	4 4.026	T B	20.0 12.0	10.000 32.000 42.000	120 0.0141	62.554 0.0 0.591		Vel = 5.22	
BFS to BFC	987.290 987.290		0.0 207.17	4 4.026			4.000 4.000	120 0.0140	63.145 4.000 0.056		* * Fixed Loss = 4 Vel = 5.22	
BFC to SRC	987.290 982.290		0.0 207.17	4 4.1	2E	29.067	50.000 29.067 79.067	140 0.0097	67.201 2.166 0.765		Vel = 5.03	
SRC to TAP	982.290 982.290		0.0 207.17	6 6.16	T E G	43.037 20.084 4.304	150.000 67.425 217.425	140 0.0013	70.132 0.0 0.289		Vel = 2.23	
TAP to TEST	982.290 982.290		0.0 207.17	8 8.27	T G 2E	55.354 6.326 56.936	450.000 118.616 568.616	140 0.0003	70.421 0.0 0.181		Vel = 1.24	
TEST			100.00 307.17						70.602		Qa = 100.00 K Factor = 36.56	
319 to 302	1028.29 1027.95	5.72	18.85 18.85	1 1.049	E T	2.0 5.0	1.080 7.000 8.080	120 0.1167	10.864 0.147 0.943		K = K @ EQ05 Vel = 7.00	

Final Calculations : Hazen-Williams

JAYHAWK FIRE SPRINKLER CO. INC
SLE ASC Expansion - 3rd Floor (Approval)

Page 10
Date

Node1 to Node2	Elev1 Elev2	K Fact	Qa Qt	Nom Act	Fitting or Equiv Len	Pipe Ftngs Total	CFact Pf/Ft	Pt Pe Pf	*****	Notes	*****
302			0.0 18.85					11.954		K Factor = 5.45	
320 to 321	1028.29 1027.95	5.72	18.90	1	E T 2.0 5.0	0.660 7.000 7.660	120	10.918 0.147 0.898		K = K @ EQ05	
321 to 322	1027.95 1027.95		18.9	1.049			0.1172	0.898		Vel = 7.02	
321 to 322	1027.95 1027.95		8.50	1.25	3E 9.0	38.390 9.000 47.390	120	11.963 0.0			
322 to 323	1027.95 1026.95		27.4	1.38			0.0613	2.905		Vel = 5.88	
322 to 323	1027.95 1026.95		0.0	1.25	T 6.0	1.000 6.000 7.000	120	14.868 0.433 0.429			
323 to 324	1026.95 1027.95		39.19	2.5	3E 18.0	12.160 18.000 30.160	120	15.730 -0.433 0.562		Vel = 4.46	
324 to 325	1027.95 1027.95		66.59	2.469			0.0186	0.562			
324 to 325	1027.95 1027.95		35.53	2.5		13.500	120	15.859 0.0			
325 to 326	1027.95 1027.95		102.12	2.469		13.500	0.0411	0.555		Vel = 6.84	
325 to 326	1027.95 1027.95		2.07	2.5		10.260	120	16.414 0.0			
326 to 327	1027.95 1027.95		104.19	2.469		10.260	0.0427	0.438		Vel = 6.98	
326 to 327	1027.95 1027.95		1.39	2.5		8.170	120	16.852 0.0			
327 to 328	1027.95 1027.95		105.58	2.469		8.170	0.0437	0.357		Vel = 7.08	
327 to 328A	1027.95 1027.950		1.88	2.5	2E 12.0	13.203 12.000 25.203	120	17.209 0.0 1.138			
328A to 328	1027.950 1027.95		107.46	2.469			0.0452	1.138		Vel = 7.20	
328A to 328	1027.950 1027.95		4.31	2.5		9.917	120	18.347 0.0			
328 to 329	1027.95 1027.95		111.77	2.469		9.917	0.0486	0.482		Vel = 7.49	
328 to 329	1027.95 1027.95		-3.28	2.5		10.770	120	18.829 0.0			
329 to 330	1027.95 1027.95		108.49	2.469		10.770	0.0460	0.495		Vel = 7.27	
329 to 330	1027.95 1027.95		-3.47	2.5		11.720	120	19.324 0.0			
330 to 331	1027.95 1027.95		105.02	2.469		11.720	0.0433	0.508		Vel = 7.04	
330 to 331	1027.95 1027.95		-5.52	2.5	4E 24.0	7.070 24.000 31.070	120	19.832 0.0 1.217			
331 to 332	1027.95 1027.95		99.5	2.469			0.0392	1.217		Vel = 6.67	
331 to 332	1027.95 1027.95		-4.15	2.5		11.380	120	21.049 0.0			
332 to 333	1027.95 1027.95		95.35	2.469		11.380	0.0362	0.412		Vel = 6.39	
332 to 333	1027.95 1027.95		-3.91	2.5		8.320	120	21.461 0.0			
333 to 334	1027.95 1027.95		91.44	2.469		8.320	0.0335	0.279		Vel = 6.13	
333 to 334	1027.95 1027.95		-11.79	2.5		12.800	120	21.740 0.0			
334 to 335	1027.95 1027.95		79.65	2.469		12.800	0.0259	0.332		Vel = 5.34	
334 to 335	1027.95 1027.95		-11.05	2.5		12.620	120	22.072 0.0			
335	1027.95		68.6	2.469		12.620	0.0197	0.249		Vel = 4.60	

Final Calculations : Hazen-Williams

JAYHAWK FIRE SPRINKLER CO. INC
SLE ASC Expansion - 3rd Floor (Approval)

Page 11
Date

Node1 to Node2	Elev1 Elev2	K Fact	Qa Qt	Nom Act	Fitting or Equiv	Len	Pipe Ftngs Total	CFact Pf/Ft	Pt Pe Pf	*****	Notes	*****
335 to 336	1027.95 1027.95		-13.38 55.22	2.5 2.469			9.750 9.750	120 0.0131	22.321 0.0 0.128		Vel = 3.70	
336 to 337	1027.95 1027.95		-26.78 28.44	2.5 2.469			8.220 8.220	120 0.0039	22.449 0.0 0.032		Vel = 1.91	
337 to 338	1027.95 1027.79		0.0 28.44	1.25 1.38	T 6E	6.0 18.0	84.610 24.000 108.610	120 0.0657	22.481 0.069 7.132		Vel = 6.10	
338 to 318	1027.79 1026.79		0.0 28.44	1.25 1.38	T	6.0	1.000 6.000 7.000	120 0.0657	29.682 0.433 0.460		Vel = 6.10	
318			0.0 28.44						30.575		K Factor = 5.14	
301 to 321	1027.95 1027.95		8.50 8.5	1.25 1.38	2E	6.0	15.090 6.000 21.090	120 0.0070	11.815 0.0 0.148		Vel = 1.82	
321			0.0 8.50						11.963		K Factor = 2.46	
303 to 339	1027.95 1027.95		-42.89 -42.89	2.5 2.469			6.310 6.310	120 -0.0082	15.283 0.0 -0.052		Vel = 2.87	
339 to 340	1027.95 1027.95		0.0 -42.89	1.25 1.38	T	6.0	37.900 6.000 43.900	120 -0.1403	15.231 0.0 -6.161		Vel = 9.20	
340 to 341	1027.95 1027.95		16.80 -26.09	1.25 1.38			8.420 8.420	120 -0.0561	9.070 0.0 -0.472		Vel = 5.60	
341 to 342	1027.95 1027.95		16.34 -9.75	1.25 1.38	2E	6.0	10.590 6.000 16.590	120 -0.0090	8.598 0.0 -0.150		Vel = 2.09	
342 to 343	1027.95 1027.95		16.05 6.3	1.25 1.38			10.050 10.050	120 0.0041	8.448 0.0 0.041		Vel = 1.35	
343 to 344	1027.95 1027.95		16.00 22.3	1.25 1.38	2E	6.0	13.350 6.000 19.350	120 0.0419	8.489 0.0 0.810		Vel = 4.78	
344 to 345	1027.95 1027.95		16.89 39.19	1.25 1.38	3E	9.0	34.140 9.000 43.140	120 0.1188	9.299 0.0 5.123		Vel = 8.41	
345 to 346	1027.95 1026.95		0.0 39.19	1.25 1.38	T	6.0	1.000 6.000 7.000	120 0.1189	14.422 0.433 0.832		Vel = 8.41	
346 to 323	1026.95 1026.95		0.0 39.19	2.5 2.469			6.120 6.120	120 0.0070	15.687 0.0 0.043		Vel = 2.63	
323			0.0 39.19						15.730		K Factor = 9.88	

Final Calculations : Hazen-Williams

JAYHAWK FIRE SPRINKLER CO. INC
SLE ASC Expansion - 3rd Floor (Approval)

Page 12
Date

Node1 to Node2	Elev1 Elev2	K Fact	Qa Qt	Nom Act	Fitting or Equiv Len	Pipe Ftngs Total	CFact Pf/Ft	Pt Pe Pf	*****	Notes	*****
347 to 342	1028.29 1027.95	5.87	16.05 16.05	1 1.049	E T 2.0 5.0	2.460 7.000 9.460	120 0.0867	7.481 0.147 0.820	K = K @ EQ08 Vel = 5.96		
342			0.0 16.05					8.448	K Factor = 5.52		
348 to 343	1028.29 1027.95	5.81	16.00 16.0	1 1.049	E T 2.0 5.0	1.810 7.000 8.810	120 0.0862	7.583 0.147 0.759	K = K @ EQ07 Vel = 5.94		
343			0.0 16.00					8.489	K Factor = 5.49		
349 to 341	1028.29 1027.95	5.87	16.34 16.34	1 1.049	E T 2.0 5.0	0.840 7.000 7.840	120 0.0895	7.749 0.147 0.702	K = K @ EQ09 Vel = 6.07		
341			0.0 16.34					8.598	K Factor = 5.57		
350 to 344	1028.29 1027.95	5.87	16.89 16.89	1 1.049	E T 2.0 5.0	2.200 7.000 9.200	120 0.0952	8.276 0.147 0.876	K = K @ EQ06 Vel = 6.27		
344			0.0 16.89					9.299	K Factor = 5.54		
351 to 340	1028.29 1027.95	5.87	16.79 16.79	1 1.049	E T 2.0 5.0	0.840 7.000 7.840	120 0.0943	8.184 0.147 0.739	K = K @ EQ10 Vel = 6.23		
340			0.0 16.79					9.070	K Factor = 5.58		
352 to 353	1028.37 1028.04	5.88	16.92 16.92	1 1.049	E T 2.0 5.0	2.110 7.000 9.110	120 0.0955	8.267 0.143 0.870	K = K @ EQ02 Vel = 6.28		
353 to 354	1028.04 1028.04		-1.14 15.78	1.25 1.38		12.920 12.920	120 0.0221	9.280 0.0	Vel = 3.38		
354 to 304	1028.04 1027.45		17.30 33.08	1.25 1.38	9E T 27.0 6.0	38.650 33.000 71.650	120 0.0868	9.565 0.256 6.219	Vel = 7.10		
304			0.0 33.08					16.040	K Factor = 8.26		
355 to 356	1028.37 1028.04	5.88	17.02 17.02	1 1.049	E T 2.0 5.0	0.950 7.000 7.950	120 0.0965	8.370 0.143 0.767	K = K @ EQ03 Vel = 6.32		
356 to 357	1028.04 1028.04		1.13 18.15	1.25 1.38		13.080 13.080	120 0.0287	9.280 0.0 0.375	Vel = 3.89		
357 to 324	1028.04 1027.95		17.38 35.53	1.25 1.38	5E T 15.0 6.0	41.200 21.000 62.200	120 0.0991	9.655 0.039 6.165	Vel = 7.62		
324			0.0 35.53					15.859	K Factor = 8.92		

Final Calculations : Hazen-Williams

JAYHAWK FIRE SPRINKLER CO. INC
SLE ASC Expansion - 3rd Floor (Approval)

Page 13
Date

Node1 to Node2	Elev1 Elev2	K Fact	Qa Qt	Nom Act	Fitting or Equiv Len	Pipe Ftngs Total	CFact Pf/Ft	Pt Pe Pf	*****	Notes	*****
358 to 354	1028.37 1028.04	5.88	17.30 17.3	1 1.049	E T 2.0 5.0	0.830 7.000 7.830	120 0.0995	8.643 0.143 0.779	K = K @ EQ01 Vel = 6.42		
354			0.0 17.30					9.565	K Factor = 5.59		
359 to 357	1028.37 1028.04	5.88	17.38 17.38	1 1.049	E T 2.0 5.0	0.810 7.000 7.810	120 0.1004	8.728 0.143 0.784	K = K @ EQ04 Vel = 6.45		
357			0.0 17.38					9.655	K Factor = 5.59		
353 to 356	1028.04 1028.04		1.14 1.14	1.25 1.38		3.990 3.990	120 0	9.280 0.0 0.0	Vel = 0.24		
356			0.0 1.14					9.280	K Factor = 0.37		
325 to 305	1027.95 1027.45		-2.07 -2.07	1.25 1.38	2T 8E 12.0 24.0	111.940 36.000 147.940	120 -0.0005	16.414 0.217 -0.077	Vel = 0.44		
305			0.0 -2.07					16.554	K Factor = -0.51		
326 to 306	1027.95 1027.45		-1.39 -1.39	1.25 1.38	2T 9E 12.0 27.0	110.070 39.000 149.070	120 -0.0003	16.852 0.217 -0.038	Vel = 0.30		
306			0.0 -1.39					17.031	K Factor = -0.34		
327 to 307	1027.95 1027.45		-1.87 -1.87	1.25 1.38	2T 6E 12.0 18.0	106.140 30.000 136.140	120 -0.0004	17.209 0.217 -0.059	Vel = 0.40		
307			0.0 -1.87					17.367	K Factor = -0.45		
328 to 308	1027.95 1027.45		3.28 3.28	1.25 1.38	2T 11E 12.0 33.0	110.950 45.000 155.950	120 0.0012	18.829 0.217 0.188	Vel = 0.70		
308			0.0 3.28					19.234	K Factor = 0.75		
329 to 309	1027.95 1027.45		3.48 3.48	1.25 1.38	2T 10E 12.0 30.0	112.740 42.000 154.740	120 0.0013	19.324 0.217 0.208	Vel = 0.75		
309			0.0 3.48					19.749	K Factor = 0.78		
330 to 310	1027.95 1027.45		5.52 5.52	1.25 1.38	2T 12E 12.0 36.0	114.730 48.000 162.730	120 0.0032	19.832 0.217 0.513	Vel = 1.18		
310			0.0 5.52					20.562	K Factor = 1.22		
331 to 311	1027.95 1027.45		4.15 4.15	1.25 1.38	6E 2T 18.0 12.0	107.460 30.000 137.460	120 0.0019	21.049 0.217 0.256	Vel = 0.89		

Final Calculations : Hazen-Williams

JAYHAWK FIRE SPRINKLER CO. INC
SLE ASC Expansion - 3rd Floor (Approval)

Page 14
Date

Node1 to Node2	Elev1 Elev2	K Fact	Qa Qt	Nom Act	Fitting or Equiv	Len	Pipe Ftngs Total	CFact Pf/Ft	Pt Pe Pf	*****	Notes	*****
311			0.0 4.15						21.522		K Factor = 0.89	
332 to 312	1027.95 1027.45		3.92 3.92	1.25 1.38	2T 4E	12.0 12.0	110.300 24.000 134.300	120 0.0017	21.461 0.217 0.224		Vel = 0.84	
312			0.0 3.92						21.902		K Factor = 0.84	
333 to 360	1027.95 1027.95		11.79 11.79	1.25 1.38	2T 2E	12.0 6.0	72.330 18.000 90.330	120 0.0129	21.740 0.0 1.162		Vel = 2.53	
360 to 313	1027.95 1027.45		-10.04 1.75	1.25 1.38	3E T	9.0 6.0	42.060 15.000 57.060	120 0.0004	22.902 0.217 0.021		Vel = 0.38	
313			0.0 1.75						23.140		K Factor = 0.36	
360 to 314	1027.95 1027.45		10.03 10.03	1.25 1.38	3E T	9.0 6.0	44.000 15.000 59.000	120 0.0095	22.902 0.217 0.563		Vel = 2.15	
314			0.0 10.03						23.682		K Factor = 2.06	
334 to 315	1027.95 1027.45		11.05 11.05	1.25 1.38	2T 10E	12.0 30.0	113.820 42.000 155.820	120 0.0114	22.072 0.217 1.778		Vel = 2.37	
315			0.0 11.05						24.067		K Factor = 2.25	
335 to 316	1027.95 1027.45		13.38 13.38	1.25 1.38	2T 8E	12.0 24.0	114.880 36.000 150.880	120 0.0163	22.321 0.217 2.456		Vel = 2.87	
316			0.0 13.38						24.994		K Factor = 2.68	
336 to 361	1027.95 1027.95		26.77 26.77	1.25 1.38	T 8E	6.0 24.0	85.660 30.000 115.660	120 0.0587	22.449 0.0 6.791		Vel = 5.74	
361 to 317	1027.95 1026.79		0.0 26.77	1.25 1.38	T	6.0	1.170 6.000 7.170	120 0.0587	29.240 0.502 0.421		Vel = 5.74	
317			0.0 26.77						30.163		K Factor = 4.87	
328A to 308A	1027.950 1027.450		-4.32 -4.32	1.25 1.38	7E	21.0	110.250 21.000 131.250	120 -0.0020	18.347 0.217 -0.264		Vel = 0.93	
308A			0.0 -4.32						18.300		K Factor = -1.01	



Hydraulic Calculations by HydraCALC

JAYHAWK FIRE SPRINKLER CO. INC
12030 S. HEDGE LANE TERRACE
OLATHE, KS 66061
913-422-3770
785-232-0975

Job Name : STANDPIPE UPGRADE FROM 4 TO 6
Drawing : BUILDING E - EXPANSION
Location : 100 NE SAINT LUKE'S BLVD. - BUILDING E EXPANSION
Remote Area :
Contract : 20543KM
Data File : STANDPIPE CALC - Upgrade to 6inch Area 4.WXF

HYDRAULIC DESIGN INFORMATION SHEET

Name - STANDPIPE UPGRADE FROM 4 TO 6 Date - 02/27/2024
Location - 100 NE SAINT LUKE'S BLVD. - BUILDING E EXPANSION
Building - BUILDING E - EXPANSION System No. -
Contractor - JAYHAWK FIRE SPRINKLER CO., INC. Contract No. - 20543KM
Calculated By - TJA Drawing No. - FP1 & FP6
Occupancy - LIGHT HAZARD

S (X)NFPA 14 Number of Standpipes ()1 (X)2 ()3 ()4 ()
Y ()Other
S ()Specific Ruling Made by Date

T
E Flow at Top Most Outlet - 500 Gpm System Type
M Pres. at Top Most Outlet - 100 Psi (X) Wet () Dry
Flow For Ea. Additional Standpipe - 250 Gpm
D Total Additional Flow - Gpm
E Elevation at Highest Outlet - 52 Feet
S Hose Valve Connection ()1 1/2" (X)2 1/2"
I Class Service ()I ()II (X)III
G Note:
N

Calculation Gpm Required 750 Psi Required 170 At Test
Summary C-Factor Used: Overhead 120 Underground 120

W Water Flow Test: Pump Data: Tank or Reservoir:
A Date of Test - Cap.
T Time of Test - Rated Cap. Elev.
E Static (Psi) - 172 @ Psi
R Residual (Psi) - 171 Elev. Well
Flow (Gpm) - 750 Proof Flow Gpm
S Elevation - 989.29

U
P Location: AT CONNECTION TO BUILDING FDC


P
L Source of Information:
Y

Water Supply Curve

JAYHAWK FIRE SPRINKLER CO. INC
STANDPIPE UPGRADE FROM 4 TO 6

City Water Supply:
C1 - Static Pressure : 170
C2 - Residual Pressure: 169
C2 - Residual Flow : 750

Demand:
D1 - Elevation : 20.715
D2 - System Flow : 500
D2 - System Pressure : 167.549
Hose (Demand) : 250
D3 - System Demand : 750
Safety Margin : 1.451

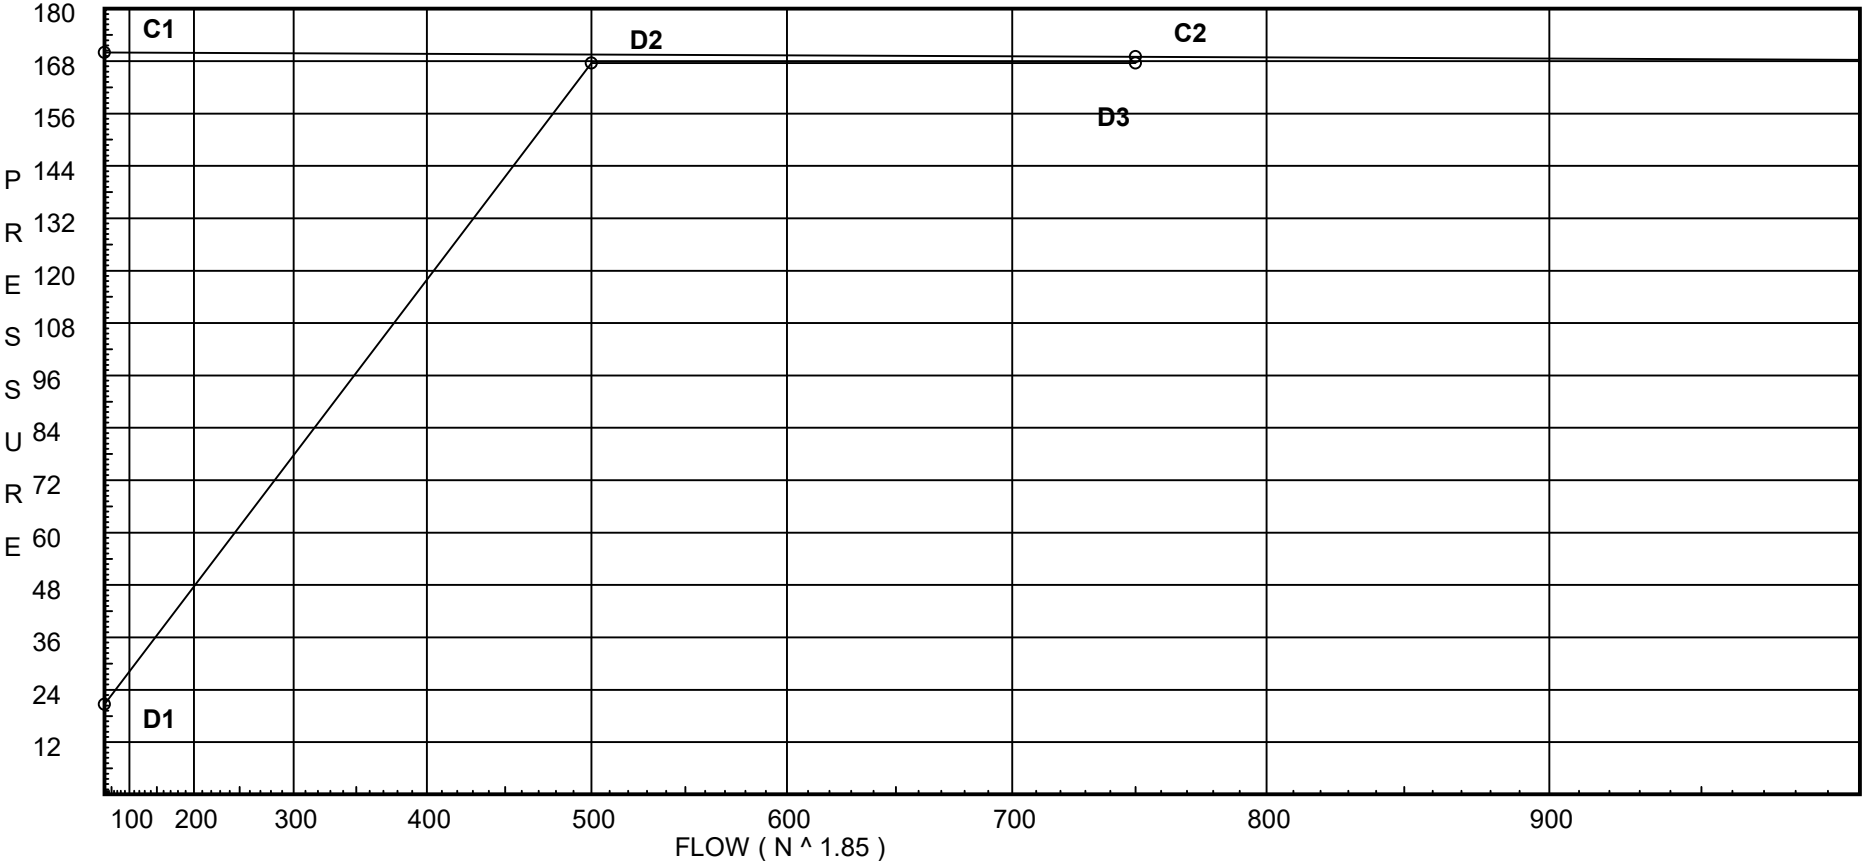

Fittings Used Summary

JAYHAWK FIRE SPRINKLER CO. INC
STANDPIPE UPGRADE FROM 4 TO 6

Page 3
Date

Fitting Legend

Abbrev.	Name	1/2	3/4	1	1 1/4	1 1/2	2	2 1/2	3	3 1/2	4	5	6	8	10	12	14	16	18	20	24
B	NFPA 13 Butterfly Valve	0	0	0	0	0	6	7	10	0	12	9	10	12	19	21	0	0	0	0	0
E	NFPA 13 90' Standard Elbow	1	2	2	3	4	5	6	7	8	10	12	14	18	22	27	35	40	45	50	61
S	NFPA 13 Swing Check	0	0	5	7	9	11	14	16	19	22	27	32	45	55	65					
V	90' Ell Firelock #001	0	0	0	0	0	3.5	4.3	5	0	6.8	8.5	10	13	0	0	0	0	0	0	0
X	90'Tee-BranchFirelock002	0	0	0	0	0	8.5	10.8	13	0	16	21	25	33	0	0	0	0	0	0	0

Units Summary

Diameter Units Inches
Length Units Feet
Flow Units US Gallons per Minute
Pressure Units Pounds per Square Inch

Note: Fitting Legend provides equivalent pipe lengths for fittings types of various diameters. Equivalent lengths shown are standard for actual diameters of Sched 40 pipe and CFactors of 120 except as noted with *. The fittings marked with a * show equivalent lengths values supplied by manufacturers based on specific pipe diameters and CFactors and they require no adjustment. All values for fittings not marked with a * will be adjusted in the calculation for CFactors of other than 120 and diameters other than Sched 40 per NFPA.

Flow Summary - NFPA

JAYHAWK FIRE SPRINKLER CO. INC
STANDPIPE UPGRADE FROM 4 TO 6

Page 4
Date

SUPPLY ANALYSIS

<i>Node at Source</i>	<i>Static Pressure</i>	<i>Residual Pressure</i>	<i>Flow</i>	<i>Available Pressure</i>	<i>Total Demand</i>	<i>Required Pressure</i>
TEST	170.0	169	750.0	169.0	750.0	167.549

NODE ANALYSIS

<i>Node Tag</i>	<i>Elevation</i>	<i>Node Type</i>	<i>Pressure at Node</i>	<i>Discharge at Node</i>	<i>Notes</i>	
500	1037.12	50	100.0	500.0	0.1	100
501	1037.12		105.3			
502	996.62		126.21			
503	996.62		126.25			
BOS	978.12		134.81			
TTR	978.12		138.4			
506	995.29		134.11			
TOR	995.29		138.88			
BOR	987.29		144.9			
FD	987.29		147.48			
TEST	989.29		167.55			
600	1021.12		114.71	250.0		
TOS	978.12		133.82			

Final Calculations : Hazen-Williams

JAYHAWK FIRE SPRINKLER CO. INC
STANDPIPE UPGRADE FROM 4 TO 6

Page 5
Date

Node1 to Node2	Elev1 Elev2	K Fact	Qa Qt	Nom Act	Fitting or Equiv Len	Pipe Ftngs Total	CFact Pf/Ft	Pt Pe Pf	*****	Notes	*****
500 to 501	1037.12 1037.12	50.00	500.00 500.0	2.5 2.469	E 6.0	0.830 6.000 6.830	120 0.7766	100.000 0.0 5.304		Vel = 33.51	
501 to 502	1037.12 996.62		0.0 500.0	6 6.065	12V B 120.0 10.0	215.070 130.000 345.070	120 0.0098	105.304 17.540 3.368		Vel = 5.55	
502 to 503	996.62 996.62		0.0 500.0	6 6.065		4.220 4.220	120 0.0097	126.212 0.0 0.041		Vel = 5.55	
503 to BOS	996.62 978.120		0.0 500.0	6 6.065	2V 20.0	35.820 20.000 55.820	120 0.0098	126.253 8.012 0.545		Vel = 5.55	
BOS to TTR	978.120 978.120		250.00 750.0	6 6.065		173.880 173.880	120 0.0207	134.810 0.0 3.592		Vel = 8.33	
TTR to 506	978.120 995.290		0.0 750.0	6 6.065	5V 50.0	102.020 50.000 152.020	120 0.0207	138.402 -7.436 3.141		Vel = 8.33	
506 to TOR	995.290 995.290		0.0 750.0	4 4.026	V 6.8	24.600 6.800 31.400	120 0.1520	134.107 0.0 4.772		Vel = 18.90	
TOR to BOR	995.290 987.290		0.0 750.0	4 4.026	V 6.8	10.000 6.800 16.800	120 0.1520	138.879 3.465 2.553		Vel = 18.90	
BOR to FD	987.290 987.290		0.0 750.0	4 4.026	X 16.0	1.000 16.000 17.000	120 0.1519	144.897 0.0 2.583		Vel = 18.90	
FD to TEST	987.290 989.290		0.0 750.0	4 4.026	6V S 40.8 22.0	74.950 62.800 137.750	120 0.1520	147.480 -0.866 20.935		Vel = 18.90	
TEST			0.0 750.00					167.549		K Factor = 57.94	
600 to TOS	1021.120 978.120	H250	250.00	4		24.333	120	114.708 18.623		Vel = 6.30	
TOS to BOS	978.120 978.120		250.0 0.0	4 4	2E B 20.0 12.0	17.920 32.000 49.920	120 0.0199	133.816 0.0 0.994		Vel = 6.30	
BOS			0.0 250.00					134.810		K Factor = 21.53	
