


1/4" = 1'

Michael Dueker

5/21/2024 | P240540

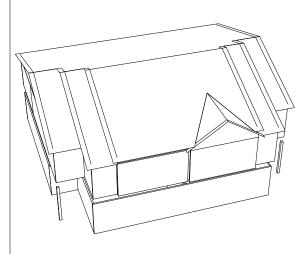

ROOF TRUSS PLACEMENT

DIAGRAM

EVERSTEAD SHOP DRAWING / SUBMITTAL

RFVIFW

SUBMITTAL WAS REVIEWED FOR DESIGN
CONFORMITY AND GENERAL CONFORMACE TO
CONTRACT DOCUMENTS ONLY. THE CONTRACTOF
IS RESPONSIBLE FOR CONFIRMING AND
CORRELATING DIMENSIONS AT JOBSITE FOR
TOLERANCE, CLEARANCE, QUANTITIES,
FABRICATION, COORDINATION OF HIS OR HER
WORK WITH OTHER TRADES, AND FULL

COMPLIANCE WITH CONTRACT DOCUMENTS.

STATUS:

APPROVED AS NOTED 06/07/2024

REVIEWED BY:

ENGINEER, EVERSTEAD ENGINEERING & DESIGN LLC.

TRUSS QUANTITY 36
GABLE AREA 593
HIP LINES 0
HORIZONTAL OVERHANG LINES 100
RAKED OVERHANG LINES 311
RIDGE LINES 69
ROOF AREA 2,919
VALLEY LINES 27

SQUARE FOOTAGE IS ESTIMATED. CONTRACTOR/FRAMER VERIFICATION REQUIRED.

- EL EXTREMO IZQUIERDO DE LOS TRUSSES (VEA LOS PERFILES)

TODAS LAS DIMENSIONES PARA LAS TRUSSES SON DE FUERA DE LA MADERA

ESTABLECER LOS TRUSSES NIVELADAS CON LA ESTRUCTURA (u.n.o.)

- LEFT END OF TRUSS (SEE TRUSS PROFILES)

ALL ROOF TRUSS DIMENSIONS ARE FROM OUTSIDE EDGE OF STUD (u.n.o.)
SET ROOF TRUSSES FLUSH WITH FRAMING (u.n.o.)

WARNING: Trusses must be handled with care to prevent damage and injury.

This truss placement diagram is to be used only as an installation aid; it is not a structural diagram. These trusses are designed as individual building components to be incorporated into the building design at the the specification of the building designer. See individual design sheets for each truss design identified on the placement drawing.

Professional advice should be sought regarding handling, installation, temporary and permanent bracing before erecting trusses. Temporary and permanent bracing is required during installation of trusses to prevent possible collapse.

For general guidance regarding bracing, consult "BCSI-06" available jointly from WTCA & TPI.

Premier Building Supply must be notified of any issues requiring a back charge prior to any work being done. Premier Building Supply reserves the right to use it's service staff in lieu of being back charged.

26-0-0

1 - SDWC 15600 REQUIRED AT ALL BEARING LOCATIONS (u.n.o.)

ALL TRUSS TO TRUSS CONNECTIONS = 'NAILED" (u.n.o.)

1 - SDWC 15600 NECESARIO EN TODO LOS PUNTOS DE APOYO (u.n.o. TODAS LAS CONEXIONES DE TRUSS A TRUSS = 'CLAVADAS " (u.n.o.)

HANGER SCHEDULE	QUANTITY
HUS26	7
SDWC 15600	100

RELEASE FOR CONSTRUCTION
AS NOTED ON PLANS REVIEW
DEVELOPMENT SERVICES
LEE'S SUMMIT, MISSOURI
06/13/2024 11:51:10

SEPARATING TOP PLATE

