

I-470 LOT 13A

LEE'S SUMMIT, JACKSON COUNTY, MISSOURI

Quist Engineering, Inc
Civil Engineering for Residential &
Commercial Site Development
824 NE Columbus St.
Lee's Summit, Missouri 64063
Phone: (816) 550-5675
email: rwalquist@quistengineering.com

COPYRIGHT © 2019

1ST ISSUE
6-20-19

REVISIONS	
△	7-24-19
△	8-7-19
△	8-21-19
△	

SHEET NO.

C301

JOB NO.
E18-337

- GENERAL NOTES:**
- ADJACENT LAND ACRES SHALL BE PROTECTED FROM EROSION AND SILTATION WITH HAY BALES OR FILTER FABRIC.
 - SILT CONTAINMENT SHALL REMAIN IN PLACE UNTIL VEGETATION IS REESTABLISHED.
 - OUTFALL LINES FROM THE ENCLOSED STORM DRAINAGE SYSTEMS SHALL BE PROVIDED WITH END SECTIONS AND THE DRAINAGE DITCHES PREPARED TO DISPERSE FLOW AND CONTROL EROSION.
 - THE FOLLOWING MAY BE USED AS EROSION/SILTATION CONTROL AS INDICATED ON THE PLANS: DEBRIS/SILT BASINS, SILT FENCING, STAKED STRAW BALES, RETENTION STRUCTURES, DIVERSIONS, OTHER METHODS AS DETAILED ON THE PLANS.
 - ALL METHODS SHALL BE UTILIZED AND MAINTAINED UNTIL THE SURFACE HAS BEEN STABILIZED WITH VEGETATION OR MULCH.
 - ALL STRAW BALES MUST BE EITHER WIRE BOUND OR STRUNG TIED. INSTALL BALES SO THAT BINDINGS ARE ORIENTED AROUND THE SIDES RATHER THAN ALONG THE TOPS AND BOTTOMS OF THE BALES. BALES SHALL BE OF STRAW ONLY.
 - GRAVING AND SEDIMENT CONTROL SHALL BE AS SPECIFIED IN THE "MODEL GRADING AND SEDIMENT CONTROL ORDINANCE" DEVELOPED BY THE MID-AMERICA ASSOCIATION OF CONSERVATION DISTRICTS AND THE MID-AMERICA REGIONAL COUNCIL.
 - STRAW BALES SHALL BE EMBEDDED IN THE SOIL A MINIMUM OF FOUR INCHES.
 - STRAW BALES SHALL BE PLACED IN A ROW AS INDICATED ON THE GRADING DRAWING.
 - STRAW BALES SHALL BE ANCHORED IN PLACE BY STAKES OR REBAR AS SHOWN IN THE DETAIL PROVIDED. THE FIRST STAKE IN EACH BALE SHALL BE ANGLED TOWARD A PREVIOUSLY Laid BALE TO FORCE THE BALES TOGETHER.
 - ACCUMULATED SILT SHALL BE REMOVED WHEN IT REACHES A DEPTH OF 6 INCHES.
 - STRAW BALES SHALL BE REMOVED UPON COMPLETION OF CONSTRUCTION AND SEEDING AND MULCHING OF GRADED AREAS.
 - CONTRACTOR SHALL BE RESPONSIBLE FOR THE MAINTENANCE OF STRAW BALES OR OTHER EROSION OR SEDIMENT CONTROL DEVICES UNTIL UPLAND AREAS HAVE BEEN STABILIZED.
 - VEGETATION ESTABLISHMENT FOR URBAN DEVELOPMENT SITES: GRADED AND EXCAVATED AREA OF 4.0 ACRES TO BE SOWN AFTER CONSTRUCTION WITH ONE OF THE FOLLOWING:
 - FALL FESCUE - 25 LBS./ACRE
 - SMOOTH BROME - 35 LBS./ACRES
 - COMBINED: FESCUE @ 20 LBS./ACRE AND BROME @ 15 LBS./ACRE
 - OTHER SEEDING MIXTURES AS APPROVED BY THE SOIL CONSERVATION SERVICE.
 - SEEDING PERIODS:
FESCUE OR BROME - MARCH 1 TO JUNE 1
MULCH RATES: (REQUIRED FOR ALL PERMANENT SEEDING)
4,356 LBS./ACRE
 - FERTILIZER:
A. NITROGEN 90 LBS./ACRE
B. PHOSPHATE 90 LBS./ACRE
C. POTASSIUM 90 LBS./ACRE
D. LIME 700 LBS./ACRE (EFFECTIVE NEUTRALIZING MATERIAL AS PER STATE EVALUATION OF QUARRIED ROCK)
E. OTHER RATES AS DEFINED BY A CURRENT SOIL TEST AND APPROVED BY THE SOIL CONSERVATION SERVICE.



- PHASE 1**
SHALL INCLUDE THE FOLLOWING:
- INSTALL SILT FENCE
 - INSTALL TEMPORARY CONSTRUCTION ENTRANCE

- PHASE 2**
SHALL INCLUDE THE FOLLOWING:
- REMOVE TOP SOIL, CURB, SIDEWALK, FENCE, AND TREES.
 - ROUGH GRADE CUT A ENGINEERED FILL
 - INSTALL UTILITIES
 - INSTALL FOOTING AND WALLS
 - INSTALL PARKING LOT, SIDEWALK AND MAIN ENTRANCES
 - SEED AND SOD ALL DISTURBED AREAS

- PHASE 3**
SHALL INCLUDE THE FOLLOWING:
- FULLY VEGETATED SITE
 - REMOVE SILTATION FENCE

NOTE:
1. ALL ESC INSPECTIONS REPORTS SHALL BE MADE PER THE CURRENT SWPPP REQUIREMENTS AND COPIES KEPT ONSITE.

SITE ESC PHASE 1 AND 2 PLAN

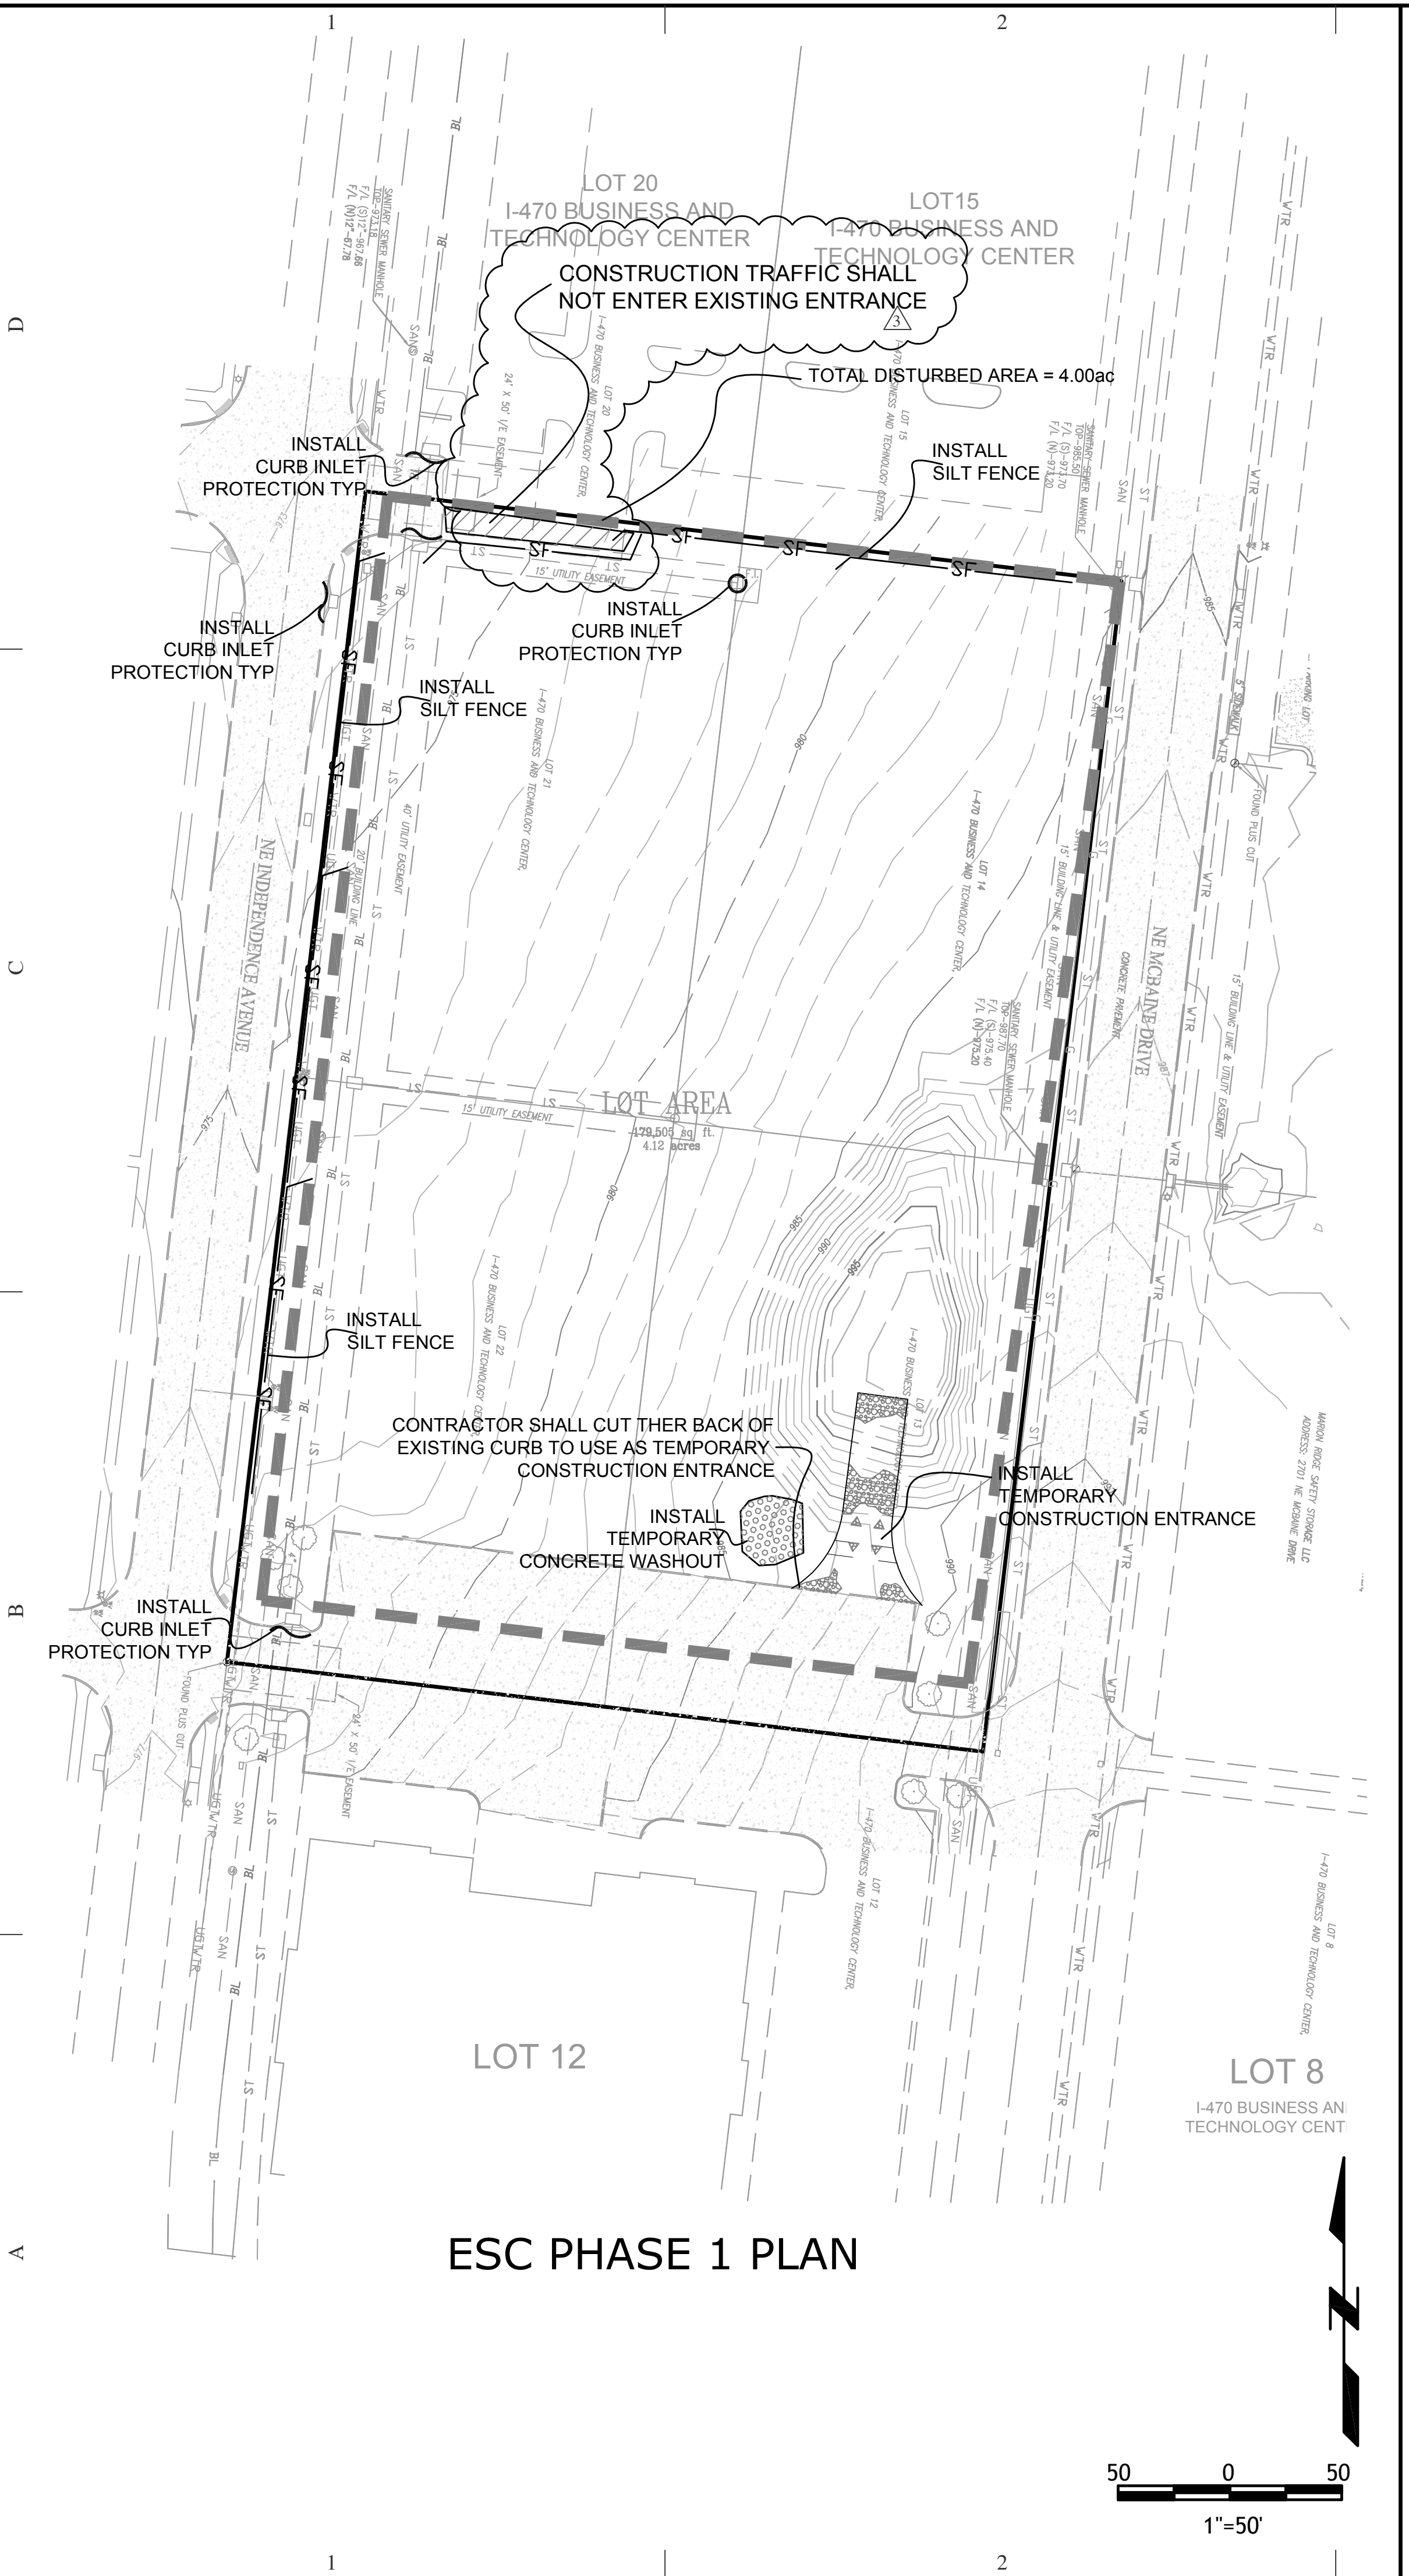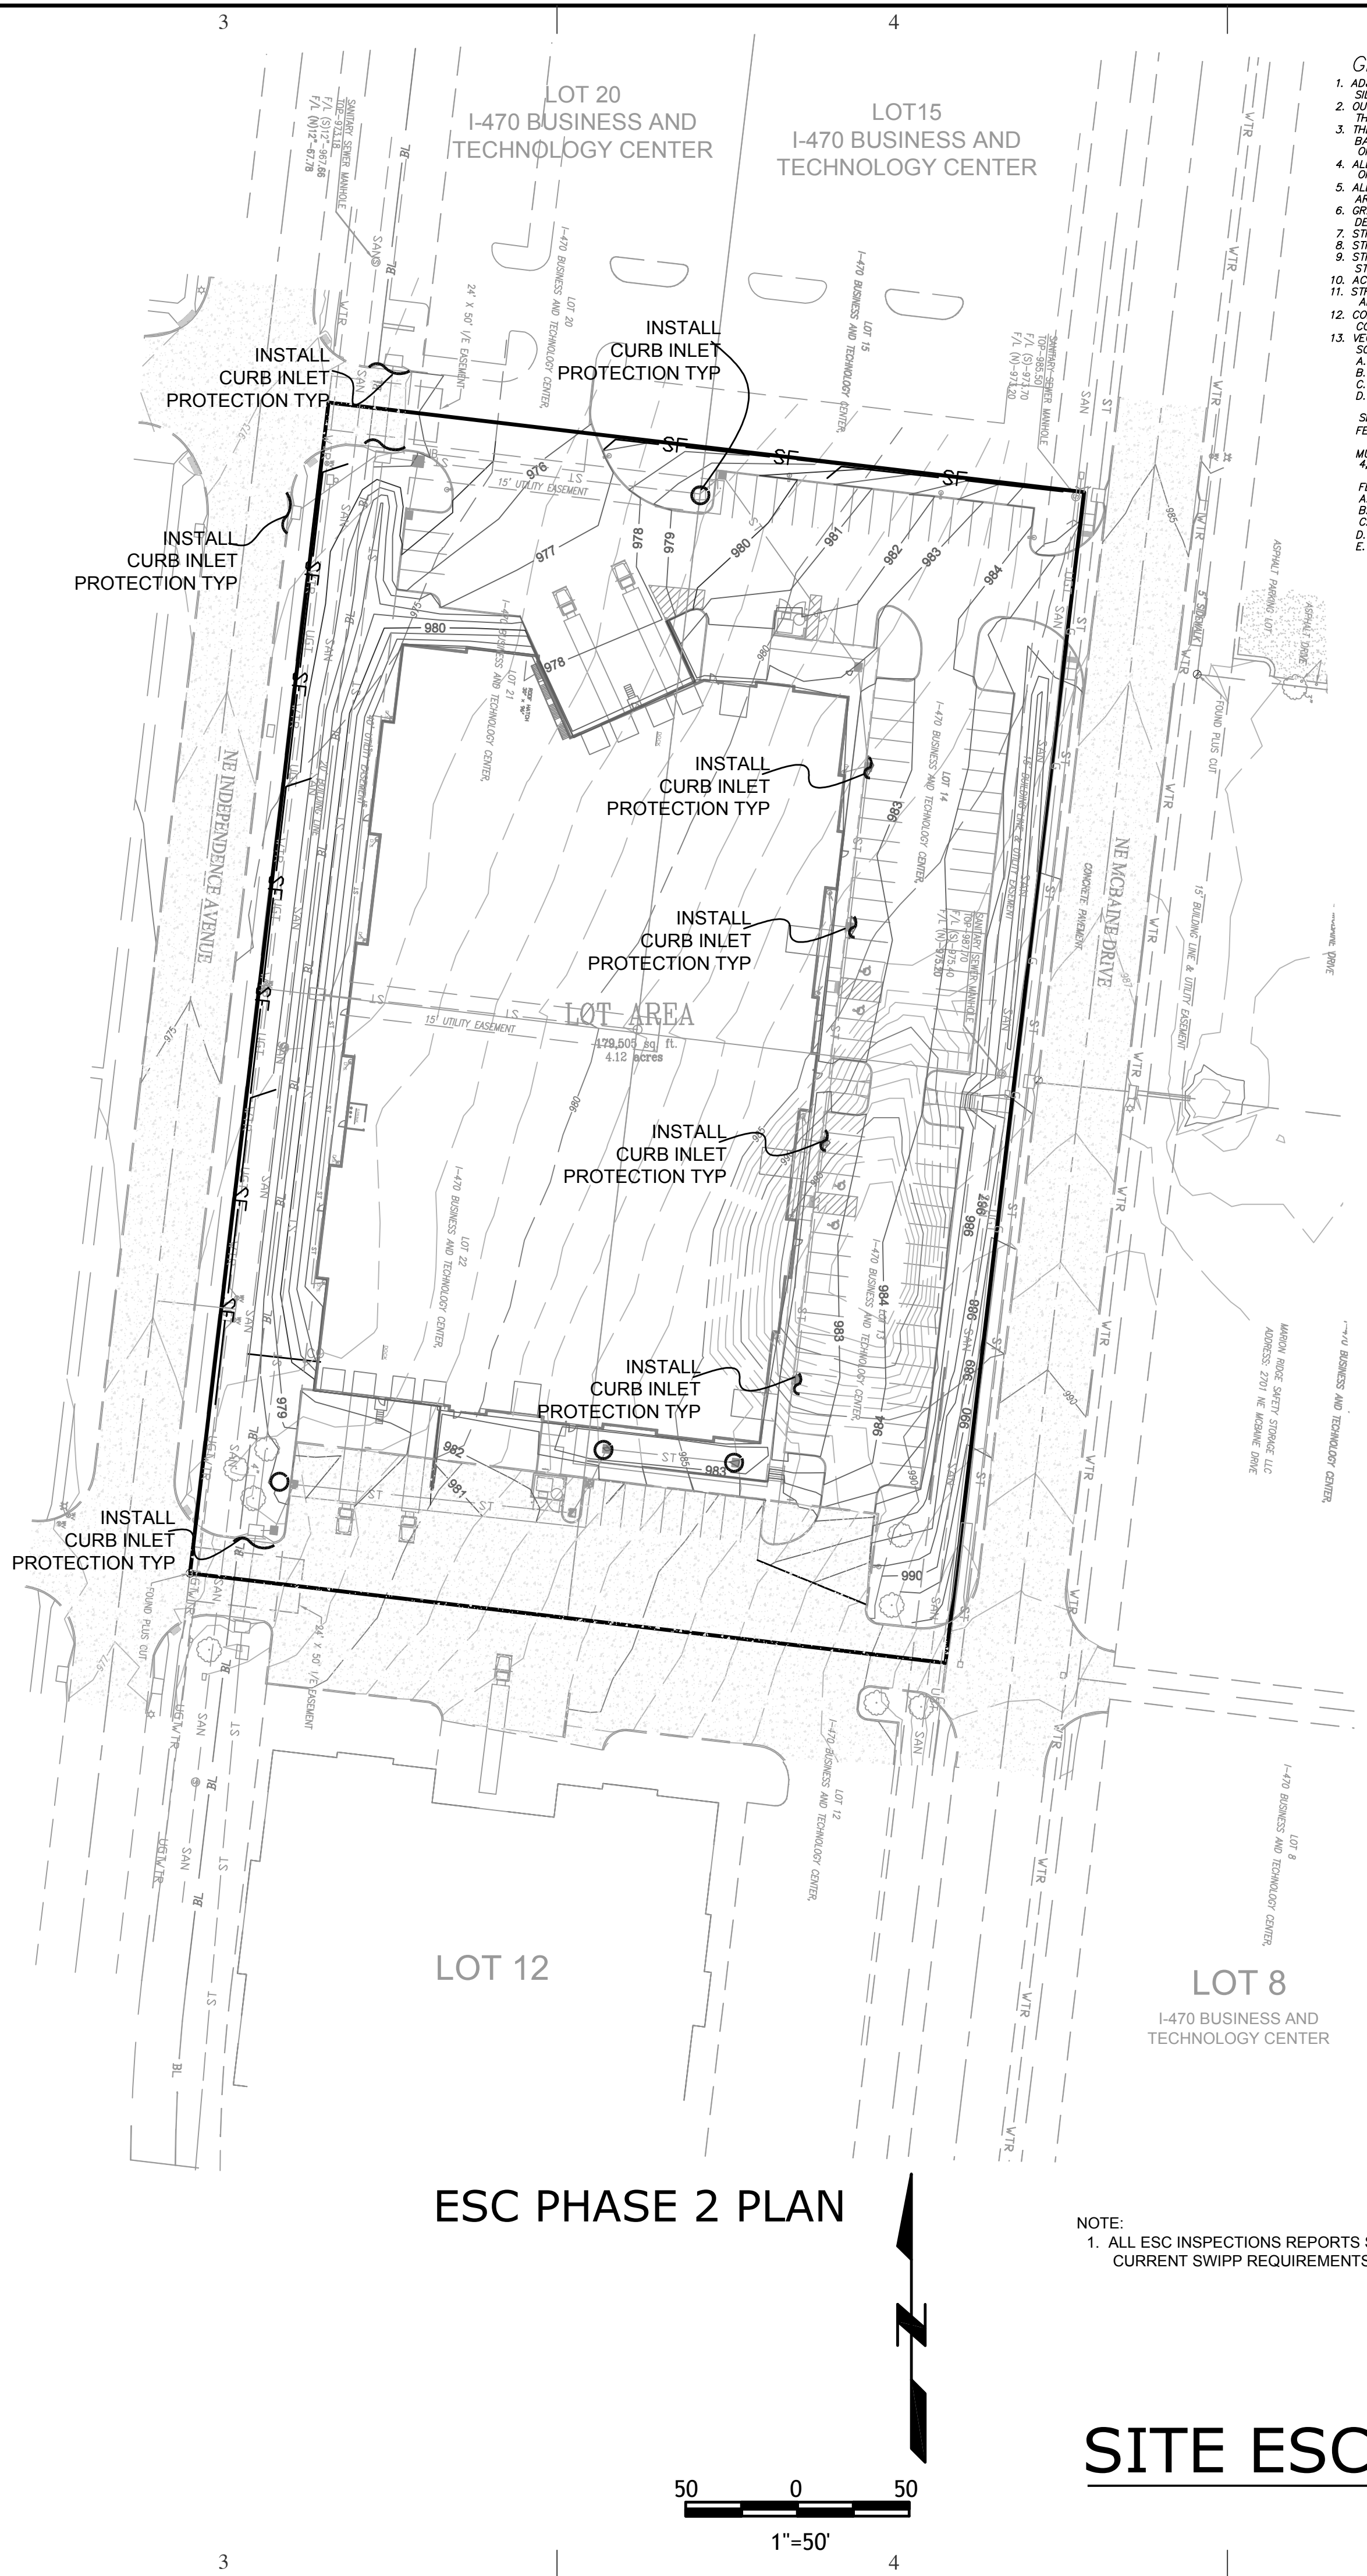

CONSTRUCTION TRAFFIC SHALL NOT ENTER EXISTING ENTRANCE

TOTAL DISTURBED AREA = 4.00ac

CONTRACTOR SHALL CUT THER BACK OF EXISTING CURB TO USE AS TEMPORARY CONSTRUCTION ENTRANCE

INSTALL TEMPORARY CONCRETE WASHOUT

INSTALL TEMPORARY CONSTRUCTION ENTRANCE

ESC PHASE 2 PLAN

1"=50'

1"=50'
