Longview Pickleball Complex Schedule and Gantt

Tarkett Sports Construction Central, LLC

Longview Pickleball Complex
3801 SW Longview Road
Lees Summit 64081
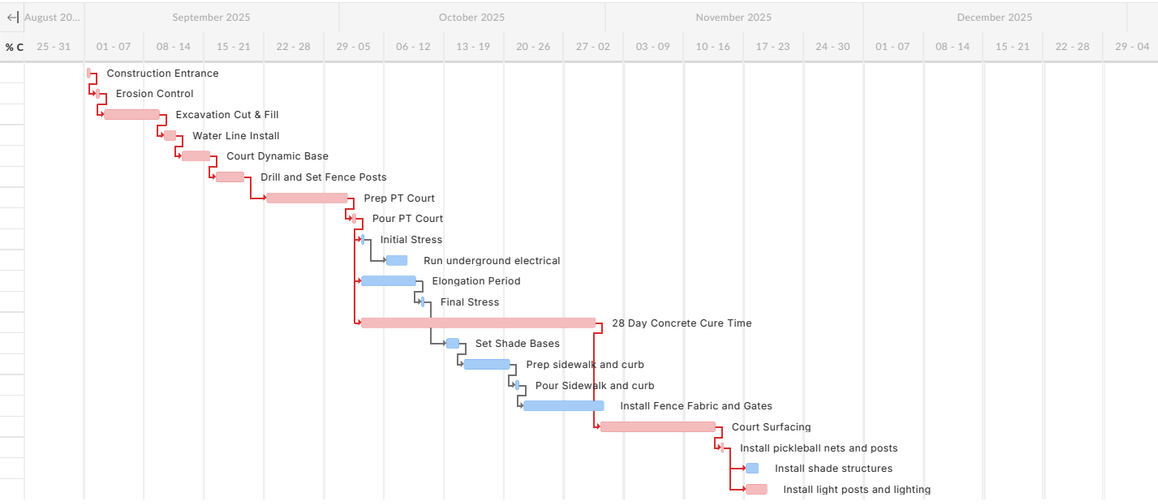
ID	Task Name	Start	Finish	Duration	% C
1	Construction Entrance	09/01/2025	09/01/2025	1 d	
2	Erosion Control	09/02/2025	09/02/2025	1 d	
3	Excavation Cut & Fill	09/03/2025	09/09/2025	5 d	
4	Water Line Install	09/10/2025	09/11/2025	2 d	
5	Court Dynamic Base	09/12/2025	09/15/2025	2 d	
6	Drill and Set Fence Posts	09/16/2025	09/19/2025	4 d	
7	Prep PT Court	09/22/2025	10/01/2025	8 d	
8	Pour PT Court	10/02/2025	10/02/2025	1 d	
9	Initial Stress	10/03/2025	10/03/2025	1 d	
10	Run underground electrical	10/06/2025	10/08/2025	3 d	
11	Elongation Period	10/03/2025	10/09/2025	5 d	
12	Final Stress	10/10/2025	10/10/2025	1 d	
13	28 Day Concrete Cure Time	10/03/2025	10/30/2025	20 d	
14	Set Shade Bases	10/13/2025	10/14/2025	2 d	
15	Prep sidewalk and curb	10/15/2025	10/20/2025	4 d	
16	Pour Sidewalk and curb	10/21/2025	10/21/2025	1 d	
17	Install Fence Fabric and Gates	10/22/2025	10/31/2025	8 d	
18	Court Surfacing	10/31/2025	11/13/2025	10 d	
19	Install pickleball nets and po...	11/14/2025	11/14/2025	1 d	
20	Install shade structures	11/17/2025	11/18/2025	2 d	
21	Install light posts and lighting	11/17/2025	11/19/2025	3 d
